40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE — COMMUNITY & OPPORTUNITY

EllisDon — We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
40th Ave & QEII Interchange Update 2023.08.10		1203d	23-Dec-20 A	15-Oct-25	23-Dec-20	02-Oct-25	-8d
Milestones		1203d	23-Dec-20 A	15-Oct-25	23-Dec-20	02-Oct-25	-8d
MILE-1000	RFPQ Closing Date	0d		23-Dec-20 A		23-Dec-20	0d
MILE-1010	ITT Closing Date	0d		09-Feb-21 A		09-Feb-21	0d
MILE-1020	Tender Award	0d		23-Feb-21 A		23-Feb-21	0d
MILE-1030	IFC's Issued	0d		09-Apr-21 A		09-Apr-21	0d
MILE-1040	Site Mobilization	0d		30-Apr-21 A		30-Apr-21	0d
MILE-1050	Nose Creek Re-Alignment Complete	0d		09-Nov-21 A		28-Oct-21	-8d
MILE-1060	New Eastbound CPR Bridge Complete	0d		14-May-23 A		29-Aug-22	-174d
MILE-1150	Completion of Mainstreet Work (Lane Closures)	0d		13-Sep-23		18-Sep-23	3d
MILE-1090	Widening of Existing Westbound CPR Bridge Complete	0d		14-Sep-23		03-Nov-22	-213d
MILE-1070	Reynolds Gate to CPR Bridge Roadworks Complete	0d		14-Sep-23		11-Oct-22	-230d
MILE-1100	40th Avenue Over Main Street Bridge Complete	0d		15-Sep-23		28-Jun-23	-54d
MILE-1110	South Point Access Roadwork's Complete	0d		21-Sep-23		28-Jun-23	-58d
MILE-1130	40th Ave Roadwork's Complete	0d		25-Sep-23		18-Jul-23	-47d
MILE-1080	Storm Pond Complete	0d		29-Sep-23		14-Oct-22	-238d
MILE-1120	40th Avenue Over QEII Bridge Complete	0d		29-Sep-23		26-Jul-23	-45d
MILE-1160	Safety Audit	0d		10-Oct-23		18-Sep-23	-15d
MILE-1140	Substantial Performance	0d		16-Oct-23		18-Sep-23	-18d
MILE-1170	Construction Completion Certificate	0d		16-Oct-23		02-Oct-23	-8d
MILE-1200	Warranty Period Start	0d		16-Oct-23		03-Oct-23	-8d
MILE-1180	QEII/40th Ave Overpass Bridge/Roadways Open For Traffic	0d		16-Oct-23		02-Oct-23	-9d
MILE-1190	Final Acceptance Certificate	0d		15-Oct-25		02-Oct-25	-8d
MILE-1210	Warranty Period Complete	0d		15-Oct-25		02-Oct-25	-8d
Preconstruction		657d	23-Dec-20 A	11-Aug-23	23-Dec-20	01-Apr-22	-339d
Tender Process		75d	23-Dec-20 A	14-Apr-21 A	23-Dec-20	29-Mar-21	-11d
P-TP-1000	Tender Process	75d	23-Dec-20 A	14-Apr-21 A	23-Dec-20	29-Mar-21	-11d
P-TP-1010	RFPQ Closing Date	1d	23-Dec-20 A	23-Dec-20 A	23-Dec-20	23-Dec-20	0d
P-TP-1020	RFQP Review Period	8d	24-Dec-20 A	07-Jan-21 A	24-Dec-20	07-Jan-21	0d
P-TP-1030	Notice Of Pre Qualification	1d	08-Jan-21 A	08-Jan-21 A	08-Jan-21	08-Jan-21	0d
P-TP-1040	ITT Development Period	22d	11-Jan-21 A	09-Feb-21 A	11-Jan-21	09-Feb-21	0d
P-TP-1050	ITT Submission	0d	09-Feb-21 A		09-Feb-21		0d
P-TP-1060	Tender Award	0d	23-Feb-21 A		23-Feb-21		0d
P-TP-1070	Contract Award	0d	14-Apr-21 A		29-Mar-21		-11d
Project Permitting and Notifications		278d	23-Feb-21 A	01-Apr-22 A	23-Feb-21	01-Apr-22	0d
Historical Resources Impact Assessment		1d	03-May-21 A	04-May-21 A	01-Jun-21	01-Jun-21	20d
P-HRIA-1000	HRIA Affected Lands - Cleared	1d	03-May-21 A	04-May-21 A	01-Jun-21	01-Jun-21	20d
Land Acquisitions		63d	31-Dec-21 A	01-Apr-22 A	31-Dec-21	01-Apr-22	0d
P-LA-1000	Storm Pond Lands	0d	31-Dec-21 A	31-Dec-21 A	31-Dec-21	31-Dec-21	0d
P-LA-1010	Jas Lands	0d	01-Apr-22 A	01-Apr-22 A	01-Apr-22	01-Apr-22	0d
Construction Access/Easement Agreement		35d	23-Feb-21 A	14-Apr-21 A	23-Feb-21	20-Apr-21	5d
P-CAEA-1000	Vesta Lands	35d	23-Feb-21 A	14-Apr-21 A	23-Feb-21	20-Apr-21	5d
Permits		57d	22-Mar-21 A	11-Jun-21 A	07-Apr-21	14-Jun-21	2d
P-PER-1030	Roadside Development Permit	1d	22-Mar-21 A	22-Mar-21 A	14-Jun-21	14-Jun-21	58d
P-PER-1000	ATCO Crossing Agreement	0d	07-Apr-21 A	07-Apr-21 A	07-Apr-21	07-Apr-21	1d
P-PER-1010	Water Act Code of Practice	10d	21-Apr-21 A	04-May-21 A	21-Apr-21	10-May-21	4d
P-PER-1020	CPR	0d	11-Jun-21 A	11-Jun-21 A	11-Jun-21	11-Jun-21	0d
Design Development		0d	09-Apr-21 A	09-Apr-21 A			
P-DES-1000	IFC's Issued	0d		09-Apr-21 A			
Road Closure Notification To Residents & Businesses (Kingsview Rd and Sharp Hill Way)		10d	23-Mar-21 A	06-Apr-21 A	23-Mar-21	06-Apr-21	0d
P-RCN-1000	Notification To Residents & Businesses	10d	23-Mar-21 A	06-Apr-21 A	23-Mar-21	06-Apr-21	0d
Submittals		96d	23-Feb-21 A	12-Jul-21 A	23-Feb-21	18-May-21	-36d
ED Submission		87d	23-Feb-21 A	28-Jun-21 A	23-Feb-21	18-May-21	-27d
P-SUBM-ED-1040	Project Signage	36d	23-Feb-21 A	15-Apr-21 A	23-Feb-21	22-Mar-21	-16d
P-SUBM-ED-1050	Notification To Residents	29d	23-Feb-21 A	06-Apr-21 A	23-Feb-21	18-May-21	31d
P-SUBM-ED-1060	ESC Plan	30d	23-Feb-21 A	07-Apr-21 A			

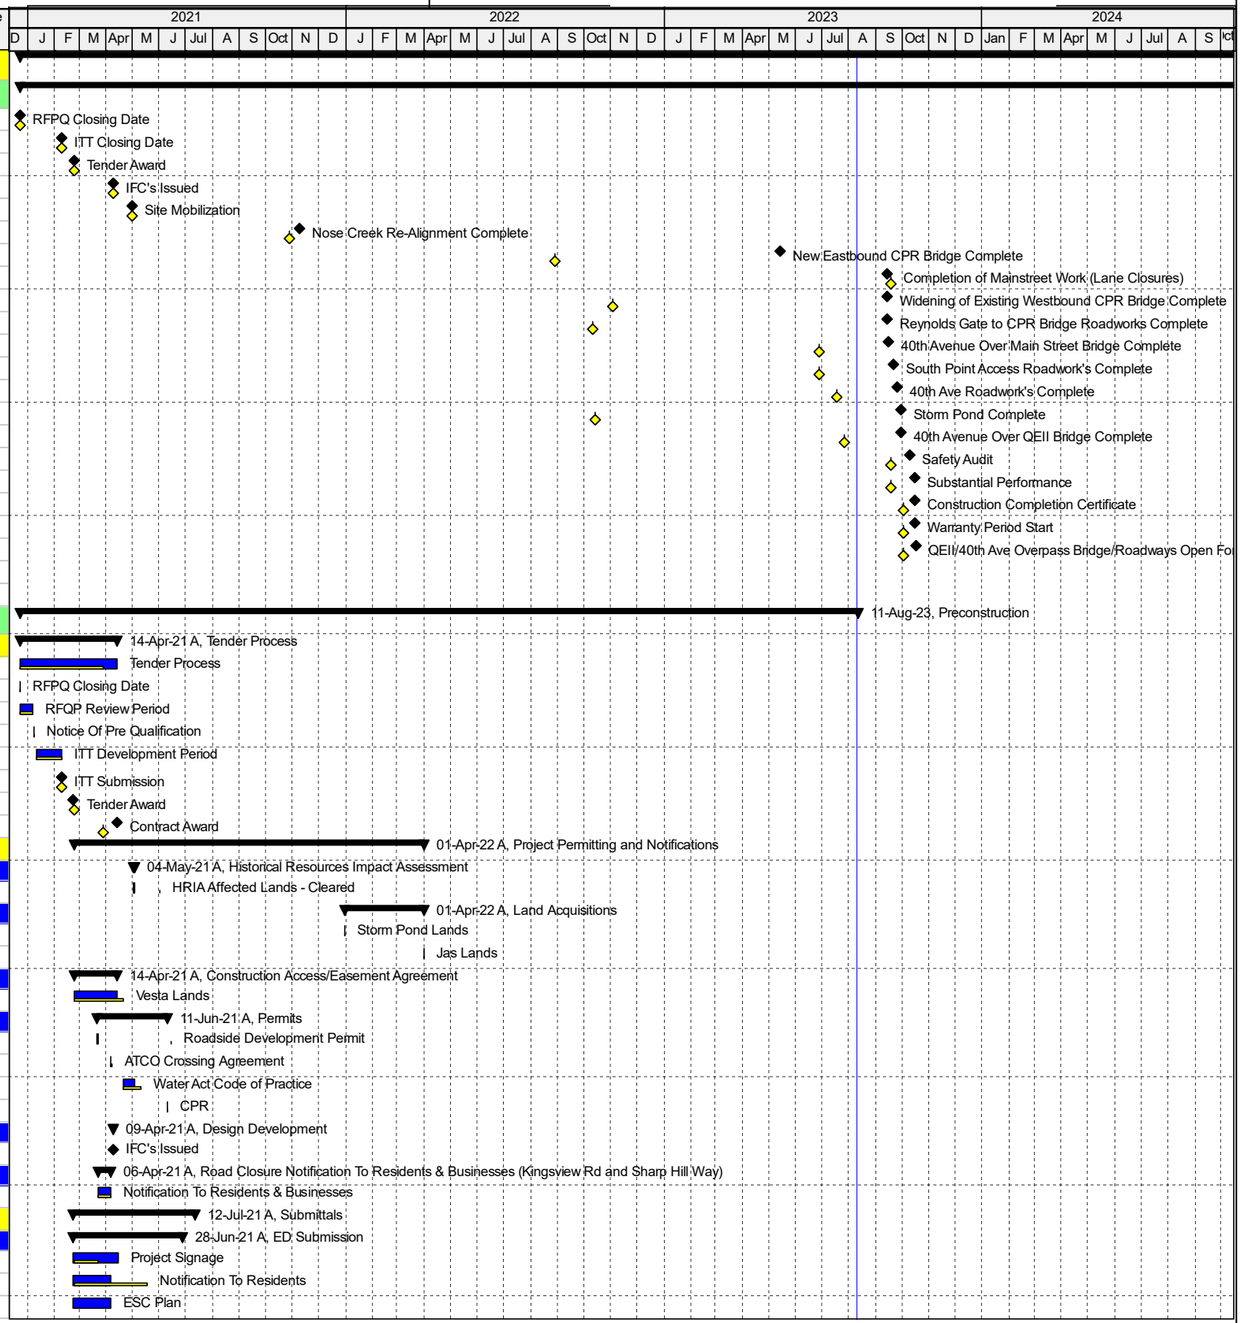

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
P-SUBM-ED-1000	ECO Plan	38d	23-Feb-21 A	19-Apr-21 A	23-Feb-21	22-Mar-21	-18d
P-SUBM-ED-1010	CP Rail Phasing Plan	87d	23-Feb-21 A	28-Jun-21 A	23-Feb-21	20-Apr-21	-47d
P-SUBM-ED-1020	Airdrie Traffic Accommodation Plan	30d	23-Feb-21 A	07-Apr-21 A	23-Feb-21	22-Mar-21	-10d
P-SUBM-ED-1030	Site Specific Safety Plan	0d	06-Apr-21 A	06-Apr-21 A	23-Feb-21	22-Mar-21	-9d
P-SUBM-ED-1070	CPR Piling Plan	0d	28-Jun-21 A	28-Jun-21 A			
City of Airdrie and Consultant Review Period		67d	06-Apr-21 A	12-Jul-21 A	23-Mar-21	27-Apr-21	-51d
P-SUBM-COARP-1020	Site Specific Safety Plan	0d	06-Apr-21 A	06-Apr-21 A	23-Mar-21	29-Mar-21	-4d
P-SUBM-COARP-1010	Airdrie Traffic Accommodation Plan	3d	07-Apr-21 A	12-Apr-21 A	23-Mar-21	06-Apr-21	-3d
P-SUBM-COARP-1050	ESC Plan	23d	07-Apr-21 A	10-May-21 A			
P-SUBM-COARP-1030	Project Signage	0d	15-Apr-21 A	15-Apr-21 A	23-Mar-21	29-Mar-21	-11d
P-SUBM-COARP-1000	ECO Plan	4d	19-Apr-21 A	23-Apr-21 A	23-Mar-21	29-Mar-21	-17d
P-SUBM-COARP-1040	CP Rail Phasing Plan	9d	28-Jun-21 A	12-Jul-21 A	21-Apr-21	27-Apr-21	-51d
P-SUBM-ED-1080	CPR Piling Plan	0d	29-Jun-21 A	29-Jun-21 A			
ED Submittal Resubmission		33d	13-Apr-21 A	28-May-21 A			
P-SUBM-EDRS-1060	Airdrie Traffic Accommodation Plan R1	0d	13-Apr-21 A	13-Apr-21 A			
P-SUBM-EDRS-1070	Airdrie Traffic Accommodation Plan R2	1d	19-Apr-21 A	20-Apr-21 A			
P-SUBM-EDRS-1080	Airdrie Traffic Accommodation Plan R3	1d	20-Apr-21 A	21-Apr-21 A			
P-SUBM-EDRS-1090	Airdrie Traffic Accommodation Plan R4	2d	21-Apr-21 A	23-Apr-21 A			
P-SUBM-EDRS-1100	Airdrie Traffic Accommodation Plan R5	0d	23-Apr-21 A	23-Apr-21 A			
P-SUBM-EDRS-1050	ESC Plan R1	13d	11-May-21 A	28-May-21 A			
City of Airdrie and Consultant Resubmission Review Period		31d	23-Apr-21 A	08-Jun-21 A	09-Apr-21	12-Apr-21	-39d
P-SUBM-COACRSR-1030	Airdrie Traffic Accommodation Plan	10d	23-Apr-21 A	07-May-21 A	09-Apr-21	12-Apr-21	-18d
P-SUBM-COACRSR-1050	ESC Plan R1	6d	31-May-21 A	08-Jun-21 A			
Shop Drawings		617d	23-Feb-21 A	11-Aug-23	23-Feb-21	25-Mar-22	-343d
Nose Creek Realignment		76d	23-Feb-21 A	11-Jun-21 A	23-Feb-21	26-May-21	-11d
P-SD-NCR-1000	Submission - Nose Creek Bridge File CSP's	13d	23-Feb-21 A	11-Mar-21 A	23-Feb-21	11-Mar-21	0d
P-SD-NCR-1010	Review - Nose Creek Bridge File CSP's	6d	12-Mar-21 A	19-Mar-21 A	12-Mar-21	19-Mar-21	0d
P-SD-NCR-1020	Resubmission - Nose Creek Bridge File CSP's	10d	22-Mar-21 A	05-Apr-21 A	22-Mar-21	05-Apr-21	0d
P-SD-NCR-1030	Resubmission Review - Nose Creek Bridge File CSP's	5d	06-Apr-21 A	12-Apr-21 A	06-Apr-21	12-Apr-21	0d
P-SD-NCR-1040	Submission - Rebar/Reinforcing Steel	15d	12-Apr-21 A	03-May-21 A	12-Apr-21	16-Apr-21	-10d
P-SD-NCR-1100	Resubmission Review - Nose Creek Bridge File SPCSP R1	17d	12-Apr-21 A	05-May-21 A			
P-SD-NCR-1070	Review - Rebar/Reinforcing Steel	26d	04-May-21 A	10-Jun-21 A	19-Apr-21	23-Apr-21	-32d
P-SD-NCR-1050	Pre-fab Meeting - Nose Creek Bridge File SPCSP's	0d	18-May-21 A	18-May-21 A	13-Apr-21	13-Apr-21	-24d
P-SD-NCR-1060	Fabrication - Nose Creek Bridge File SPCSP's	16d	19-May-21 A	11-Jun-21 A	14-Apr-21	26-May-21	-11d
Eastbound CPR Bridge		372d	12-Apr-21 A	03-Oct-22 A	12-Apr-21	03-Nov-21	-229d
P-SD-ECPRB-1050	Submission - ACP Mix Designs & Deck Paving Procedure	6d	04-Jul-22 A	12-Jul-22 A	12-Apr-21	30-Sep-21	-194d
P-SD-ECPRB-1380	Review - ACP Mix Designs & Deck Paving Procedure	23d	18-Jul-22 A	19-Aug-22 A	01-Oct-21	15-Oct-21	-211d
P-SD-ECPRB-1390	Resubmission - ACP Mix Designs & Deck Paving Procedure	20d	22-Aug-22 A	19-Sep-22 A	18-Oct-21	22-Oct-21	-227d
P-SD-ECPRB-1400	Resubmission Review - ACP Mix Designs & Deck Paving Procedure	10d	20-Sep-22 A	03-Oct-22 A	25-Oct-21	29-Oct-21	-232d
ED Submission		90d	12-Apr-21 A	18-Aug-21 A	12-Apr-21	06-Jul-21	-30d
P-SD-ECPRB-1000	Piling	22d	12-Apr-21 A	12-May-21 A	12-Apr-21	23-Apr-21	-12d
P-SD-ECPRB-1010	MSE Revision 0	78d	12-Apr-21 A	30-Jul-21 A	12-Apr-21	30-Apr-21	-63d
P-SD-ECPRB-1020	Bearings	49d	12-Apr-21 A	21-Jun-21 A	12-Apr-21	06-Jul-21	11d
P-SD-ECPRB-1060	Rebar/Reinforcing Steel	28d	12-Apr-21 A	20-May-21 A	12-Apr-21	06-Jul-21	32d
P-SD-ECPRB-1030	Girders Revision 0	28d	01-Jun-21 A	09-Jul-21 A	12-Apr-21	06-Jul-21	-3d
P-SD-ECPRB-1410	Girder Bracing (With Revisions)	11d	04-Aug-21 A	18-Aug-21 A			
P-SD-ECPRB-1070	Precast Deck Panels Revision 0	2d	13-Aug-21 A	16-Aug-21 A	12-Apr-21	06-Jul-21	-28d
City of Airdrie and Consultant Review Period		126d	12-May-21 A	10-Nov-21 A	26-Apr-21	20-Jul-21	-78d
P-SD-ECPRB-1080	Piling	5d	12-May-21 A	19-May-21 A	26-Apr-21	07-May-21	-7d
P-SD-ECPRB-1220	Rebar/Reinforcing Steel	4d	20-May-21 A	27-May-21 A	07-Jul-21	20-Jul-21	38d
P-SD-ECPRB-1200	Bearings	5d	21-Jun-21 A	28-Jun-21 A	07-Jul-21	20-Jul-21	16d
P-SD-ECPRB-1210	Girders Revision 1	21d	28-Jul-21 A	26-Aug-21 A	07-Jul-21	20-Jul-21	-26d
P-SD-ECPRB-1090	MSE Revision 1	16d	30-Aug-21 A	22-Sep-21 A	03-May-21	14-May-21	-88d
P-SD-ECPRB-1130	Concrete Mix Designs	10d	22-Sep-21 A	05-Oct-21 A	25-May-21	07-Jun-21	-83d
P-SD-ECPRB-1230	Precast Deck Panels Revision 1	5d	04-Nov-21 A	10-Nov-21 A	07-Jul-21	20-Jul-21	-78d
ED Submittal Resubmission		5d	22-Sep-21 A	28-Sep-21 A	17-May-21	27-Jul-21	-43d
P-SD-ECPRB-1110	MSE	5d	22-Sep-21 A	28-Sep-21 A	17-May-21	21-May-21	-88d

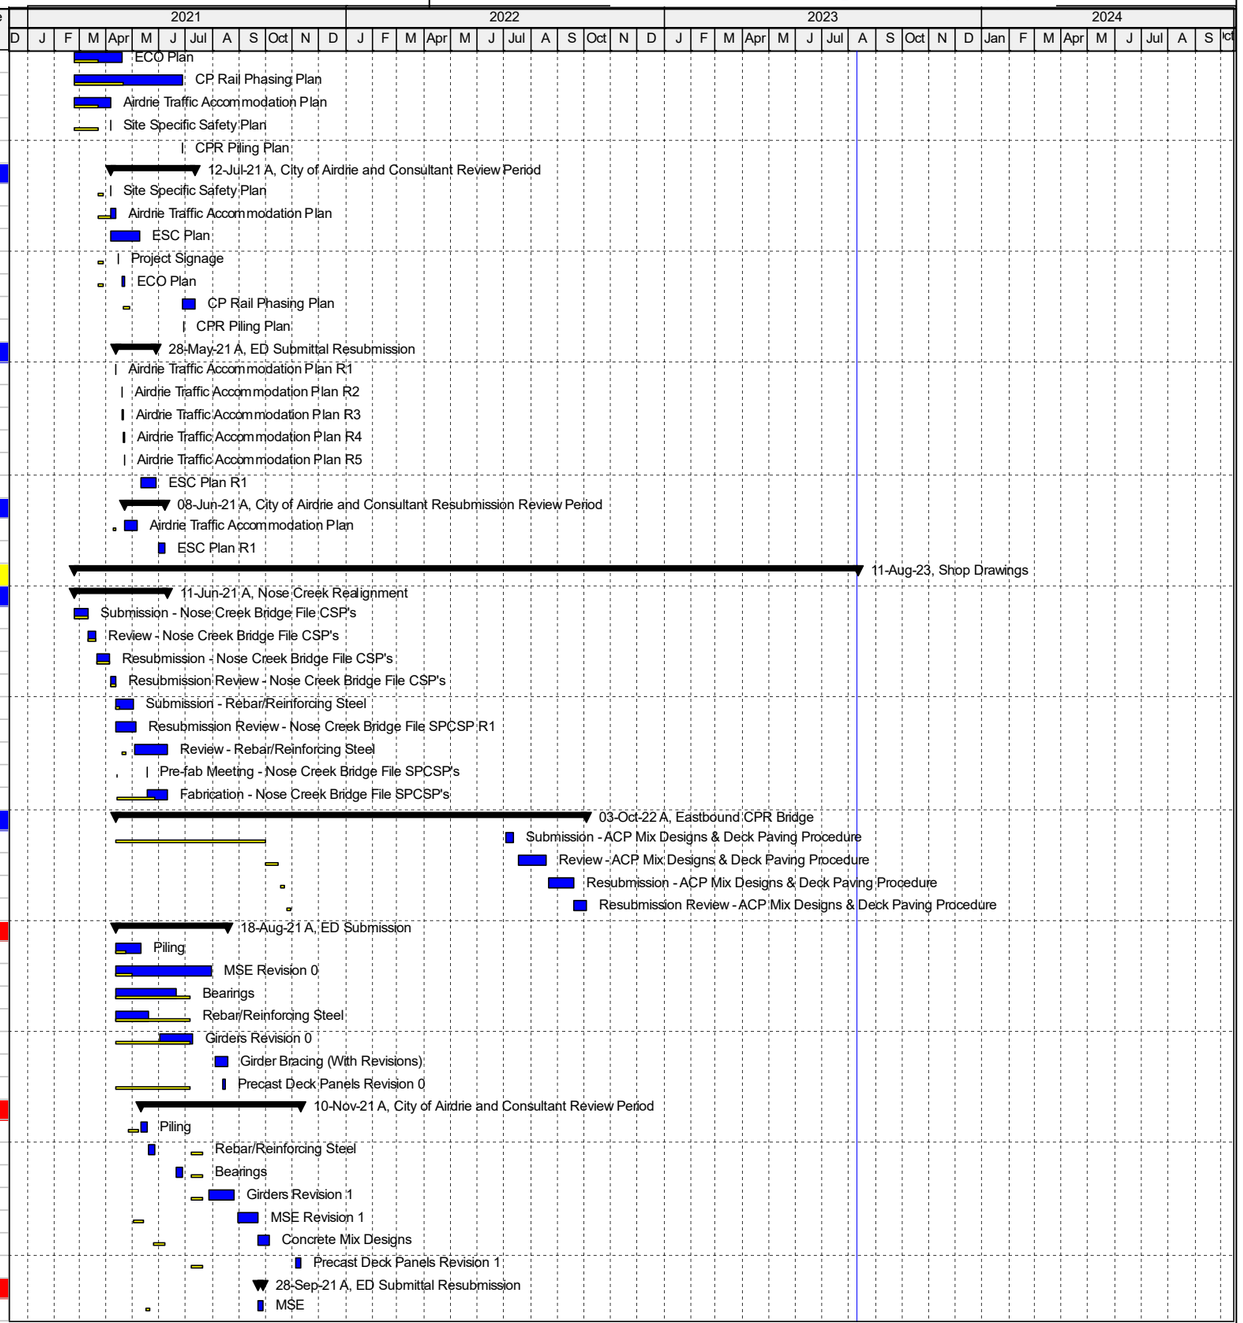

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE — COMMUNITY & OPPORTUNITY

EllisDon — We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
P-SD-ECPRB-1250	Girders	5d	22-Sep-21 A	28-Sep-21 A	21-Jul-21	27-Jul-21	-43d
City of Airdrie and Consultant Resubmission Review Period		23d	23-Aug-21 A	23-Sep-21 A	25-May-21	04-Aug-21	-35d
P-SD-ECPRB-1300	Girders	3d	23-Aug-21 A	25-Aug-21 A	28-Jul-21	04-Aug-21	-15d
P-SD-ECPRB-1140	MSE	2d	22-Sep-21 A	23-Sep-21 A	25-May-21	31-May-21	-80d
Prefabrication Meeting		77d	29-Jul-21 A	17-Nov-21 A	01-Jun-21	09-Aug-21	-70d
P-SD-ECPRB-1320	Bearings	39d	29-Jul-21 A	23-Sep-21 A	05-Aug-21	05-Aug-21	-34d
P-SD-ECPRB-1330	Girders	1d	20-Sep-21 A	20-Sep-21 A	06-Aug-21	06-Aug-21	-30d
P-SD-ECPRB-1160	MSE	0d	23-Sep-21 A	23-Sep-21 A	01-Jun-21	01-Jun-21	-78d
P-SD-ECPRB-1350	Precast Deck Panels	1d	17-Nov-21 A	17-Nov-21 A	09-Aug-21	09-Aug-21	-70d
Fabrication		112d	10-Sep-21 A	18-Feb-22 A	02-Jun-21	03-Nov-21	-74d
P-SD-ECPRB-1170	MSE	45d	10-Sep-21 A	15-Nov-21 A	02-Jun-21	29-Jun-21	-94d
P-SD-ECPRB-1420	Girder Bracing	57d	22-Oct-21 A	14-Jan-22 A			
P-SD-ECPRB-1340	Bearings	69d	29-Oct-21 A	07-Feb-22 A	06-Aug-21	01-Nov-21	-67d
P-SD-ECPRB-1360	Girders	2d	13-Jan-22 A	14-Jan-22 A	09-Aug-21	02-Nov-21	-50d
P-SD-ECPRB-1370	Precast Deck Panels	27d	13-Jan-22 A	18-Feb-22 A	10-Aug-21	03-Nov-21	-74d
Additional Preconstruction Meetings		1d	02-Jun-21 A	02-Jun-21 A	25-May-21	25-May-21	-6d
P-SD-ECPRB-1150	Piling	1d	02-Jun-21 A	02-Jun-21 A	25-May-21	25-May-21	-6d
Miscellaneous		31d	15-Jun-22 A	29-Jul-22 A			
P-SD-ECPRB-1430	Anchor Bolts for Street Lights	17d	15-Jun-22 A	08-Jul-22 A			
P-SD-ECPRB-1440	Fabrication of Anchor Bolts for Street Lights	14d	11-Jul-22 A	29-Jul-22 A			
Westbound CPR Bridge Widening		367d	12-Apr-21 A	26-Sep-22 A	12-Apr-21	02-Nov-21	-225d
P-SD-WCPRB-1030	Submission - ACP Mix Designs & Deck Paving Procedure	6d	04-Jul-22 A	12-Jul-22 A	12-Apr-21	30-Sep-21	-194d
P-SD-WCPRB-1210	Review - ACP Mix Designs & Deck Paving Procedure	24d	18-Jul-22 A	19-Aug-22 A	01-Oct-21	15-Oct-21	-212d
P-SD-WCPRB-1220	Resubmission - ACP Mix Designs & Deck Paving Procedure	20d	22-Aug-22 A	19-Sep-22 A	18-Oct-21	22-Oct-21	-227d
P-SD-WCPRB-1230	Resubmission Review - ACP Mix Designs & Deck Paving Procedure	5d	20-Sep-22 A	26-Sep-22 A	25-Oct-21	29-Oct-21	-227d
ED Submission		148d	12-Apr-21 A	10-Nov-21 A	12-Apr-21	06-Jul-21	-88d
P-SD-WCPRB-1000	Bearings	51d	12-Apr-21 A	23-Jun-21 A	12-Apr-21	06-Jul-21	9d
P-SD-WCPRB-1010	Girders	78d	12-Apr-21 A	02-Aug-21 A	12-Apr-21	06-Jul-21	-18d
P-SD-WCPRB-1020	Concrete Mix Designs	102d	12-Apr-21 A	03-Sep-21 A	12-Apr-21	21-May-21	-72d
P-SD-WCPRB-1040	Girder Bracing (Including Revisions)	18d	18-Oct-21 A	10-Nov-21 A	12-Apr-21	06-Jul-21	-88d
City of Airdrie and Consultant Review Period		36d	23-Jun-21 A	16-Aug-21 A	07-Jul-21	20-Jul-21	-17d
P-SD-WCPRB-1080	Bearings	3d	23-Jun-21 A	28-Jun-21 A	07-Jul-21	20-Jul-21	16d
P-SD-WCPRB-1090	Girders	9d	02-Aug-21 A	16-Aug-21 A	07-Jul-21	20-Jul-21	-17d
Prefabrication Meeting		32d	29-Jul-21 A	14-Sep-21 A	05-Aug-21	06-Aug-21	-26d
P-SD-WCPRB-1170	Bearings	1d	29-Jul-21 A	30-Jul-21 A	05-Aug-21	05-Aug-21	4d
P-SD-WCPRB-1180	Girders	1d	14-Sep-21 A	14-Sep-21 A	06-Aug-21	06-Aug-21	-26d
Fabrication		106d	06-Sep-21 A	07-Feb-22 A	06-Aug-21	02-Nov-21	-66d
P-SD-WCPRB-1190	Bearings	106d	06-Sep-21 A	07-Feb-22 A	06-Aug-21	01-Nov-21	-67d
P-SD-WCPRB-1240	Girder Bracing	41d	22-Nov-21 A	20-Jan-22 A			
P-SD-WCPRB-1200	Girders	12d	05-Jan-22 A	20-Jan-22 A	09-Aug-21	02-Nov-21	-54d
Main Street Bridge		367d	12-Apr-21 A	26-Sep-22 A	12-Apr-21	03-Nov-21	-224d
P-SD-MSB-1050	Submission - ACP Mix Designs & Deck Paving Procedure	6d	04-Jul-22 A	12-Jul-22 A	12-Apr-21	30-Sep-21	-194d
P-SD-MSB-1380	Review - ACP Mix Designs & Deck Paving Procedure	24d	18-Jul-22 A	19-Aug-22 A	01-Oct-21	15-Oct-21	-212d
P-SD-MSB-1390	Resubmission - ACP Mix Designs & Deck Paving Procedure	20d	22-Aug-22 A	19-Sep-22 A	18-Oct-21	22-Oct-21	-227d
P-SD-MSB-1400	Resubmission Review - ACP Mix Designs & Deck Paving Procedure	5d	20-Sep-22 A	26-Sep-22 A	25-Oct-21	29-Oct-21	-227d
ED Submission		132d	12-Apr-21 A	19-Oct-21 A	12-Apr-21	06-Jul-21	-72d
P-SD-MSB-1000	Piling	22d	12-Apr-21 A	12-May-21 A	12-Apr-21	23-Apr-21	-12d
P-SD-MSB-1010	MSE	20d	12-Apr-21 A	10-May-21 A	12-Apr-21	23-Apr-21	-10d
P-SD-MSB-1020	Bearings	50d	12-Apr-21 A	22-Jun-21 A	12-Apr-21	06-Jul-21	10d
P-SD-MSB-1030	Girders	68d	12-Apr-21 A	19-Jul-21 A	12-Apr-21	06-Jul-21	-8d
P-SD-MSB-1040	Concrete Mix Designs	66d	12-Apr-21 A	15-Jul-21 A	12-Apr-21	21-May-21	-36d
P-SD-MSB-1060	Rebar/Reinforcing Steel	29d	12-Apr-21 A	21-May-21 A	12-Apr-21	06-Jul-21	31d
P-SD-MSB-1070	Precast Deck Panels Revision 0	18d	20-Jul-21 A	16-Aug-21 A	12-Apr-21	06-Jul-21	-27d
P-SD-MSB-1100	Girder Bracing	2d	18-Oct-21 A	19-Oct-21 A	10-May-21	14-May-21	-107d
City of Airdrie and Consultant Review Period		80d	10-May-21 A	01-Sep-21 A	26-Apr-21	20-Jul-21	-30d
P-SD-MSB-1090	MSE	5d	10-May-21 A	17-May-21 A	26-Apr-21	07-May-21	-5d
P-SD-MSB-1080	Piling	3d	12-May-21 A	17-May-21 A	26-Apr-21	07-May-21	-5d

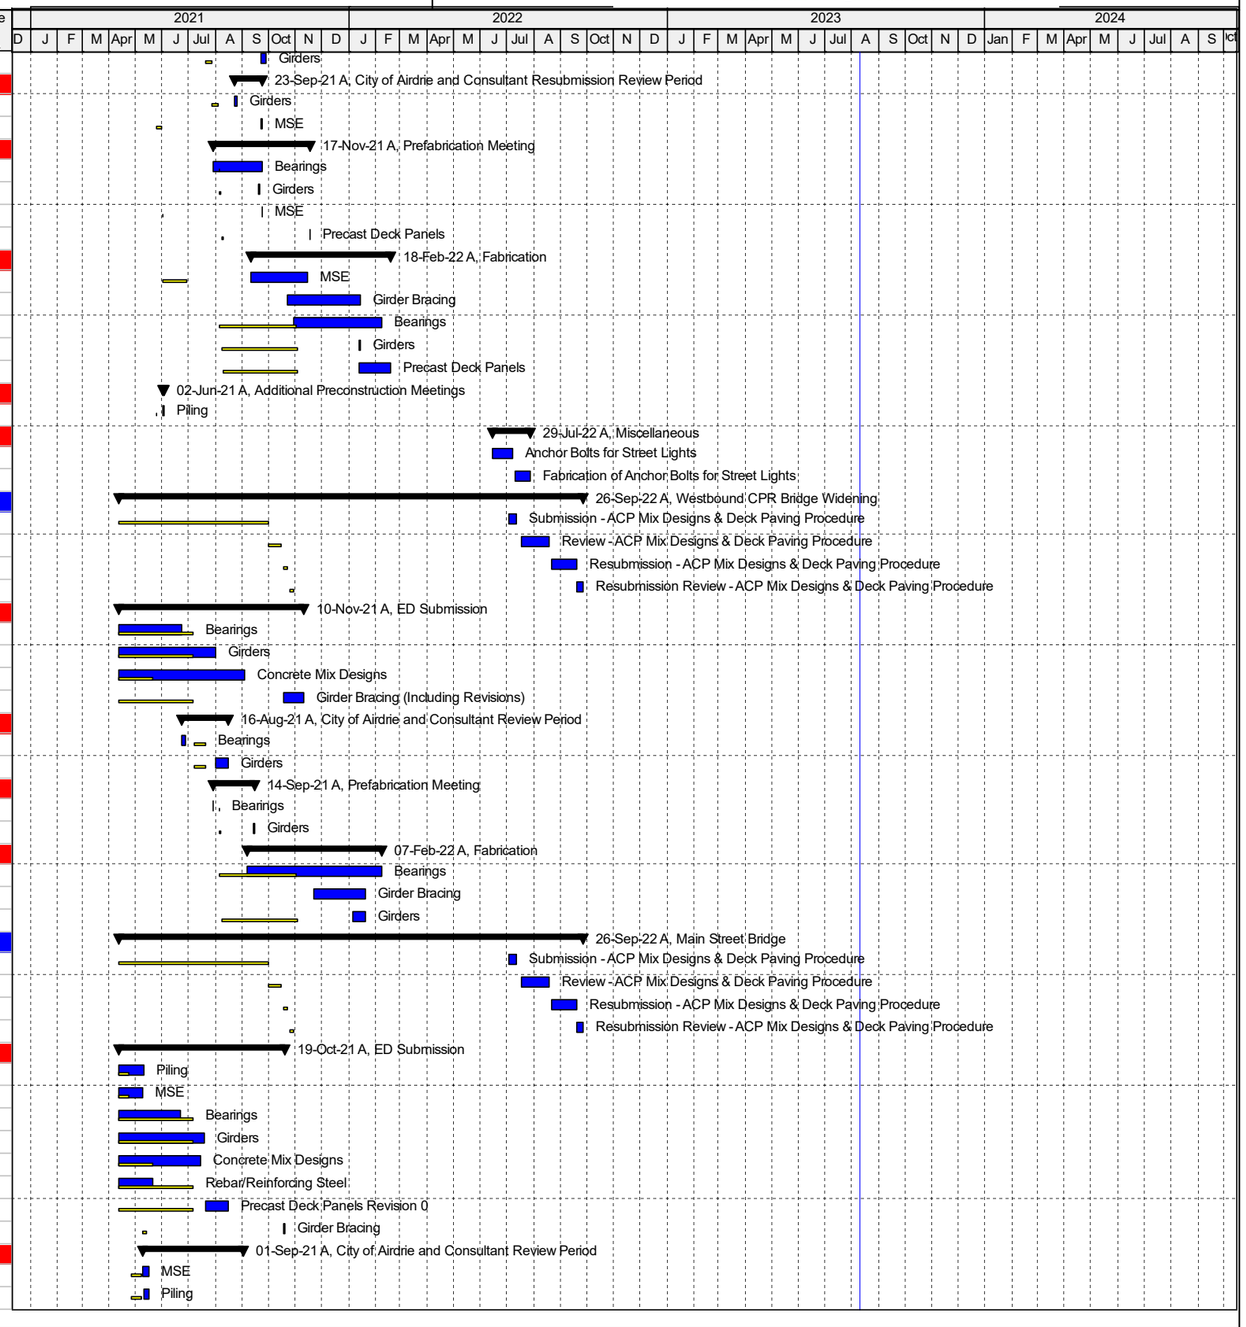

Remaining Level of Effort · Actual Work · Critical Remaining Work · Critical M/S · Project Baseline
Actual Level of Effort · Remaining Work · Milestone · Summary · Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE — COMMUNITY & OPPORTUNITY

EllisDon — We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
P-SD-MSB-1220	Rebar/Reinforcing Steel	1d	21-May-21 A	25-May-21 A	07-Jul-21	20-Jul-21	40d
P-SD-MSB-1140	Concrete Mix Designs	4d	15-Jul-21 A	21-Jul-21 A	25-May-21	07-Jun-21	-30d
P-SD-MSB-1210	Girders	8d	19-Jul-21 A	29-Jul-21 A	07-Jul-21	20-Jul-21	-6d
P-SD-MSB-1230	Precast Deck Panels	6d	25-Aug-21 A	01-Sep-21 A	07-Jul-21	20-Jul-21	-30d
ED Submittal Resubmission		25d	02-Aug-21 A	08-Sep-21 A	21-Jul-21	27-Jul-21	-28d
P-SD-MSB-1250	Girders	0d	02-Aug-21 A	02-Aug-21 A	21-Jul-21	27-Jul-21	-3d
P-SD-MSB-1270	Precast Deck Panels Revision 1	3d	02-Sep-21 A	08-Sep-21 A	21-Jul-21	27-Jul-21	-28d
City of Airdrie and Consultant Resubmission Review Period		26d	03-Aug-21 A	08-Sep-21 A	28-Jul-21	04-Aug-21	-24d
P-SD-MSB-1290	Girders	6d	03-Aug-21 A	11-Aug-21 A	28-Jul-21	04-Aug-21	-4d
P-SD-MSB-1310	Precast Deck Panels	4d	02-Sep-21 A	08-Sep-21 A	28-Jul-21	04-Aug-21	-24d
Prefabrication Meeting		69d	11-Aug-21 A	17-Nov-21 A	25-May-21	09-Aug-21	-70d
P-SD-MSB-1150	MSE	1d	11-Aug-21 A	11-Aug-21 A	25-May-21	25-May-21	-54d
P-SD-MSB-1330	Girders	1d	20-Sep-21 A	20-Sep-21 A	06-Aug-21	06-Aug-21	-30d
P-SD-MSB-1350	Precast Deck Panels	1d	17-Nov-21 A	17-Nov-21 A	09-Aug-21	09-Aug-21	-70d
Fabrication		170d	18-May-21 A	20-Jan-22 A	26-May-21	03-Nov-21	-53d
P-SD-MSB-1170	MSE	52d	18-May-21 A	02-Aug-21 A	26-May-21	15-Jun-21	-32d
P-SD-MSB-1340	Bearings	12d	10-Aug-21 A	25-Aug-21 A	06-Aug-21	01-Nov-21	46d
P-SD-MSB-1420	Girder Bracing	57d	29-Oct-21 A	20-Jan-22 A			
P-SD-MSB-1360	Girders	51d	08-Nov-21 A	20-Jan-22 A	09-Aug-21	02-Nov-21	-54d
P-SD-MSB-1370	Precast Deck Panels	38d	25-Nov-21 A	20-Jan-22 A	10-Aug-21	03-Nov-21	-53d
Additional Preconstruction Meetings		1d	02-Jun-21 A	02-Jun-21 A	25-May-21	25-May-21	-6d
P-SD-MSB-1160	Piling	1d	02-Jun-21 A	02-Jun-21 A	25-May-21	25-May-21	-6d
QEII Interchange Bridge		367d	12-Apr-21 A	26-Sep-22 A	12-Apr-21	10-Jan-22	-179d
P-SD-QE2IB-1310	Fabrication - Girders	52d	07-Feb-22 A	22-Apr-22 A	31-Aug-21	10-Jan-22	-71d
P-SD-QE2IB-1280	Fabrication - MSE	19d	25-Feb-22 A	24-Mar-22 A	27-Aug-21	08-Oct-21	-113d
P-SD-QE2IB-1040	Submission - ACP Mix Designs & Deck Paving Procedure	6d	04-Jul-22 A	12-Jul-22 A	12-Apr-21	30-Sep-21	-194d
P-SD-QE2IB-1320	Review - ACP Mix Designs & Deck Paving Procedure	24d	18-Jul-22 A	19-Aug-22 A	01-Oct-21	15-Oct-21	-212d
P-SD-QE2IB-1330	Resubmission - ACP Mix Designs & Deck Paving Procedure	20d	22-Aug-22 A	19-Sep-22 A	18-Oct-21	22-Oct-21	-227d
P-SD-QE2IB-1340	Resubmission Review - ACP Mix Designs & Deck Paving Procedure	5d	20-Sep-22 A	26-Sep-22 A	25-Oct-21	29-Oct-21	-227d
ED Submission		66d	12-Apr-21 A	15-Jul-21 A	12-Apr-21	27-Jul-21	9d
P-SD-QE2IB-1000	Piling	47d	12-Apr-21 A	17-Jun-21 A	12-Apr-21	23-Apr-21	-37d
P-SD-QE2IB-1020	Girders	32d	12-Apr-21 A	27-May-21 A	12-Apr-21	06-Jul-21	28d
P-SD-QE2IB-1030	Concrete Mix Designs	66d	12-Apr-21 A	15-Jul-21 A	12-Apr-21	21-May-21	-36d
P-SD-QE2IB-1050	Rebar/Reinforcing Steel	29d	12-Apr-21 A	21-May-21 A	12-Apr-21	06-Jul-21	31d
P-SD-QE2IB-1070	MSE	4d	03-May-21 A	07-May-21 A	03-May-21	27-Jul-21	56d
City of Airdrie and Consultant Review Period		51d	07-May-21 A	21-Jul-21 A	26-Apr-21	11-Aug-21	15d
P-SD-QE2IB-1200	MSE	14d	07-May-21 A	28-May-21 A	28-Jul-21	11-Aug-21	52d
P-SD-QE2IB-1160	Rebar/Reinforcing Steel	22d	21-May-21 A	23-Jun-21 A	07-Jul-21	20-Jul-21	19d
P-SD-QE2IB-1150	Girders	5d	27-May-21 A	03-Jun-21 A	07-Jul-21	20-Jul-21	33d
P-SD-QE2IB-1060	Piling	9d	17-Jun-21 A	30-Jun-21 A	26-Apr-21	07-May-21	-36d
P-SD-QE2IB-1100	Concrete Mix Designs	3d	16-Jul-21 A	21-Jul-21 A	25-May-21	07-Jun-21	-30d
Prefabrication Meeting		13d	01-Sep-21 A	20-Sep-21 A	26-Aug-21	30-Aug-21	-14d
P-SD-QE2IB-1260	MSE	1d	01-Sep-21 A	01-Sep-21 A	26-Aug-21	26-Aug-21	-4d
P-SD-QE2IB-1290	Girders	1d	20-Sep-21 A	20-Sep-21 A	30-Aug-21	30-Aug-21	-14d
Traffic Poles, Signals, Control Boxes, Davits, Arms, Lights and Street Lighting		180d	10-Oct-22 A	04-Jul-23 A	12-Apr-21	08-Nov-21	-410d
P-SD-TPS-1000	Submission - Traffic Poles, Signals, Control Boxes, Davits, Arms, Lights and St	15d	10-Oct-22 A	31-Oct-22 A	12-Apr-21	18-Aug-21	-301d
P-SD-TPS-1010	Review - Traffic Poles, Signals, Control Boxes, Davits, Arms, Lights and Street	24d	01-Nov-22 A	02-Dec-22 A	19-Aug-21	01-Sep-21	-315d
P-SD-TPS-1020	Resubmission - Traffic Poles, Signals, Control Boxes, Davits, Arms, Lights and	63d	05-Dec-22 A	10-Mar-23 A	02-Sep-21	16-Sep-21	-368d
P-SD-TPS-1030	Resubmission Review - Traffic Poles, Signals, Control Boxes, Davits, Arms, Lig	19d	13-Mar-23 A	07-Apr-23 A	17-Sep-21	23-Sep-21	-382d
P-SD-TPS-1050	Fabrication - Traffic Poles, Signals, Control Boxes, Davits, Arms, Lights and Str	59d	10-Apr-23 A	04-Jul-23 A	27-Sep-21	08-Nov-21	-410d
High Mast Lighting		179d	21-Nov-22 A	11-Aug-23	12-Apr-21	09-Nov-21	-437d
P-SD-HML-1000	Submission - High Mast Lighting	10d	21-Nov-22 A	02-Dec-22 A	12-Apr-21	18-Aug-21	-325d
P-SD-HML-1010	Review - High Mast Lighting	3d	05-Dec-22 A	07-Dec-22 A	19-Aug-21	01-Sep-21	-318d
P-SD-HML-1020	Resubmission - High Mast Lighting	40d	08-Dec-22 A	10-Feb-23 A	02-Sep-21	16-Sep-21	-348d
P-SD-HML-1030	Resubmission Review - High Mast Lighting	5d	10-Feb-23 A	16-Feb-23 A	17-Sep-21	23-Sep-21	-348d
P-SD-HML-1050	Fabrication - High Mast Lighting	119d	22-Feb-23 A	11-Aug-23	28-Sep-21	09-Nov-21	-437d
Sign Structures		400d	04-Jan-22 A	11-Aug-23	12-Apr-21	25-Mar-22	-342d

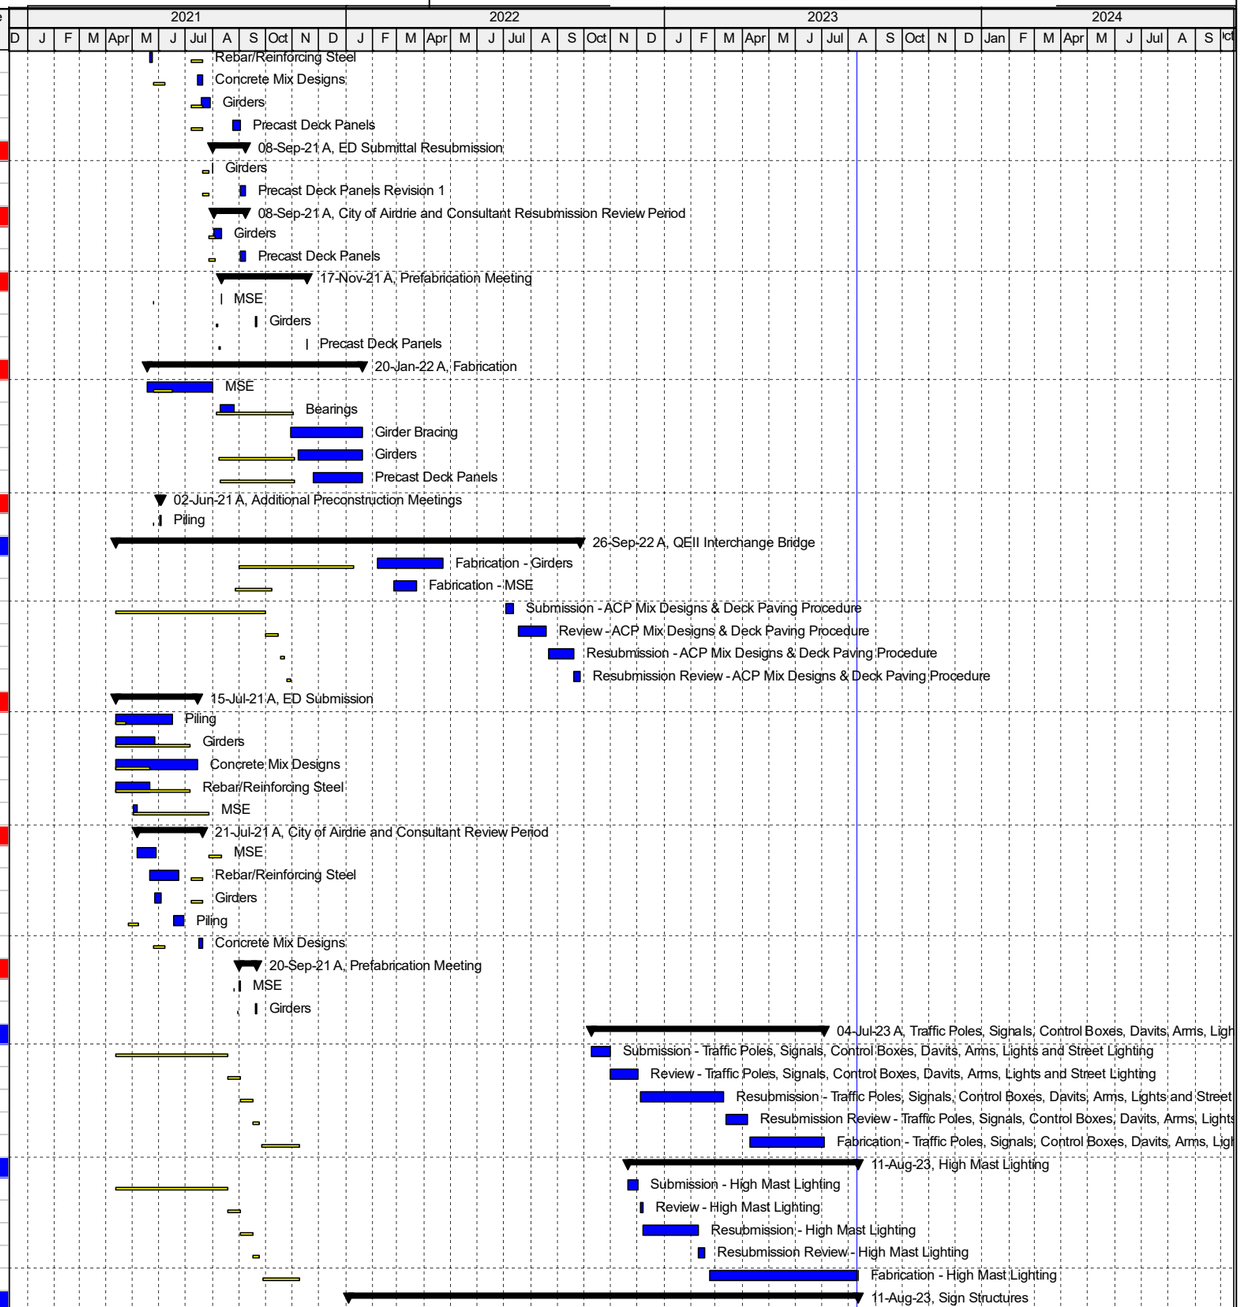

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
P-SD-SS-1000	Submission - Sign Structures	10d	04-Jan-22 A	18-Jan-22 A	12-Apr-21	30-Sep-21	-73d
P-SD-SS-1010	Review - Sign Structures	133d	19-Jan-22 A	29-Jul-22 A	01-Oct-21	15-Oct-21	-197d
P-SD-SS-1060	Supply of Steel	48d	01-Aug-22 A	11-Oct-22 A			
P-SD-SS-1040	Pre-fab Meeting - Sign Structures	1d	12-Oct-22 A	12-Oct-22 A	15-Nov-21	15-Nov-21	-227d
P-SD-SS-1050	Fabrication - Sign Structures	205d	13-Oct-22 A	11-Aug-23	16-Nov-21	25-Mar-22	-342d
Third Party Utilities		288d	23-Feb-21 A	18-Apr-22 A	23-Feb-21	16-May-22	20d
Utility Relocation Coordination		57d	23-Feb-21 A	14-May-21 A	23-Feb-21	18-May-21	3d
P-TPU-1000	Utility Relocation Coordination (Telus)	57d	23-Feb-21 A	14-May-21 A	23-Feb-21	18-May-21	3d
P-TPU-1010	Utility Protection Coordination (Atco)	30d	23-Feb-21 A	06-Apr-21 A	23-Feb-21	06-Apr-21	0d
P-TPU-1020	Utility Relocation Coordination (Fortis)	15d	23-Feb-21 A	15-Mar-21 A	23-Feb-21	15-Mar-21	0d
P-TPU-1030	Utility Relocation Coordination (Shaw)	40d	23-Feb-21 A	20-Apr-21 A	23-Feb-21	20-Apr-21	0d
P-TPU-1040	Utility Relocation Coordination (Others)	40d	23-Feb-21 A	20-Apr-21 A	23-Feb-21	20-Apr-21	0d
Utility Relocations, Removals and Salvage Completions		273d	16-Mar-21 A	18-Apr-22 A	16-Mar-21	16-May-22	20d
P-TPU-1050	Salvage 5 Powerpoles and guy Wires for Nose Creek Re-alignment (Fortis)	0d	16-Mar-21 A		16-Mar-21		0d
P-TPU-1060	Salvage 282m of Powerline (Fortis)	0d	16-Mar-21 A		16-Mar-21		0d
P-TPU-1080	Salvage Streetlighting at EB CPR East and West Abutments	0d	28-Apr-21 A		01-Jun-21		23d
P-TPU-1070	Salvage Power Pole at Main Street Bridge East Abutment	0d	28-Apr-21 A		30-Apr-21		2d
P-TPU-1290	Relocate Telus Optik Line At main Street Bridge East Abutment	0d		14-May-21 A			
P-TPU-1280	Relocate ATCO At main Street Bridge West Abutment	0d		26-Jul-21 A			
P-TPU-1090	Salvage Variabe Message Board	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1100	Bury Existing Shaw Vault (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1110	Remove 508m of Buried Power (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1120	Relocate 562m of Buried Telus (Telus/Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1130	Salvage 40m of Overhead Power (Fortis)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1140	Relocate 56m of Buried Shaw Cable (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1150	Relocate 96m of Buried Shaw Cable (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1160	Relocate 275m of Buried Shaw Cable (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1170	Relocate 398m of Buried Shaw Fibre (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1180	Relocate 215m of Powerline (Fortis)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1190	Relocate 6 Power Poles (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1200	Remove Street Lighting (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1210	Salvage Street Lighting (Fortis)	43d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-49d
P-TPU-1220	Salvage 260m of Powerline (Fortis)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1230	Relocate 241m of Buried Shaw Fibre (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1240	Relocate 443m of Overhead Shaw Cable (Others)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1250	Salvage 8 Existing Power Poles (Fortis)	44d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	09-Aug-21	-50d
P-TPU-1260	Remove/Salvage Street Lighting for Southpoint Landing Roadworks (TBC Fort	0d	18-Apr-22 A		16-May-22		20d
P-TPU-1270	Remove/Salvage Street Lighting for Reynolds Gate Roadworks (TBC Fortis & (	0d	18-Apr-22 A		16-May-22		20d
Changes & Delays		539d	17-May-21 A	13-Jul-23 A			
Atco Conflict Relocation @ Main Street		10d	17-May-21 A	01-Jun-21 A			
X-ATCO-1000	Anticipated Redesign	10d	17-May-21 A	01-Jun-21 A			
Main Street Bridge Design Delay		9d	21-May-21 A	04-Jun-21 A			
X-MSBDD-1000	Redesign Of Pile Layout	9d	21-May-21 A	04-Jun-21 A			
COVID		1d	16-Sep-21 A	16-Sep-21 A			
X-COVD-1000	COVID Mandatory Work From Home	1d	16-Sep-21 A	16-Sep-21 A			
Storm Pond Design Developement		77d	31-Dec-21 A	22-Apr-22 A			
P-LA-1020	Storm Pond Wetland Permit	77d	31-Dec-21 A	22-Apr-22 A			
Storm Pond Water Contamination		157d	25-May-22 A	13-Jan-23 A			
X-PWC-1000	Water Sample - Contamination Discovered	1d	25-May-22 A	25-May-22 A			
X-PWC-1010	Rain Event - Pond Filled with Rainwater	8d	14-Jun-22 A	23-Jun-22 A			
X-PWC-1020	Grading Activities Stopped	1d	14-Jun-22 A	14-Jun-22 A			
X-PWC-1030	Rainwater Testing - Contaminents Found	1d	23-Jun-22 A	23-Jun-22 A			
X-PWC-1040	Letter sent to City with Options	1d	24-Jun-22 A	24-Jun-22 A			
X-PWC-1050	City Review and Response	8d	27-Jun-22 A	08-Jul-22 A			
X-PWC-1070	Pump Water into New Reserve	125d	11-Jul-22 A	13-Jan-23 A			

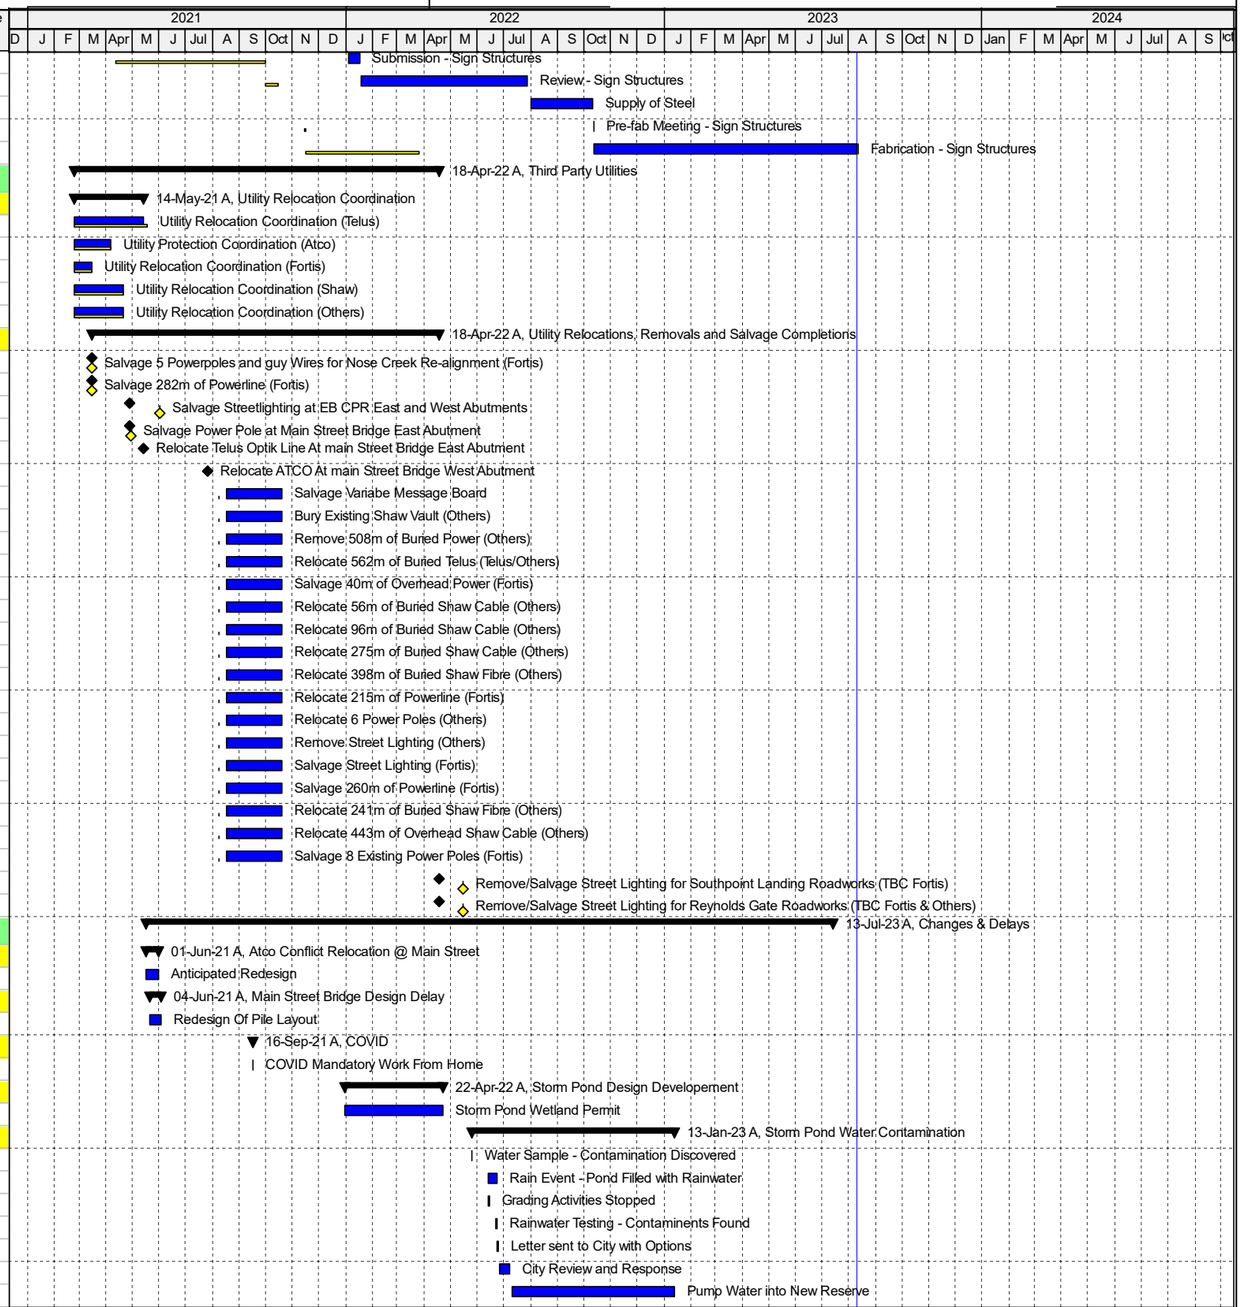

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
X-PWC-1090	Grading Starts	36d	11-Jul-22 A	30-Aug-22 A			
Precast Panel		4d	11-Aug-22 A	16-Aug-22 A			
X-MSE-1000	Change in Dimension of Precast Panel of MSE Wall on East CPR Bridge	1d	11-Aug-22 A	11-Aug-22 A			
X-MSE-1010	Procurement of Precast Panel of MSE Wall on East CPR Bridge	3d	12-Aug-22 A	16-Aug-22 A			
QE2 Abutment Erosion Repair		184d	23-Aug-22 A	19-May-23 A			
X-ERO-1000	Submission of Repair Procedure	5d	23-Aug-22 A	29-Aug-22 A			
X-ERO-1010	Review of Repair Procedure	20d	30-Aug-22 A	27-Sep-22 A			
X-ERO-1020	Approval of Repair Procedure	1d	28-Sep-22 A	28-Sep-22 A			
X-ERO-1030	Potential Issue Identified	1d	28-Oct-22 A	28-Oct-22 A			
X-ERO-1040	Alternate Repair Procedure Proposed (Fill-Foam)	5d	31-Oct-22 A	04-Nov-22 A			
X-ERO-1050	Review of Alternate Repair Procedure (Fill-Foam)	53d	07-Nov-22 A	27-Jan-23 A			
X-ERO-1060	Multiple Solutions Proposed/Consultant Reviewing	47d	30-Jan-23 A	05-Apr-23 A			
West End of Bridge		21d	11-Apr-23 A	09-May-23 A			
X-ERO-1070	Completion of Repair (Lower Stage - West)	13d	11-Apr-23 A	28-Apr-23 A			
X-ERO-1090	Completion of Repair (Upper Stage - West)	8d	28-Apr-23 A	09-May-23 A			
East End of Bridge		16d	28-Apr-23 A	19-May-23 A			
X-ERO-1110	Completion of Repair (Lower Stage - East)	8d	28-Apr-23 A	09-May-23 A			
X-ERO-1100	Completion of Repair (Upper Stage - East)	8d	10-May-23 A	19-May-23 A			
WB CPR - Bridge Offset Dimensions		168d	18-Feb-22 A	20-Oct-22 A			
X-CPBD-1000	RFI-096 Issued - Diaphram Dimensions	1d	18-Feb-22 A	18-Feb-22 A			
X-CPBD-1010	RFI-096 Reponse - Dimensions Revised	2d	19-Feb-22 A	23-Feb-22 A			
X-CPBD-1020	RFI-096 Revised Response - Dimensions Revised	1d	08-Mar-22 A	08-Mar-22 A			
X-CPBD-1030	RFI-163 - Bridge Offset Dimensions	1d	12-Oct-22 A	12-Oct-22 A			
X-CPBD-1040	RFI-163 - Response	6d	13-Oct-22 A	20-Oct-22 A			
Atco Conflict West of CPR		28d	02-Jun-23 A	13-Jul-23 A			
X-DEL-001-1000	Delay - Gas Line Conflict - West of CPR Bridge	28d	02-Jun-23 A	13-Jul-23 A			
Integrated Phased Planning		519d	02-Sep-21 A	02-Oct-23			
IPP Planning		207d	28-Mar-22 A	26-Jan-23 A			
IPP-PLAN-1000	2022 Baseline Planning - Structures	77d	28-Mar-22 A	18-Jul-22 A			
IPP-PLAN-1010	2022 Baseline Planning - Roads	60d	21-Apr-22 A	18-Jul-22 A			
IPP-PLAN-1020	2022 Baseline is Complete	0d		18-Jul-22 A			
IPP-PLAN-1030	2023 Baseline Planning	18d	02-Jan-23 A	26-Jan-23 A			
IPP Safety		476d	20-Oct-21 A	15-Sep-23			
IPP-SAFE-1000	Third Party Joint Use Trench Handover	1d	20-Oct-21 A	20-Oct-21 A			
IPP-SAFE-1010	Winter Shutdown Preparation	5d	13-Dec-21 A	17-Dec-21 A			
IPP-SAFE-1040	Subcontractor Coordination Deep Utilities	1d	01-Feb-22 A	01-Feb-22 A			
IPP-SAFE-1120	MSB Pre Girder Erection Rigging Inspection	0d	14-Feb-22 A	14-Feb-22 A			
IPP-SAFE-1020	Pre Construction Mtg. Girder Erection Over CP Bridge	1d	23-Feb-22 A	23-Feb-22 A			
IPP-SAFE-1030	EBCPR Pre Girder Erection Rigging Inspection	1d	23-Feb-22 A	23-Feb-22 A			
IPP-SAFE-1110	WBCPR Pre Girder Erection Rigging Inspection	1d	23-Feb-22 A	23-Feb-22 A			
IPP-SAFE-1140	EBCPR Pre Deck Panel Rigging Inspection	0d	25-Feb-22 A	25-Feb-22 A			
IPP-SAFE-1160	MSB Pre Deck Panel Rigging Inspection	0d	25-Feb-22 A	25-Feb-22 A			
IPP-SAFE-1180	EBCPR Fall Protection Training Workshop	1d	01-Mar-22 A	02-Mar-22 A			
IPP-SAFE-1210	MSB Fall Protection Training Workshop	1d	01-Mar-22 A	01-Mar-22 A			
IPP-SAFE-1050	Procedure and Stand Down Working Over Live Traffic QEII	1d	21-Apr-22 A	21-Apr-22 A			
IPP-SAFE-1220	MSB Fall Protection Training Workshop	1d	04-May-22 A	04-May-22 A			
IPP-SAFE-1230	QEII Fall Protection Training Workshop	1d	09-May-22 A	09-May-22 A			
IPP-SAFE-1130	QEII Pre Girder Erection Rigging Inspection	1d	10-May-22 A	10-May-22 A			
IPP-SAFE-1070	EBCPR Safety Stand Down Pre Deck Pour	7d	10-Jun-22 A	21-Jun-22 A			
IPP-SAFE-1090	MSB Safety Stand Down Pre Deck Pour	0d	08-Jul-22 A	08-Jul-22 A			
IPP-SAFE-1100	QEII Safety Stand Down Pre Deck Pour	1d	09-Sep-22 A	09-Sep-22 A			
IPP-SAFE-1170	Winter Safety Planning	4d	17-Oct-22 A	20-Oct-22 A			
IPP-SAFE-1150	WBCPR Pre Deck Panel Rigging Inspection	1d	13-Jan-23 A	13-Jan-23 A			
IPP-SAFE-1200	WBCPR Fall Protection Training Workshop	1d	20-Jan-23 A	20-Jan-23 A			
IPP-SAFE-1190	Safety Stand Down - CP Rail - WB CPR Deck Pour	1d	29-May-23 A	29-May-23 A			
IPP-SAFE-1060	Safety Stand Down Pre Completion Drive	1d	15-Sep-23	15-Sep-23			

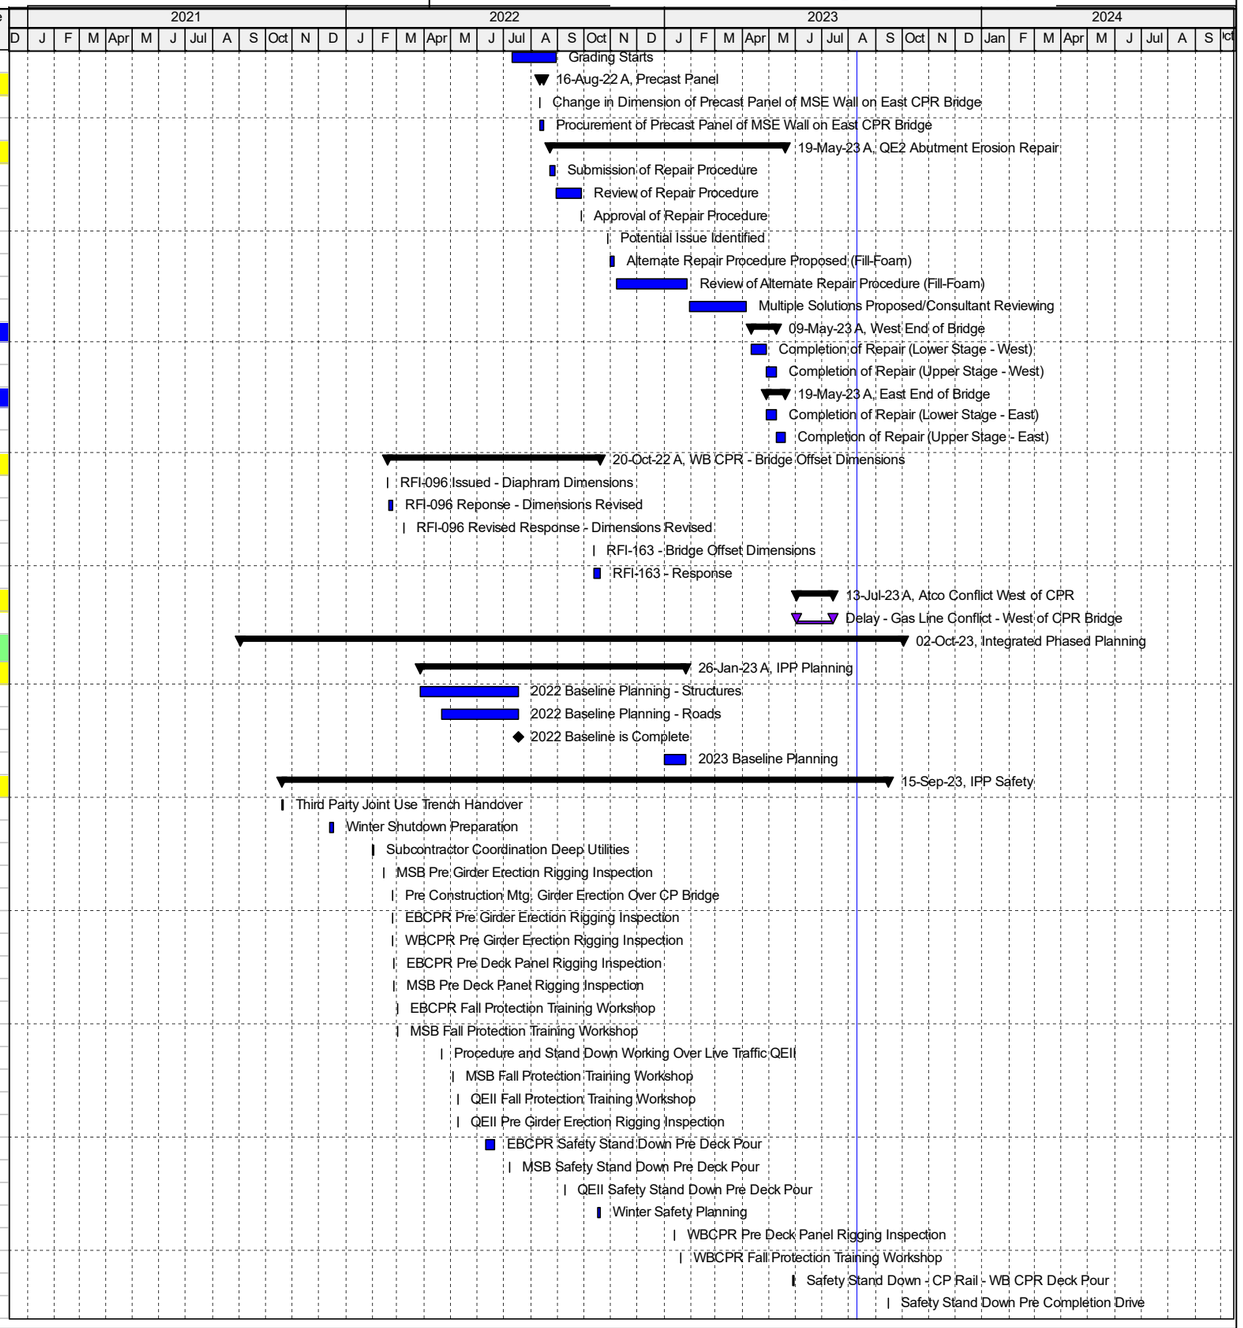

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline

Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
IPP QA/QC		489d	18-Oct-21 A	02-Oct-23			
IPP-QAQC-1000	Main Street MSE Walls Handover Package	0d	18-Oct-21 A	18-Oct-21 A			
IPP-QAQC-1010	CPR Abutment 1 MSE Wall Partial Handover Package	1d	04-Nov-21 A	04-Nov-21 A			
IPP-QAQC-1020	Creek Handover	1d	08-Nov-21 A	08-Nov-21 A			
IPP-QAQC-1030	East Bound CPR Bridge Pre Safety InspectionWalkthrough	1d	11-May-23 A	11-May-23 A			
IPP-QAQC-1100	Construction Completion Strategy Meeting	1d	17-Aug-23	17-Aug-23			
IPP-QAQC-1050	West Bound CPR Bridge Widening Pre Safety Inspection Walkthrough	1d	31-Aug-23	31-Aug-23			
IPP-QAQC-1090	Deficiency Strategy Meeting	1d	18-Sep-23	18-Sep-23			
IPP-QAQC-1070	Main Street Bridge Pre safety Inspection Walkthrough	1d	18-Sep-23	18-Sep-23			
IPP-QAQC-1080	QEII Interchange Bridge Pre Safety Inspection Walkthrough	1d	18-Sep-23	18-Sep-23			
IPP-QAQC-1040	Drainage Handover and Redline Markups	1d	02-Oct-23	02-Oct-23			
IPP-QAQC-1060	Storm Pond Certificate Of Completion	1d	02-Oct-23	02-Oct-23			
Central Purchasing		106d	02-Sep-21 A	03-Feb-22 A			
IPP-CP-1000	Pre Winter Heating Review	1d	02-Sep-21 A	02-Sep-21 A			
IPP-CP-1010	Quarterly Central Purchasing Meeting	1d	03-Feb-22 A	03-Feb-22 A			
Work Constraints		556d	01-Apr-21 A	23-Jun-23 A	01-Apr-21	15-May-23	-27d
WX-1000	In Stream Work 2021	61d	01-Apr-21 A	31-May-21 A	01-Apr-21	31-May-21	0d
WX-1010	Winter 2021 - 2022	160d	14-Nov-21 A	22-Apr-22 A	14-Nov-21	15-May-22	23d
WX-1020	Winter 2022 - 2023	181d	31-Oct-22 A	29-Apr-23 A	14-Nov-22	15-May-23	16d
Weather Event - 2022.11.01		7d	01-Nov-22 A	10-Nov-22 A			
WX-6000	Snowfall Event >20cm Snow & Extreme Cold	7d	01-Nov-22 A	10-Nov-22 A			
Weather Event - 2023.02.20		4d	20-Feb-23 A	24-Feb-23 A			
WX-1040	Snow >30cm Followed by Extreme Cold	4d	20-Feb-23 A	24-Feb-23 A			
Weather Event - 2023.06.20		2d	20-Jun-23 A	23-Jun-23 A			
X-WEA-003-1000	Rain >25mm - Site Drying Time	2d	20-Jun-23 A	23-Jun-23 A			
Construction		1144d	22-Mar-21 A	15-Oct-25	22-Mar-21	02-Oct-25	-8d
Mobilization		44d	22-Mar-21 A	21-May-21 A	22-Mar-21	07-May-21	-10d
C-MOB-1000	Early Access Request and Approval	5d	22-Mar-21 A	26-Mar-21 A	22-Mar-21	26-Mar-21	0d
C-MOB-1010	Early Access Mobilization (Set Up Trailers, Construction Fencing, Tree Protectic	20d	05-Apr-21 A	30-Apr-21 A	05-Apr-21	30-Apr-21	0d
C-MOB-1020	Mobilize to Site - Work Commences	1d	21-May-21 A	21-May-21 A	07-May-21	07-May-21	-10d
Structures		601d	05-May-21 A	29-Sep-23	03-May-21	26-Jul-23	-45d
Eastbound CPR Bridge		468d	28-Jun-21 A	14-May-23 A	14-Jun-21	19-Aug-22	-180d
Foundations		67d	28-Jun-21 A	01-Oct-21 A	14-Jun-21	17-Sep-21	-10d
Site Preparation		15d	28-Jun-21 A	19-Jul-21 A	14-Jun-21	25-Jun-21	-15d
C-ECPRB-1000	Site Stripping & Pre-grading	15d	28-Jun-21 A	19-Jul-21 A	14-Jun-21	25-Jun-21	-15d
Abutment Piling		19d	07-Sep-21 A	01-Oct-21 A	22-Jul-21	17-Sep-21	-10d
C-ECPRB-1040	Abutment 2 Piling - 11 H Piles (Drilled)	9d	07-Sep-21 A	17-Sep-21 A	03-Sep-21	17-Sep-21	0d
C-ECPRB-1010	Abutment 1 Piling - 12 H Piles (Drilled)	7d	23-Sep-21 A	01-Oct-21 A	22-Jul-21	05-Aug-21	-40d
Pier Piling		18d	26-Jul-21 A	20-Aug-21 A	06-Aug-21	02-Sep-21	10d
C-ECPRB-1020	Pier Piling - 10 Battered CIP Piles	18d	26-Jul-21 A	20-Aug-21 A	06-Aug-21	02-Sep-21	10d
Substructure (Including MSE)		130d	18-Aug-21 A	23-Feb-22 A	20-Sep-21	17-Jan-22	-26d
Abutment Seat		42d	21-Oct-21 A	17-Dec-21 A	20-Sep-21	04-Nov-21	-31d
C-ECPRB-1080	Abutment Seat 2 w/ Plinth - F/R/P (Including 4th pour)	11d	21-Oct-21 A	04-Nov-21 A	12-Oct-21	01-Nov-21	-3d
C-ECPRB-1110	Abutment Seat 2 - Cure	7d	05-Nov-21 A	11-Nov-21 A	02-Nov-21	04-Nov-21	-7d
C-ECPRB-1050	Abutment Seat 1 w/ Plinth - F/R/P	19d	15-Nov-21 A	09-Dec-21 A	20-Sep-21	08-Oct-21	-43d
C-ECPRB-1090	Abutment Seat 1 - Cure	8d	10-Dec-21 A	17-Dec-21 A	12-Oct-21	14-Oct-21	-64d
Pier		113d	18-Aug-21 A	28-Jan-22 A	04-Oct-21	14-Jan-22	-10d
C-ECPRB-1060	Mudslab	2d	18-Aug-21 A	20-Aug-21 A	04-Oct-21	04-Oct-21	31d
C-ECPRB-1070	Pier Footing	9d	24-Aug-21 A	03-Sep-21 A	05-Oct-21	19-Oct-21	30d
C-ECPRB-1100	Pier Columns F/R/P	45d	06-Sep-21 A	09-Nov-21 A	20-Oct-21	14-Dec-21	25d
C-ECPRB-1120	Pier Cap	15d	10-Jan-22 A	28-Jan-22 A	15-Dec-21	07-Jan-22	-15d
C-ECPRB-1130	Pier Cap Plinth	1d	28-Jan-22 A	28-Jan-22 A	10-Jan-22	14-Jan-22	-10d
Bearing Installation		1d	23-Feb-22 A	23-Feb-22 A	17-Jan-22	17-Jan-22	-26d
C-ECPRB-1140	Bearing Installation	1d	23-Feb-22 A	23-Feb-22 A	17-Jan-22	17-Jan-22	-26d
Superstructure		401d	04-Oct-21 A	14-May-23 A	06-Aug-21	19-Aug-22	-180d
Girder Erection		3d	23-Feb-22 A	28-Feb-22 A	18-Jan-22	26-Jan-22	-21d
C-ECPRB-1150	Girder Erection (14)	3d	23-Feb-22 A	28-Feb-22 A	18-Jan-22	26-Jan-22	-21d

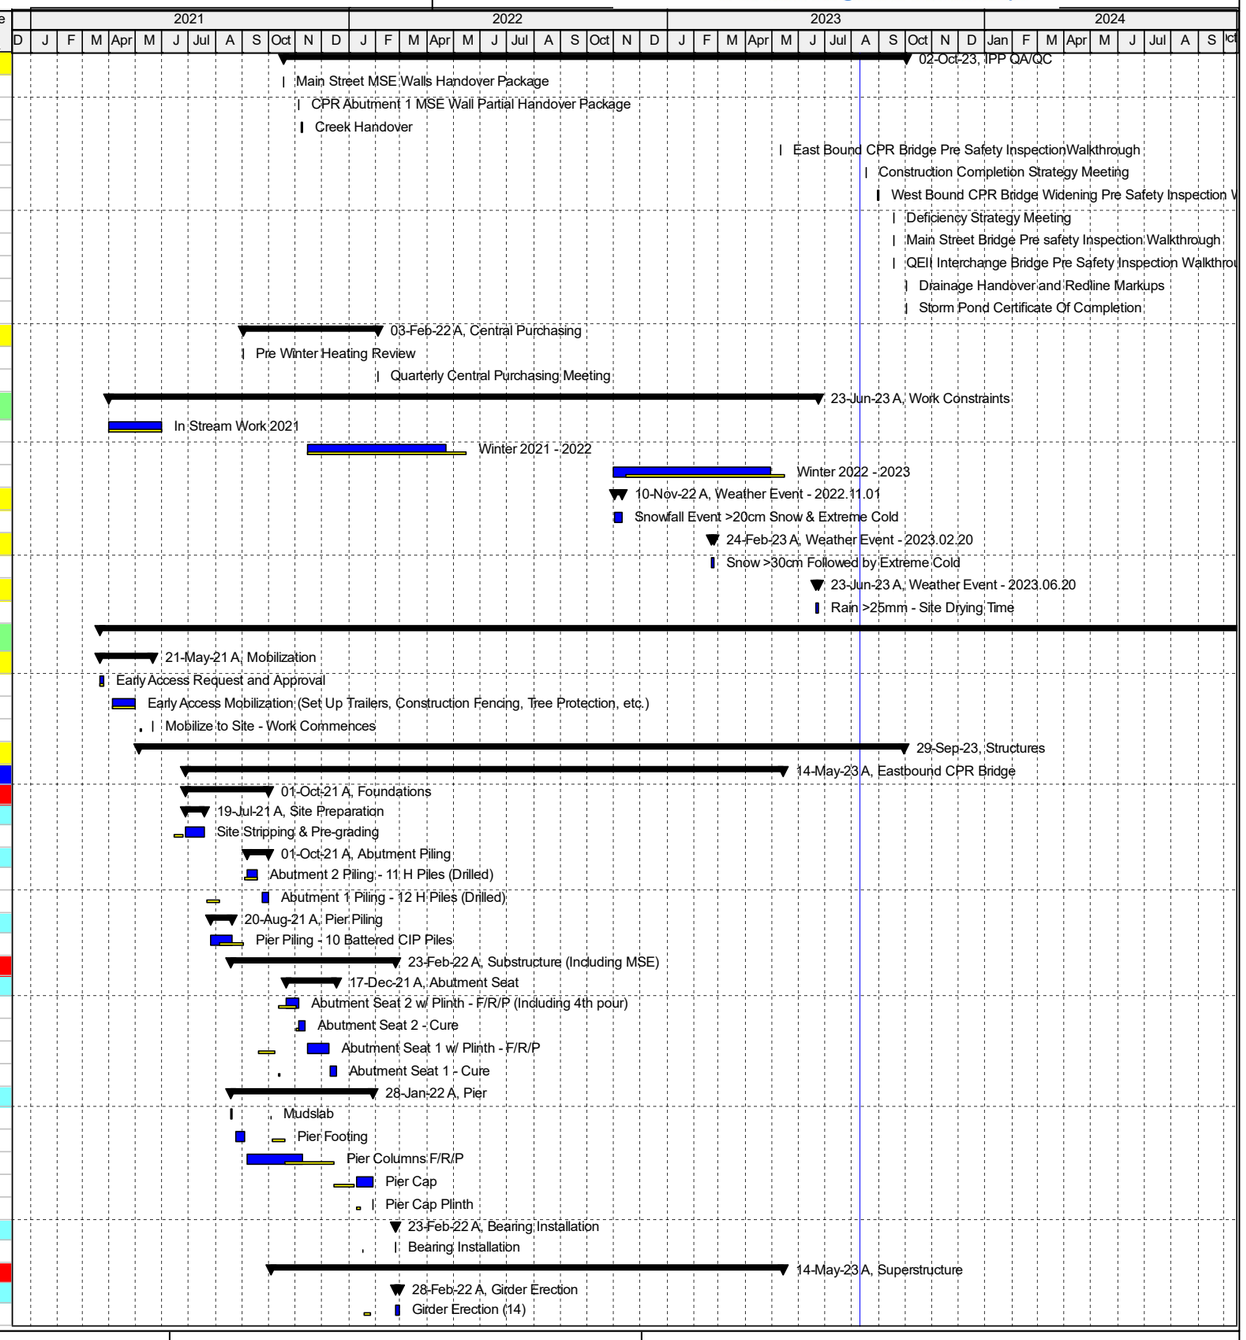

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
Diaphragms		27d	08-Apr-22 A	18-May-22 A	27-Jan-22	24-Feb-22	-57d
West Diaphragm		18d	08-Apr-22 A	05-May-22 A	27-Jan-22	09-Feb-22	-58d
C-ECPRB-1410	Form West Abutment (Abutment 1)	7d	08-Apr-22 A	20-Apr-22 A			
C-ECPRB-1160	Rebar West Abutment Diaphragms	2d	25-Apr-22 A	26-Apr-22 A	27-Jan-22	09-Feb-22	-52d
C-ECPRB-1440	Close West Abutment Forms, QC Inspection/Signoff	3d	27-Apr-22 A	29-Apr-22 A			
C-ECPRB-1480	Pour West Diaphragm	0d	05-May-22 A	05-May-22 A			
Pier Diaphragm		16d	26-Apr-22 A	18-May-22 A	10-Feb-22	24-Feb-22	-57d
C-ECPRB-1170	Pier Diaphragm Rebar	3d	26-Apr-22 A	28-Apr-22 A	10-Feb-22	24-Feb-22	-44d
C-ECPRB-1450	Form Pier Diaphragm, QC Signoff	5d	29-Apr-22 A	05-May-22 A			
C-ECPRB-1800	Pour Pier Diaphragm	0d	18-May-22 A	18-May-22 A			
East Diaphragm		8d	06-May-22 A	18-May-22 A			
C-ECPRB-1370	Rebar East Abutment Diaphragms	4d	06-May-22 A	11-May-22 A			
C-ECPRB-1420	Form East Abutment (Abutment 2)	0d	06-May-22 A	06-May-22 A			
C-ECPRB-1430	Close Forms, QC Inspections/Signoff	3d	12-May-22 A	16-May-22 A			
C-ECPRB-1470	Pour East Diaphragm	0d	18-May-22 A	18-May-22 A			
Deck		101d	01-Mar-22 A	25-Jul-22 A	25-Feb-22	06-Aug-22	9d
C-ECPRB-1380	Install Pier Diaphragm Walkway	4d	01-Mar-22 A	05-Mar-22 A			
C-ECPRB-1390	Strip Pier Cap Soffit	5d	07-Mar-22 A	11-Mar-22 A			
C-ECPRB-1360	Deck Survey/Haunch Calculations	17d	14-Mar-22 A	06-Apr-22 A			
C-ECPRB-1180	Precast Deck Panel Installation	9d	11-Apr-22 A	22-Apr-22 A	25-Feb-22	17-Mar-22	-25d
C-ECPRB-1460	Install Overhangs	11d	09-May-22 A	25-May-22 A			
C-ECPRB-1190	Form Deck Edge	8d	30-May-22 A	09-Jun-22 A	18-Mar-22	13-May-22	-17d
C-ECPRB-1400	Deck Rebar Install	15d	30-May-22 A	20-Jun-22 A			
C-ECPRB-1490	Deck Screed Setup + Dry Runs	2d	16-Jun-22 A	20-Jun-22 A			
C-ECPRB-1200	Deck Placement 1 - Pour	1d	20-Jun-22 A	21-Jun-22 A	16-May-22	16-May-22	-24d
C-ECPRB-1500	Pour 2 Prep	4d	21-Jun-22 A	25-Jun-22 A			
C-ECPRB-1210	Deck Placement 2 with pier - Pour	2d	23-Jun-22 A	25-Jun-22 A	20-May-22	20-May-22	-24d
C-ECPRB-1540	Demobilize Deck Screed	3d	27-Jun-22 A	30-Jun-22 A			
C-ECPRB-1290	Pour prep 3	5d	04-Jul-22 A	10-Jul-22 A	31-Jul-22	06-Aug-22	19d
C-ECPRB-1600	Deck Placememnt 3 - Pour	1d	09-Jul-22 A	10-Jul-22 A			
C-ECPRB-1230	Deck Curing	14d	11-Jul-22 A	25-Jul-22 A	24-May-22	10-Jun-22	-44d
MSE Walls		262d	04-Oct-21 A	19-Oct-22 A	06-Aug-21	25-Jul-22	-59d
C-ECPRB-1030	Abutment 1 MSE Wall - Phase 1	15d	04-Oct-21 A	26-Oct-21 A	06-Aug-21	17-Sep-21	-25d
C-ECPRB-1220	Abutment 1 MSE Wall - Phase 2 (West)	28d	20-Jul-22 A	30-Aug-22 A	24-May-22	13-Jun-22	-53d
C-ECPRB-1810	Abutment 2 MSE Wall to Top U/S Diaphragm (East)	7d	08-Aug-22 A	17-Aug-22 A			
C-ECPRB-1510	Abutment 2 MSE Coping (East)	32d	22-Aug-22 A	05-Oct-22 A			
C-ECPRB-1260	Abutment 1 MSE Coping (West)	25d	31-Aug-22 A	05-Oct-22 A	27-Jun-22	25-Jul-22	-50d
C-ECPRB-1550	Curing	14d	06-Oct-22 A	19-Oct-22 A			
Approach Slabs		38d	25-Aug-22 A	19-Oct-22 A	25-Jun-22	29-Jun-22	-76d
C-ECPRB-1530	East Approach Slab - F/R/P	8d	25-Aug-22 A	07-Sep-22 A			
C-ECPRB-1250	West Approach Slab - F/R/P	3d	01-Sep-22 A	07-Sep-22 A	25-Jun-22	29-Jun-22	-46d
C-ECPRB-1520	East Approach Cure	14d	08-Sep-22 A	21-Sep-22 A			
C-ECPRB-1610	West Moment Slab F/R/P	20d	08-Sep-22 A	05-Oct-22 A			
C-ECPRB-1620	East Moment Slab F/R/P	20d	08-Sep-22 A	05-Oct-22 A			
C-ECPRB-1630	West Moment Slab Cure	14d	06-Oct-22 A	19-Oct-22 A			
Barriers		105d	05-Jul-22 A	01-Dec-22 A	21-Jul-22	19-Aug-22	-72d
C-ECPRB-1280	Deck Barrier - F/R/P	28d	05-Jul-22 A	15-Aug-22 A	21-Jul-22	30-Jul-22	-9d
C-ECPRB-1300	Deck Barrier Curing	14d	16-Aug-22 A	30-Aug-22 A	02-Aug-22	19-Aug-22	-10d
C-ECPRB-1560	Transition Barriers - F/R/P	25d	10-Oct-22 A	14-Nov-22 A			
C-ECPRB-1640	Transition Barrier Heating & Hoarding	5d	07-Nov-22 A	14-Nov-22 A			
C-ECPRB-1570	Transition Barriers Cure	17d	15-Nov-22 A	01-Dec-22 A			
Paving		5d	08-May-23 A	12-May-23 A	08-Aug-22	11-Aug-22	-186d
C-ECPRB-1310	Waterproofing	4d	08-May-23 A	11-May-23 A	08-Aug-22	10-Aug-22	-64d
C-ECPRB-1320	Bridge Paving - 1st Lift (EB CPR Bridge)	1d	11-May-23 A	12-May-23 A	11-Aug-22	11-Aug-22	-63d
C-ECPRB-1580	Temp Barrier Install	1d	11-May-23 A	12-May-23 A			
C-ECPRB-1820	Bridge Paving - 2nd Lift (EB CPR Bridge)	1d	12-May-23 A	12-May-23 A			
Finishing		0d	13-May-23 A	14-May-23 A	12-Aug-22	12-Aug-22	-185d

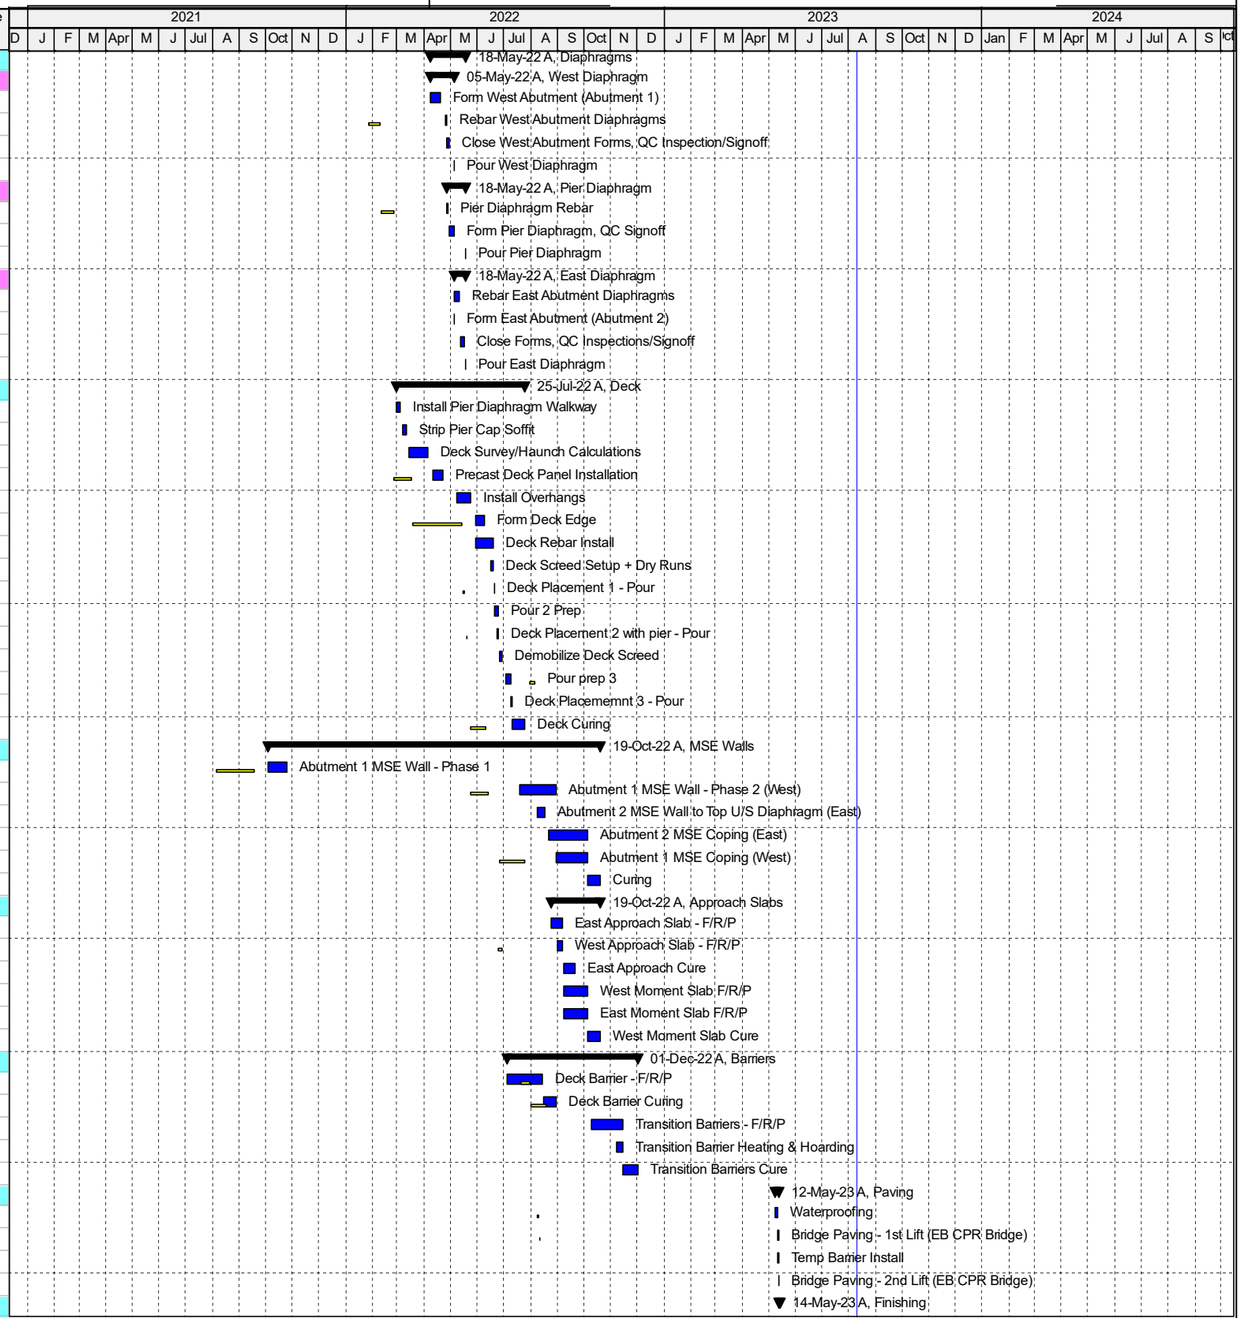

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-ECPRB-1330	Temp Traffic Configuration	1d	13-May-23 A	13-May-23 A	12-Aug-22	12-Aug-22	-274d
C-ECPRB-1590	Eastbound CPR Bridge is Ready for Traffic	0d		14-May-23 A			
Westbound CPR Bridge Widening		411d	21-Jan-22 A	14-Sep-23	02-Nov-21	03-Nov-22	-213d
Site Preparation		56d	15-Mar-22 A	03-Jun-22 A	02-Nov-21	18-Nov-21	-134d
C-WCPRB-1010	Install Falsedeck	1d	15-Mar-22 A	16-Mar-22 A	05-Nov-21	18-Nov-21	-79d
C-WCPRB-1000	Initiate Detour TAS - Line Painting, Barrier Install, Signage	4d	30-May-22 A	03-Jun-22 A	02-Nov-21	04-Nov-21	-144d
Removals		164d	21-Jan-22 A	15-Sep-22 A	18-Jan-22	24-Mar-22	-120d
C-WCPRB-1020	Anchor Blockout Bearing Removal	2d	21-Jan-22 A	24-Jan-22 A	18-Jan-22	20-Jan-22	-2d
C-WCPRB-1080	Deck Removal	32d	27-Jun-22 A	12-Aug-22 A	03-Feb-22	24-Feb-22	-116d
C-WCPRB-1060	Bridge Rail Dismantle	8d	27-Jun-22 A	08-Jul-22 A	27-Jan-22	02-Feb-22	-107d
C-WCPRB-1110	Expansion Joint Concrete Removal	11d	16-Aug-22 A	31-Aug-22 A	18-Mar-22	24-Mar-22	-109d
C-WCPRB-1090	Curtain Wall Removal	12d	25-Aug-22 A	13-Sep-22 A	25-Feb-22	10-Mar-22	-127d
C-WCPRB-1100	Approach Slab Concrete Removal	1d	15-Sep-22 A	15-Sep-22 A	11-Mar-22	17-Mar-22	-125d
Substructure		209d	23-Feb-22 A	20-Dec-22 A	21-Jan-22	29-Aug-22	-79d
C-WCPRB-1030	Pier Diaphragm Bearing Structure	1d	23-Feb-22 A	23-Feb-22 A	21-Jan-22	24-Jan-22	-21d
C-WCPRB-1040	Abutment Bearing Installation	1d	23-Feb-22 A	23-Feb-22 A	21-Jan-22	24-Jan-22	-21d
C-WCPRB-1230	Bearings - Welding/Grouting	8d	09-Dec-22 A	20-Dec-22 A	16-Aug-22	29-Aug-22	-79d
Superstructure		379d	23-Feb-22 A	30-Aug-23	25-Jan-22	12-Oct-22	-219d
Girder Erection		3d	23-Feb-22 A	28-Feb-22 A	25-Jan-22	26-Jan-22	-21d
C-WCPRB-1050	Girder Erection	3d	23-Feb-22 A	28-Feb-22 A	25-Jan-22	26-Jan-22	-21d
Diaphragm		43d	03-Oct-22 A	01-Dec-22 A	27-Jan-22	15-Aug-22	-76d
X-CPBD-1050	DELAY - BRIDGE OFFSET DIMENSIONS	14d	03-Oct-22 A	21-Oct-22 A			
C-WCPRB-1070	Diaphragm Extension - F/R/P	16d	24-Oct-22 A	14-Nov-22 A	27-Jan-22	09-Feb-22	-191d
C-WCPRB-1220	Cure Time	17d	15-Nov-22 A	01-Dec-22 A	02-Aug-22	15-Aug-22	-108d
Deck		143d	17-Jan-23 A	11-Aug-23	08-Apr-22	08-Jul-22	-270d
C-WCPRB-1340	Install Overhangs	4d	17-Jan-23 A	20-Jan-23 A			
C-WCPRB-1130	Form Interior Bays (Deck Extension)	76d	30-Jan-23 A	17-May-23 A	08-Apr-22	20-May-22	-245d
C-WCPRB-1350	Install Deck Edge & Soffit Formwork	8d	06-Feb-23 A	15-Feb-23 A			
X-DEL-2200	DELAY - Awaiting Answers on Deflection Calcs from Designer	19d	13-Feb-23 A	13-Mar-23 A			
X-DEL-2210	Drill & Install Dowels	47d	16-Feb-23 A	26-Apr-23 A			
C-WCPRB-1360	Deck Rebar Placement	10d	18-May-23 A	01-Jun-23 A			
C-WCPRB-1150	Deck Placement 1 - Pour	1d	05-Jun-23 A	05-Jun-23 A	27-May-22	27-May-22	-253d
C-WCPRB-1160	Initial Cure & Strip Bulkheads	5d	06-Jun-23 A	12-Jun-23 A	02-Jun-22	02-Jun-22	-254d
C-WCPRB-1180	Deck Placement 2 - Pour	1d	13-Jun-23 A	13-Jun-23 A	17-Jun-22	08-Jul-22	-230d
C-WCPRB-1170	Deck Cure Time	17d	14-Jun-23 A	30-Jun-23 A	03-Jun-22	16-Jun-22	-379d
C-WCPRB-1380	Form/Rebar/Pour Expansion Joints & Curtainwall	32d	26-Jun-23 A	11-Aug-23			
Barrier		32d	04-Jul-23 A	17-Aug-23	11-Jul-22	12-Aug-22	-251d
C-WCPRB-1190	Deck Barrier Form	7d	04-Jul-23 A	12-Jul-23 A	11-Jul-22	29-Jul-22	-235d
C-WCPRB-1390	Deck Barrier Rebar	4d	13-Jul-23 A	18-Jul-23 A			
C-WCPRB-1410	Close Forms & Anchor Bolts	10d	19-Jul-23 A	01-Aug-23 A			
C-WCPRB-1400	Pour Deck Barriers	1d	03-Aug-23 A	03-Aug-23 A			
C-WCPRB-1200	Deck Barrier Cure Time	14d	04-Aug-23 A	17-Aug-23	30-Jul-22	12-Aug-22	-370d
Transition Barrier		17d	07-Aug-23 A	30-Aug-23	21-Sep-22	12-Oct-22	-219d
C-WCPRB-1250	Transition Barrier - F/R/P	7d	07-Aug-23 A	16-Aug-23	21-Sep-22	12-Oct-22	-209d
C-WCPRB-1320	Transition Barrier - Cure Time	14d	17-Aug-23	30-Aug-23			
Asphalt		4d	31-Aug-23	06-Sep-23	13-Oct-22	18-Oct-22	-219d
C-WCPRB-1260	Waterproofing	3d	31-Aug-23	05-Sep-23	13-Oct-22	17-Oct-22	-219d
C-WCPRB-1270	Bridge Paving (2 Lifts - WB CPR Bridge)	1d	06-Sep-23	06-Sep-23	18-Oct-22	18-Oct-22	-219d
Finishing		24d	11-Aug-23	14-Sep-23	24-May-22	03-Nov-22	-213d
C-WCPRB-1140	Vertical Face of Soffit Finishing	10d	11-Aug-23	24-Aug-23	24-May-22	06-Jun-22	-303d
C-WCPRB-1210	Barrier Finishing	10d	31-Aug-23	14-Sep-23	02-Aug-22	15-Aug-22	-269d
C-WCPRB-1280	Line Painting	1d	07-Sep-23	07-Sep-23	19-Oct-22	19-Oct-22	-219d
C-WCPRB-1290	Bridge Light Install	5d	07-Sep-23	13-Sep-23	20-Oct-22	02-Nov-22	-213d
C-WCPRB-1300	Safety Audit and Inspection	1d	14-Sep-23	14-Sep-23	03-Nov-22	03-Nov-22	-213d
C-WCPRB-1310	Westbound CPR Bridge is Ready for Traffic	0d		14-Sep-23			
Main Street Bridge		591d	05-May-21 A	15-Sep-23	03-May-21	28-Jun-23	-54d
Site Preparation		6d	05-May-21 A	12-May-21 A	03-May-21	10-May-21	-2d

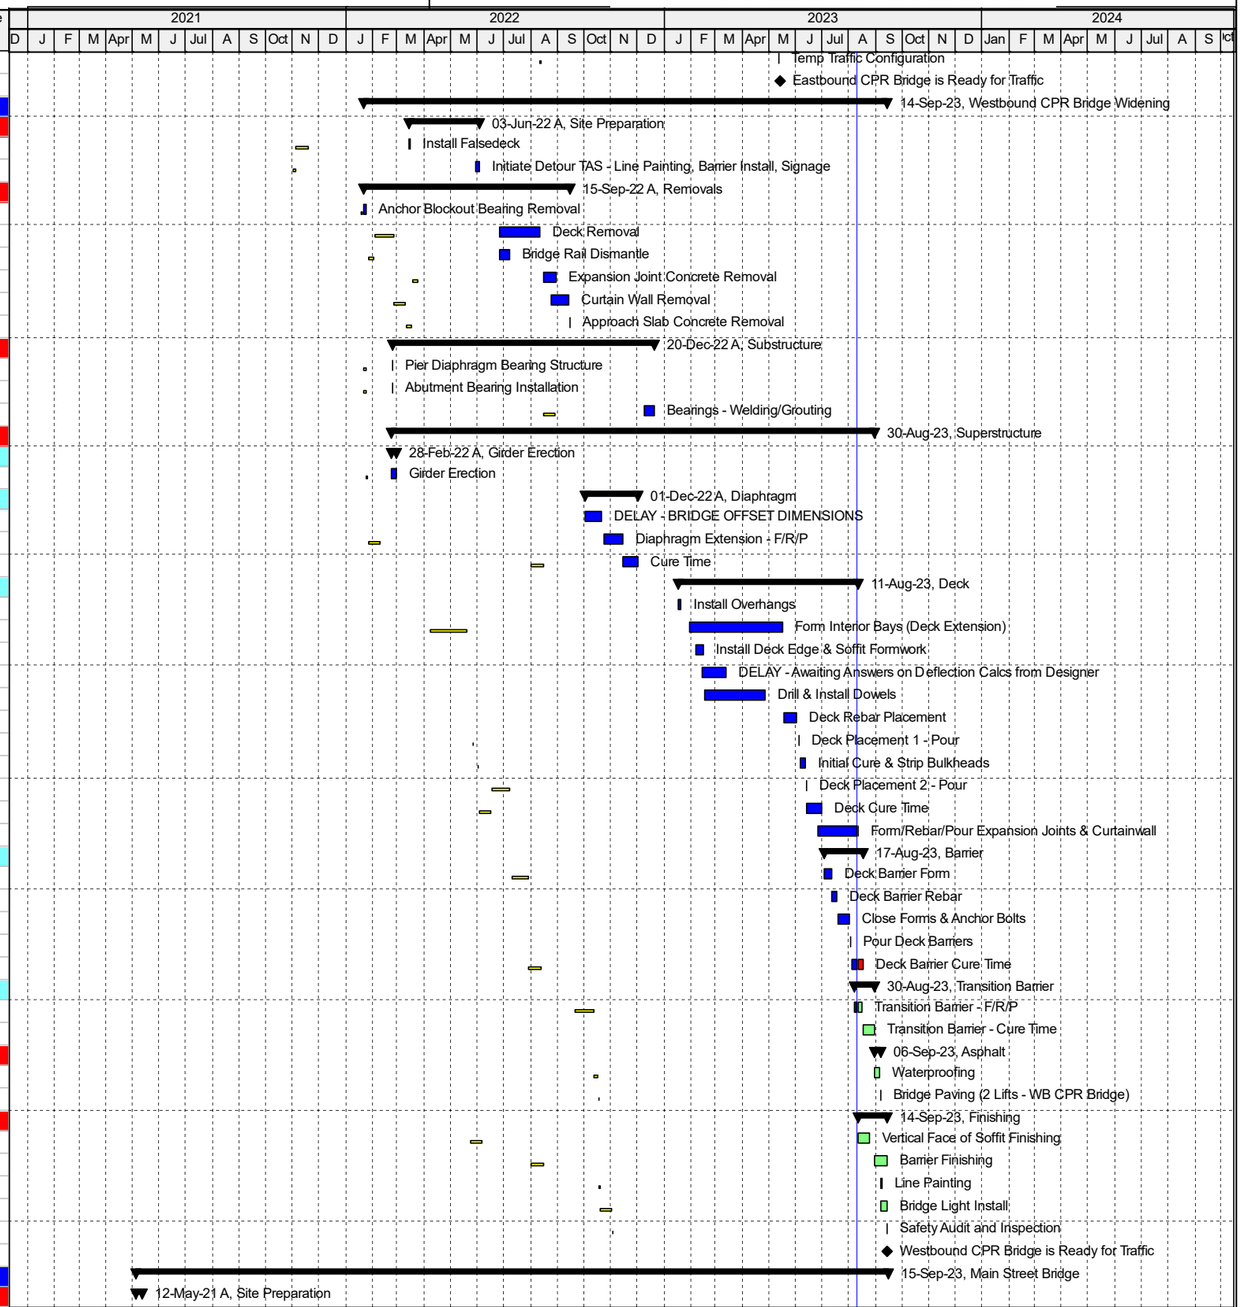

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-MSB-1000	Site Stripping and Pre-grading	6d	05-May-21 A	12-May-21 A	03-May-21	10-May-21	-2d
Foundations		37d	30-Jun-21 A	23-Aug-21 A	26-May-21	21-Jul-21	-22d
Abutment Piling		37d	30-Jun-21 A	23-Aug-21 A	26-May-21	21-Jul-21	-22d
C-MSB-1320	Abutment 2 Ground Improvments	4d	30-Jun-21 A	07-Jul-21 A			
C-MSB-1330	Abutment 1 Ground Improvements	5d	08-Jul-21 A	14-Jul-21 A			
C-MSB-1010	Abutment 2 Piling - 21 H Piles	5d	19-Jul-21 A	23-Jul-21 A	26-May-21	22-Jun-21	-22d
C-MSB-1020	Abutment 1 Piling - 21 H Piles	7d	13-Aug-21 A	23-Aug-21 A	23-Jun-21	21-Jul-21	-22d
Substructure (Including MSE)		134d	03-Aug-21 A	11-Feb-22 A	23-Jun-21	16-Dec-21	-38d
MSE Walls & Earthworks		43d	03-Aug-21 A	01-Oct-21 A	23-Jun-21	19-Aug-21	-30d
C-MSB-1030	Abutment 2 MSE Wall	21d	03-Aug-21 A	31-Aug-21 A	23-Jun-21	21-Jul-21	-28d
C-MSB-1040	Abutment 1 MSE Wall	19d	07-Sep-21 A	01-Oct-21 A	22-Jul-21	19-Aug-21	-30d
Abutment Seat		40d	07-Sep-21 A	02-Nov-21 A	12-Oct-21	09-Dec-21	27d
C-MSB-1070	Abutment Seat 2 w/ Plinth - F/R/P	20d	07-Sep-21 A	04-Oct-21 A	09-Nov-21	06-Dec-21	44d
C-MSB-1060	Abutment Seat 1 w/ Plinth - F/R/P	12d	08-Oct-21 A	26-Oct-21 A	12-Oct-21	08-Nov-21	9d
C-MSB-1090	Abutment Seat 2 - Cure & Stripping	9d	11-Oct-21 A	22-Oct-21 A	07-Dec-21	09-Dec-21	34d
C-MSB-1080	Abutment Seat 1 - Cure	7d	27-Oct-21 A	02-Nov-21 A	09-Nov-21	11-Nov-21	9d
Bearing Installation		1d	11-Feb-22 A	11-Feb-22 A	10-Dec-21	16-Dec-21	-57d
C-MSB-1100	Bearing Installation	1d	11-Feb-22 A	11-Feb-22 A	10-Dec-21	16-Dec-21	-57d
Superstructure		259d	14-Feb-22 A	01-Mar-23 A	17-Dec-21	12-Oct-22	-93d
Girder Erection		3d	14-Feb-22 A	16-Feb-22 A	17-Dec-21	04-Jan-22	-31d
C-MSB-G-1000	Girder Erection & Bracing (12)	3d	14-Feb-22 A	16-Feb-22 A	17-Dec-21	04-Jan-22	-31d
Deck		97d	09-Mar-22 A	27-Jul-22 A	02-Feb-22	30-Jun-22	-17d
C-MSB-DK-1000	Bridge Deck Hauch Calculation	13d	09-Mar-22 A	28-Mar-22 A			
C-MSB-DK-1010	Precast Deck Panel Installation	2d	04-Apr-22 A	06-Apr-22 A	02-Feb-22	02-Mar-22	-24d
C-MSB-DK-1020	Deck Formwork	22d	11-Apr-22 A	12-May-22 A	03-Mar-22	27-May-22	11d
C-MSB-DK-1030	Rebar Placement	20d	13-May-22 A	13-Jun-22 A			
C-MSB-DK-1040	Set Up Deck Screed, Dry Runs	3d	01-Jul-22 A	07-Jul-22 A			
C-MSB-DK-1050	Deck Placement 1 - Pour	0d	09-Jul-22 A	11-Jul-22 A	10-Jun-22	10-Jun-22	-19d
C-MSB-DK-1070	Demobilize Deck Screed	12d	11-Jul-22 A	27-Jul-22 A			
C-MSB-DK-1060	Deck Curing	14d	11-Jul-22 A	25-Jul-22 A	17-Jun-22	30-Jun-22	-24d
Deck Barriers		86d	24-Oct-22 A	01-Mar-23 A	31-Aug-22	12-Oct-22	-93d
C-MSB-DKB-1020	Form & Rebar - North Barrier	69d	24-Oct-22 A	03-Feb-23 A	31-Aug-22	21-Sep-22	-90d
C-MSB-DKB-1000	Form & Rebar - South Traffic Barrier	69d	24-Oct-22 A	03-Feb-23 A			
C-MSB-DKB-1010	Form & Rebar - South Pedestrian Barrier	69d	24-Oct-22 A	03-Feb-23 A			
C-MSB-DKB-1040	Barrier Heating & Hoarding	4d	06-Feb-23 A	10-Feb-23 A			
C-MSB-DKB-1050	Pour Barriers	1d	10-Feb-23 A	10-Feb-23 A			
C-MSB-DKB-1030	Barrier Curing	14d	11-Feb-23 A	24-Feb-23 A	22-Sep-22	12-Oct-22	-135d
C-MSB-DKB-1060	Strip Barriers	3d	27-Feb-23 A	01-Mar-23 A			
Backwalls/Wingwalls		62d	06-Jul-22 A	03-Oct-22 A	04-Jul-22	18-Aug-22	-31d
BW/WW #1 - West		55d	06-Jul-22 A	22-Sep-22 A	04-Jul-22	27-Jul-22	-39d
C-MSB-WW-W-1000	Stand Forms	12d	06-Jul-22 A	22-Jul-22 A			
C-MSB-WW-W-1010	Rebar	10d	11-Jul-22 A	25-Jul-22 A			
C-MSB-WW-W-1020	Close Forms, QA/QC Signoff	3d	22-Jul-22 A	27-Jul-22 A			
C-MSB-WW-W-1040	Abutment Wingwall 1 - Cure & Stripping	14d	28-Jul-22 A	11-Aug-22 A	25-Jul-22	27-Jul-22	-14d
C-MSB-WW-W-1030	Pour Abutment Diaphragm/Wingwall #1	1d	28-Jul-22 A	28-Jul-22 A	04-Jul-22	22-Jul-22	-4d
C-MSB-WW-W-1050	Wingwall Patching and Finishing	3d	20-Sep-22 A	22-Sep-22 A			
BW/WW #2 - East		29d	23-Aug-22 A	03-Oct-22 A	25-Jul-22	18-Aug-22	-31d
C-MSB-WW-E-1000	Stand Forms	5d	23-Aug-22 A	29-Aug-22 A			
C-MSB-WW-E-1010	Rebar	1d	31-Aug-22 A	01-Sep-22 A			
C-MSB-WW-E-1020	Close Forms, QA/QC Signoff	2d	02-Sep-22 A	06-Sep-22 A			
C-MSB-WW-E-1030	Pour Abutment Diaphragm/Wingwall #2	1d	07-Sep-22 A	07-Sep-22 A	25-Jul-22	15-Aug-22	-16d
C-MSB-WW-E-1040	Abutment Wingwall 2 - Cure & Stripping	16d	08-Sep-22 A	23-Sep-22 A	16-Aug-22	18-Aug-22	-36d
C-MSB-WW-E-1050	Wingwall Patching and Finishing	3d	29-Sep-22 A	03-Oct-22 A			
Approach Slabs		172d	04-Oct-22 A	14-Jun-23 A	31-Aug-22	13-Sep-22	-186d
C-MSB-AS-1000	Backfill to U/S of Approach Slab (Both Sides Simultaneously)	6d	04-Oct-22 A	12-Oct-22 A			
C-MSB-AS-W-1020	Approach Slab Final Grading (E&W)	3d	09-May-23 A	12-May-23 A			
Approach Slab #2 - East		17d	16-May-23 A	08-Jun-23 A			
C-MSB-AS-E-1030	Approach Slab Rebar (East)	3d	16-May-23 A	18-May-23 A			

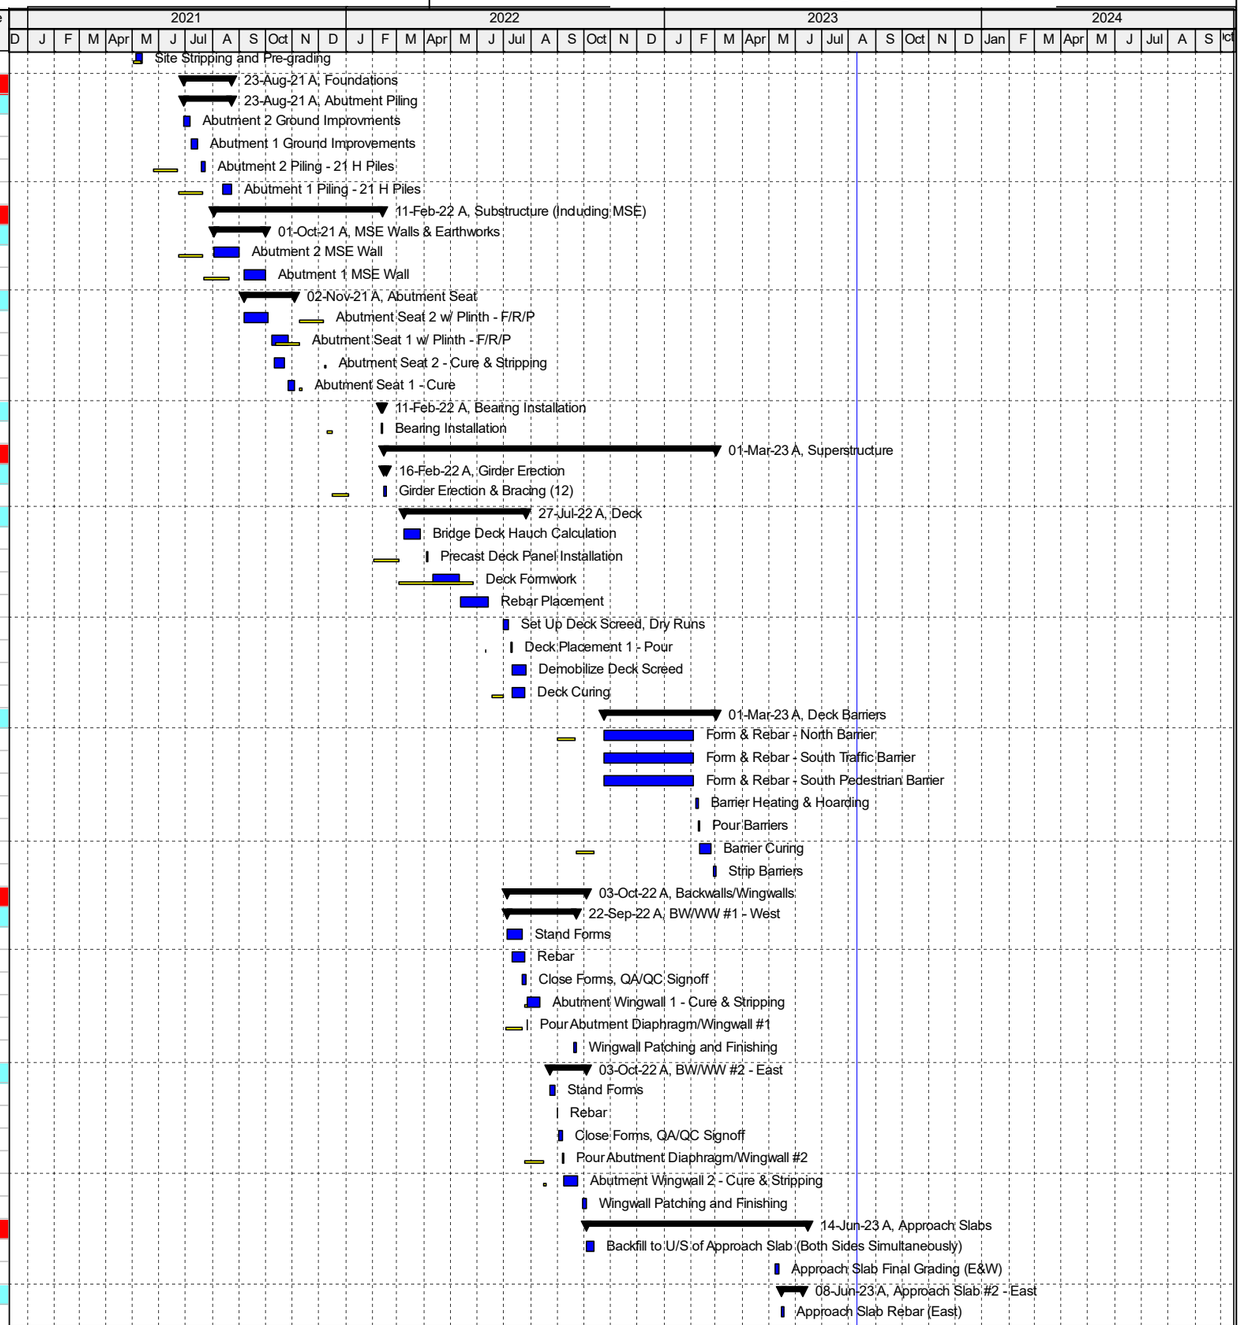

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-MSB-AS-E-1000	Form Approach Slab (East)	3d	19-May-23 A	24-May-23 A			
C-MSB-AS-E-1020	Pour Approach Slab	1d	25-May-23 A	25-May-23 A			
C-MSB-AS-E-1010	Approach Slab Cure Time	14d	26-May-23 A	08-Jun-23 A			
Approach Slab #1 - West		19d	18-May-23 A	14-Jun-23 A	31-Aug-22	13-Sep-22	-186d
C-MSB-AS-W-1030	Approach Slab Rebar (East)	5d	18-May-23 A	26-May-23 A			
C-MSB-AS-W-1000	Form Approach Slab (West)	3d	26-May-23 A	30-May-23 A			
C-MSB-AS-W-1040	Pour Approach Slab (West)	1d	31-May-23 A	31-May-23 A			
C-MSB-AS-W-1010	Approach Slab Cure Time (West)	14d	01-Jun-23 A	14-Jun-23 A	31-Aug-22	13-Sep-22	-274d
Transition Barriers		22d	05-Jun-23 A	06-Jul-23 A			
C-MSB-TB-1030	East Approach Slab Barriers	6d	05-Jun-23 A	13-Jun-23 A			
C-MSB-TB-1040	West Approach Slab Barriers	6d	05-Jun-23 A	13-Jun-23 A			
C-MSB-TB-1000	F/R/P West Transition Barriers	13d	14-Jun-23 A	30-Jun-23 A			
C-MSB-TB-1010	F/R/P East Transition Barriers	13d	14-Jun-23 A	30-Jun-23 A			
C-MSB-TB-1020	Transition Barriers Cure Time	7d	30-Jun-23 A	06-Jul-23 A			
Paving		28d	04-Jul-23 A	13-Aug-23	16-Jun-23	23-Jun-23	-33d
C-MSB-1280	Waterproofing	4d	04-Jul-23 A	07-Jul-23 A	16-Jun-23	21-Jun-23	-11d
C-MSB-1290	Bridge Paving (2 Lifts - Main Street Bridge)	2d	12-Aug-23*	13-Aug-23	22-Jun-23	23-Jun-23	-51d
MSE Wall Coping		100d	13-Feb-23 A	06-Jul-23 A	20-Aug-21	16-Jun-22	-261d
C-MSB-1050	Form MSE Wall Coping	24d	13-Feb-23 A	17-Mar-23 A	20-Aug-21	02-Sep-21	-382d
C-MSB-1110	Rebar	10d	15-Mar-23 A	28-Mar-23 A			
C-MSB-1120	Pour	2d	04-May-23 A	05-May-23 A	05-Jan-22	01-Feb-22	-313d
C-MSB-1130	Curing	14d	06-May-23 A	19-May-23 A			
C-MSB-1140	Strip Forms	24d	23-May-23 A	23-Jun-23 A			
C-MSB-1150	Sack-Rub & Finish	5d	26-Jun-23 A	03-Jul-23 A			
C-MSB-1160	Railing Install	3d	03-Jul-23 A	06-Jul-23 A	16-Jun-22	16-Jun-22	-261d
Finishing		144d	20-Feb-23 A	15-Sep-23	14-Sep-22	28-Jun-23	-54d
C-MSB-1460	Bridge Rail Installation	8d	20-Feb-23 A	02-Mar-23 A			
C-MSB-1250	Sidewalk Concrete - F/R/P	8d	10-Jul-23 A	19-Jul-23 A	14-Sep-22	27-Sep-22	-200d
C-MSB-1300	Line Painting. Signs, etc.	2d	14-Aug-23	15-Aug-23	26-Jun-23	27-Jun-23	-33d
C-MSB-1310	Safety Audit and Inspection	1d	16-Aug-23	16-Aug-23	28-Jun-23	28-Jun-23	-33d
C-MSB-1470	Road Tie-In Barriers (x4)	10d	16-Aug-23	29-Aug-23			
C-MSB-1480	Curing (Tie-in Barriers)	14d	30-Aug-23	12-Sep-23			
C-MSB-1490	Dry-Finishing Barriers	3d	13-Sep-23	15-Sep-23			
C-MSB-1450	Main Street Bridge is Ready for Traffic	0d		15-Sep-23			
QEII Interchange Bridge		530d	17-Aug-21 A	29-Sep-23	15-Jun-21	26-Jul-23	-45d
Site Preparation		64d	17-Aug-21 A	16-Nov-21 A	15-Jun-21	12-Oct-21	-25d
C-QE2IB-1020	Utility Relocations at Abutment 2	45d	17-Aug-21 A	20-Oct-21 A	09-Aug-21	26-Aug-21	-37d
C-QE2IB-1030	Topsoil Stripping - Abutment 2	2d	18-Oct-21 A	20-Oct-21 A	27-Aug-21	10-Sep-21	-26d
C-QE2IB-1000	Construct QEII Crossover Detours	14d	30-Oct-21 A	16-Nov-21 A	15-Jun-21	28-Jun-21	-116d
C-QE2IB-1060	Topsoil Stripping - Abutment 1	2d	11-Nov-21 A	12-Nov-21 A	08-Oct-21	12-Oct-21	-23d
Earthworks		186d	21-Oct-21 A	19-Jul-22 A	13-Sep-21	06-Jun-22	-29d
C-QE2IB-1050	Abutment 2 Backfill to Underside	16d	21-Oct-21 A	11-Nov-21 A	13-Sep-21	24-Sep-21	-33d
C-QE2IB-1080	Abutment 1 Backfill to Underside	12d	12-Nov-21 A	29-Nov-21 A	13-Oct-21	26-Oct-21	-24d
C-QE2IB-1230	MSE Wall	35d	30-May-22 A	19-Jul-22 A	16-May-22	06-Jun-22	-29d
Foundations		38d	28-Oct-21 A	20-Dec-21 A	15-Jun-21	21-Dec-21	1d
Abutment Piling		26d	15-Nov-21 A	20-Dec-21 A	27-Oct-21	21-Dec-21	1d
C-QE2IB-1110	Abutment 2 Piling - 24 H Piles	6d	15-Nov-21 A	22-Nov-21 A	24-Nov-21	21-Dec-21	21d
C-QE2IB-1090	Abutment 1 Piling - 24 H Piles	14d	01-Dec-21 A	20-Dec-21 A	27-Oct-21	23-Nov-21	-19d
Pier Footings		27d	28-Oct-21 A	03-Dec-21 A	15-Jun-21	01-Nov-21	-24d
C-QE2IB-1040	Spread Footing Excavation and Compaction	8d	28-Oct-21 A	05-Nov-21 A	13-Sep-21	17-Sep-21	-41d
C-QE2IB-1010	Construct Crossovers	8d	28-Oct-21 A	05-Nov-21 A	15-Jun-21	28-Jun-21	-108d
C-QE2IB-1410	F/R/P Mudslab	1d	10-Nov-21 A	10-Nov-21 A	20-Sep-21	24-Sep-21	-39d
C-QE2IB-1070	Pier Spread Footing F/R/P	10d	15-Nov-21 A	26-Nov-21 A	27-Sep-21	25-Oct-21	-24d
C-QE2IB-1420	Concrete Curing - Winter Conditions	7d	27-Nov-21 A	03-Dec-21 A	26-Oct-21	01-Nov-21	-32d
Substructure		81d	20-Dec-21 A	19-Apr-22 A	02-Nov-21	10-Mar-22	-26d
Abutment Seat		63d	20-Dec-21 A	22-Mar-22 A	04-Jan-22	10-Mar-22	-8d
Abutment 2 (East)		41d	20-Dec-21 A	17-Feb-22 A	01-Feb-22	04-Mar-22	10d

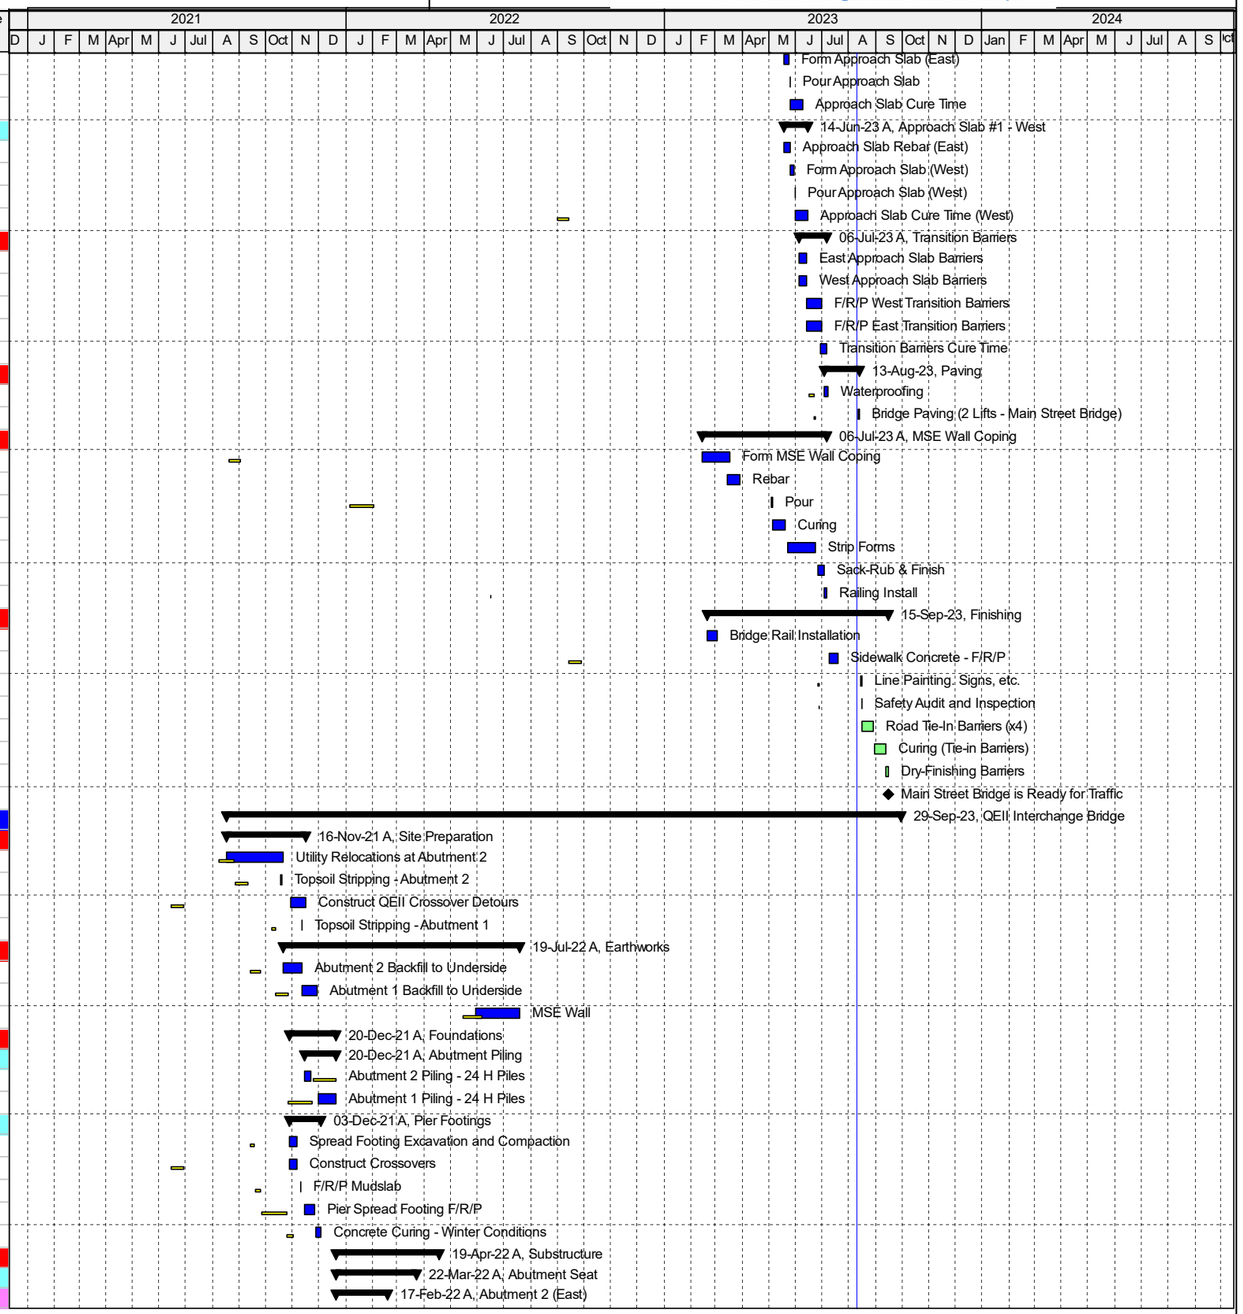

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline

Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-QE2IB-1140	Abutment Seat 2 w/ Plinth - F/R/P	34d	20-Dec-21 A	08-Feb-22 A	01-Feb-22	01-Mar-22	14d
C-QE2IB-1170	Cure Abutment	9d	09-Feb-22 A	17-Feb-22 A	02-Mar-22	04-Mar-22	15d
Abutment 1 (West)		19d	24-Feb-22 A	22-Mar-22 A	04-Jan-22	10-Mar-22	-8d
C-QE2IB-1120	Stand Forms	4d	24-Feb-22 A	01-Mar-22 A	04-Jan-22	31-Jan-22	-20d
C-QE2IB-1160	Rebar	5d	02-Mar-22 A	08-Mar-22 A	25-Feb-22	10-Mar-22	2d
C-QE2IB-1460	Close Forms, QC Signoff	4d	09-Mar-22 A	14-Mar-22 A			
C-QE2IB-1470	Pour Abutment (incl. Plinths)	1d	15-Mar-22 A	15-Mar-22 A			
C-QE2IB-1150	Cure Abutment	7d	16-Mar-22 A	22-Mar-22 A	01-Feb-22	03-Feb-22	-47d
Pier		69d	10-Jan-22 A	19-Apr-22 A	02-Nov-21	24-Feb-22	-36d
Pier Columns		52d	10-Jan-22 A	23-Mar-22 A	02-Nov-21	20-Jan-22	-43d
C-QE2IB-1100	Pier Columns - F/R/P	49d	10-Jan-22 A	18-Mar-22 A	02-Nov-21	13-Jan-22	-45d
C-QE2IB-1430	Pier Column Concrete Final Cure	5d	19-Mar-22 A	23-Mar-22 A	14-Jan-22	20-Jan-22	-62d
Pier Cap		20d	21-Mar-22 A	19-Apr-22 A	21-Jan-22	24-Feb-22	-36d
C-QE2IB-1480	Pier Cap Access/Falsework Install	1d	21-Mar-22 A	22-Mar-22 A			
C-QE2IB-1130	Stand Forms	2d	30-Mar-22 A	01-Apr-22 A	21-Jan-22	17-Feb-22	-29d
C-QE2IB-1490	Pier Cap Rebar	2d	06-Apr-22 A	08-Apr-22 A			
C-QE2IB-1500	Close Forms/QC Signoff	3d	08-Apr-22 A	13-Apr-22 A			
C-QE2IB-1440	Cure Pier Cap	5d	14-Apr-22 A	19-Apr-22 A	18-Feb-22	24-Feb-22	-53d
C-QE2IB-1510	Pour Pier Cap	0d	14-Apr-22 A	14-Apr-22 A			
Superstructure		348d	25-Apr-22 A	15-Sep-23	17-Mar-22	03-Jan-23	-177d
Girder Erection		39d	25-Apr-22 A	20-Jun-22 A	17-Mar-22	13-Apr-22	-45d
C-QE2IB-1190	Install Girders (26)	10d	25-Apr-22 A	06-May-22 A	17-Mar-22	13-Apr-22	-16d
C-QE2IB-1520	Install Falsedeck	15d	25-Apr-22 A	13-May-22 A			
C-QE2IB-1450	Install Steel Diaphragm Bracing	24d	16-May-22 A	20-Jun-22 A			
Diaphragms		137d	04-Jul-22 A	23-Jan-23 A	14-Apr-22	05-May-22	-176d
C-QE2IB-1210	Form Pier Diaphragm	49d	04-Jul-22 A	13-Sep-22 A	14-Apr-22	05-May-22	-88d
Abutment 1 (West)		75d	04-Jul-22 A	19-Oct-22 A	14-Apr-22	05-May-22	-114d
C-QE2IB-1200	Form West Abut Diaphragm	9d	04-Jul-22 A	15-Jul-22 A	14-Apr-22	05-May-22	-48d
C-QE2IB-1730	Rebar West Abut Diaphragm	13d	01-Aug-22 A	19-Aug-22 A			
C-QE2IB-1740	Close West Abut Diaphragm	28d	09-Sep-22 A	19-Oct-22 A			
Abutment 2 (East)		84d	19-Sep-22 A	23-Jan-23 A			
C-QE2IB-1810	Form East Abut Diaphragm	5d	19-Sep-22 A	23-Sep-22 A			
C-QE2IB-1820	Rebar East Abut Diaphragm	14d	26-Sep-22 A	14-Oct-22 A			
C-QE2IB-1830	Close East Abut Diaphragm	8d	28-Nov-22 A	07-Dec-22 A			
C-QE2IB-1890	Pour East Abutment Diaphragm	1d	23-Jan-23 A	23-Jan-23 A			
Deck		289d	16-May-22 A	13-Jul-23 A	06-May-22	13-Sep-22	-206d
C-QE2IB-1220	Form Deck	67d	16-May-22 A	20-Aug-22 A	06-May-22	16-Aug-22	-3d
C-QE2IB-1620	Survey, Haunch Calculations	2d	02-Jun-22 A	06-Jun-22 A			
C-QE2IB-1530	Deck Rebar	37d	14-Jul-22 A	07-Sep-22 A			
C-QE2IB-1800	Install Deck Drains	1d	20-Jul-22 A	20-Jul-22 A			
C-QE2IB-1540	Setup Deck Screed & Dry Runs	3d	02-Sep-22 A	08-Sep-22 A			
C-QE2IB-1240	Deck Placement 1.1 East Pour	1d	09-Sep-22 A	09-Sep-22 A	17-Aug-22	17-Aug-22	-16d
C-QE2IB-1700	Deck Placement 1.2 West Pour	1d	12-Sep-22 A	12-Sep-22 A			
C-QE2IB-1710	Deck Placement 2 Pier Diaphragm Pour	1d	14-Sep-22 A	14-Sep-22 A			
X-DEL-004-1000	Awaiting Approval of Pour Procedure	22d	06-Feb-23 A	09-Mar-23 A			
C-QE2IB-1990	Deck Placement 3 (East Deck End)	1d	21-Mar-23 A	21-Mar-23 A			
C-QE2IB-2070	Deck Curing	14d	22-Mar-23 A	04-Apr-23 A			
C-QE2IB-1250	Deck Placement 4 (West Deck End)	1d	03-May-23 A	03-May-23 A	23-Aug-22	23-Aug-22	-171d
C-QE2IB-1270	Deck Curing	17d	04-May-23 A	20-May-23 A	24-Aug-22	13-Sep-22	-249d
Deck Barriers		66d	11-Apr-23 A	13-Jul-23 A			
East Span		49d	11-Apr-23 A	19-Jun-23 A			
C-QE2IB-1840	Form Curb/Barrier (East Span)	19d	11-Apr-23 A	05-May-23 A			
C-QE2IB-2010	Barrier Rebar (East Span)	10d	08-May-23 A	19-May-23 A			
C-QE2IB-2030	Close Barrier Forms (East Span)	9d	29-May-23 A	09-Jun-23 A			
C-QE2IB-2020	Pour Barriers (East Span)	1d	09-Jun-23 A	09-Jun-23 A			
C-QE2IB-1850	Curing Barrier (East Span)	10d	10-Jun-23 A	19-Jun-23 A			
West Span		43d	12-May-23 A	13-Jul-23 A			

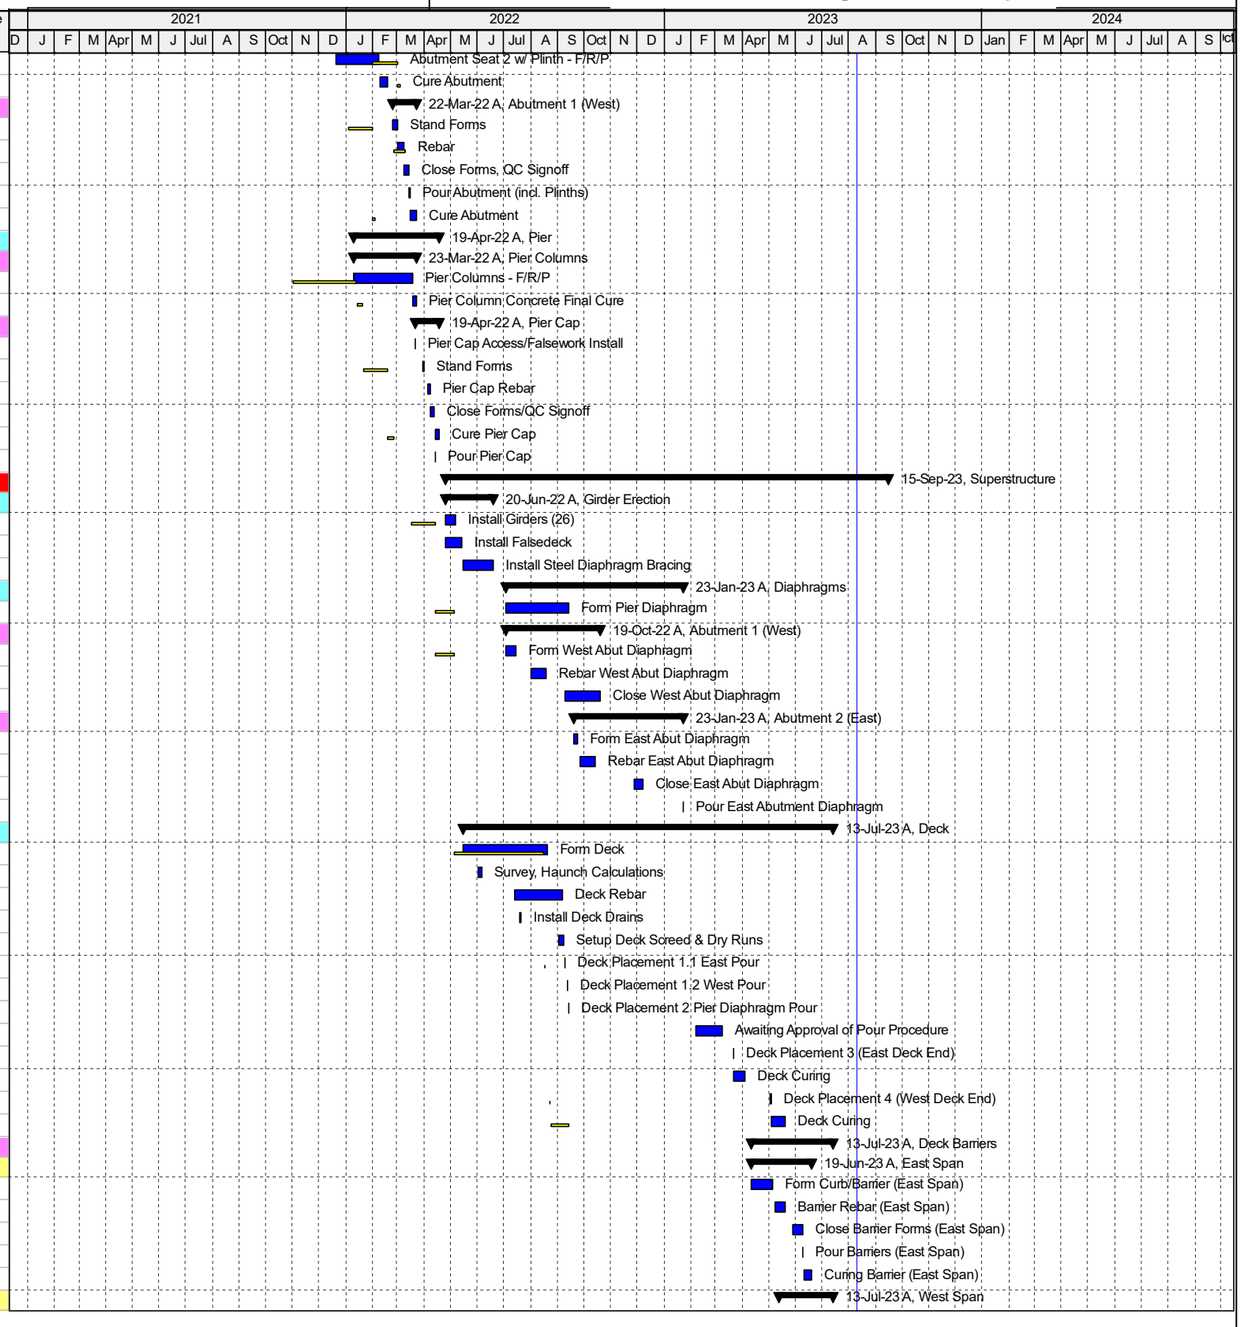

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE — COMMUNITY & OPPORTUNITY

EllisDon — We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-QE2IB-2080	Form Curb/Barrier (West Span)	6d	12-May-23 A	19-May-23 A			
C-QE2IB-2090	Barrier Rebar (West Span)	6d	15-May-23 A	23-May-23 A			
C-QE2IB-2100	Close Barrier Forms (West Span)	8d	09-Jun-23 A	20-Jun-23 A			
C-QE2IB-2110	Pour Barriers (West Span)	1d	22-Jun-23 A	22-Jun-23 A			
C-QE2IB-2120	Curing Barrier (West Span)	14d	23-Jun-23 A	13-Jul-23 A			
Abutment Wingwall		150d	11-Oct-22 A	18-May-23 A	24-Aug-22	11-Oct-22	-149d
Abutment 1 (West)		150d	11-Oct-22 A	18-May-23 A	24-Aug-22	19-Sep-22	-164d
C-QE2IB-1260	Form West Wingwalls	5d	11-Oct-22 A	17-Oct-22 A	24-Aug-22	14-Sep-22	-22d
C-QE2IB-1560	Rebar	5d	11-Oct-22 A	17-Oct-22 A			
C-QE2IB-1570	Close Forms, QC Signoff	4d	18-Oct-22 A	21-Oct-22 A			
C-QE2IB-1580	Pour West Wingwalls	1d	24-Oct-22 A	24-Oct-22 A			
C-QE2IB-1290	Cure West Wingwalls	17d	25-Oct-22 A	10-Nov-22 A	15-Sep-22	19-Sep-22	-52d
C-QE2IB-1760	Formwork Stripping	1d	10-Nov-22 A	10-Nov-22 A			
C-QE2IB-1750	West Wingwall Patching & Finishing	5d	12-May-23 A	18-May-23 A			
Abutment 2 (East)		121d	21-Nov-22 A	18-May-23 A	15-Sep-22	11-Oct-22	-149d
C-QE2IB-1280	Form East Wingwalls	10d	21-Nov-22 A	02-Dec-22 A	15-Sep-22	05-Oct-22	-41d
C-QE2IB-1590	Rebar	4d	01-Dec-22 A	06-Dec-22 A			
C-QE2IB-1600	Close Forms, QC Signoff	11d	07-Dec-22 A	21-Dec-22 A			
C-QE2IB-1790	Heating & Hoarding & Cleaning	16d	22-Dec-22 A	20-Jan-23 A			
C-QE2IB-1610	Pour East Wingwalls	1d	23-Jan-23 A	23-Jan-23 A			
C-QE2IB-1300	Cure East Wingwalls	16d	24-Jan-23 A	09-Feb-23 A	06-Oct-22	11-Oct-22	-120d
C-QE2IB-1770	Formwork Stripping	8d	04-Apr-23 A	14-Apr-23 A			
C-QE2IB-1780	East Wingwall Patching & Finishing	5d	12-May-23 A	18-May-23 A			
Approach Slabs		50d	23-May-23 A	01-Aug-23 A	12-Oct-22	22-Nov-22	-170d
West Approach		50d	23-May-23 A	01-Aug-23 A	12-Oct-22	22-Nov-22	-170d
C-QE2IB-1310	Backfill West Approach (QEII Bridge)	10d	23-May-23 A	05-Jun-23 A	12-Oct-22	08-Nov-22	-35d
C-QE2IB-1630	Rebar Sleeper Slab	5d	23-Jun-23 A	29-Jun-23 A			
C-QE2IB-1640	Form Sleeper Slab	4d	30-Jun-23 A	07-Jul-23 A			
C-QE2IB-1650	Pour Sleeper Slab	1d	07-Jul-23 A	07-Jul-23 A			
C-QE2IB-1660	Cure Sleeper Slab	3d	08-Jul-23 A	10-Jul-23 A			
C-QE2IB-2050	Gravel Backfill	1d	11-Jul-23 A	11-Jul-23 A			
C-QE2IB-1670	Form Approach Slab	2d	12-Jul-23 A	13-Jul-23 A			
C-QE2IB-1680	Rebar Approach Slab	2d	14-Jul-23 A	17-Jul-23 A			
C-QE2IB-1690	Pour Approach Slab	1d	18-Jul-23 A	18-Jul-23 A			
C-QE2IB-1330	Cure Approach Slab	14d	19-Jul-23 A	01-Aug-23 A	09-Nov-22	22-Nov-22	-252d
East Approach		46d	23-May-23 A	26-Jul-23 A			
C-QE2IB-1900	Backfill East Approach (QEII Bridge)	10d	23-May-23 A	05-Jun-23 A			
C-QE2IB-1910	Rebar Sleeper Slab	6d	16-Jun-23 A	23-Jun-23 A			
C-QE2IB-1920	Form Sleeper Slab	5d	23-Jun-23 A	29-Jun-23 A			
C-QE2IB-1930	Pour Sleeper Slab	1d	30-Jun-23 A	30-Jun-23 A			
C-QE2IB-1950	Cure Sleeper Slab	3d	01-Jul-23 A	03-Jul-23 A			
C-QE2IB-2060	Gravel Backfill	4d	04-Jul-23 A	07-Jul-23 A			
C-QE2IB-1940	Form Approach Slab	1d	10-Jul-23 A	10-Jul-23 A			
C-QE2IB-1960	Rebar Approach Slab	1d	11-Jul-23 A	11-Jul-23 A			
C-QE2IB-1970	Pour Approach Slab	1d	12-Jul-23 A	12-Jul-23 A			
C-QE2IB-1980	Cure Approach Slab	14d	13-Jul-23 A	26-Jul-23 A			
Barriers		43d	17-Jul-23 A	15-Sep-23	09-Nov-22	03-Jan-23	-177d
West Barrier		14d	24-Jul-23 A	11-Aug-23	09-Nov-22	03-Jan-23	-153d
C-QE2IB-1320	Form West Transition Barriers	4d	24-Jul-23 A	27-Jul-23 A	09-Nov-22	20-Dec-22	-147d
C-QE2IB-1720	Pour West Barriers	1d	28-Jul-23 A	28-Jul-23 A			
C-QE2IB-1340	Cure Barriers	14d	29-Jul-23 A	11-Aug-23	21-Dec-22	03-Jan-23	-220d
East Barrier		15d	17-Jul-23 A	04-Aug-23 A			
C-QE2IB-1880	Form East Transition Barriers	4d	17-Jul-23 A	20-Jul-23 A			
C-QE2IB-1860	Pour East Barriers	1d	21-Jul-23 A	21-Jul-23 A			
C-QE2IB-1870	Cure Barriers	14d	22-Jul-23 A	04-Aug-23 A			
Roadway Tie-In barriers		24d	14-Aug-23	15-Sep-23			
C-QE2IB-2000	F/R/P Transition Tie-In to Roadway Barriers (x4)	10d	14-Aug-23*	25-Aug-23			

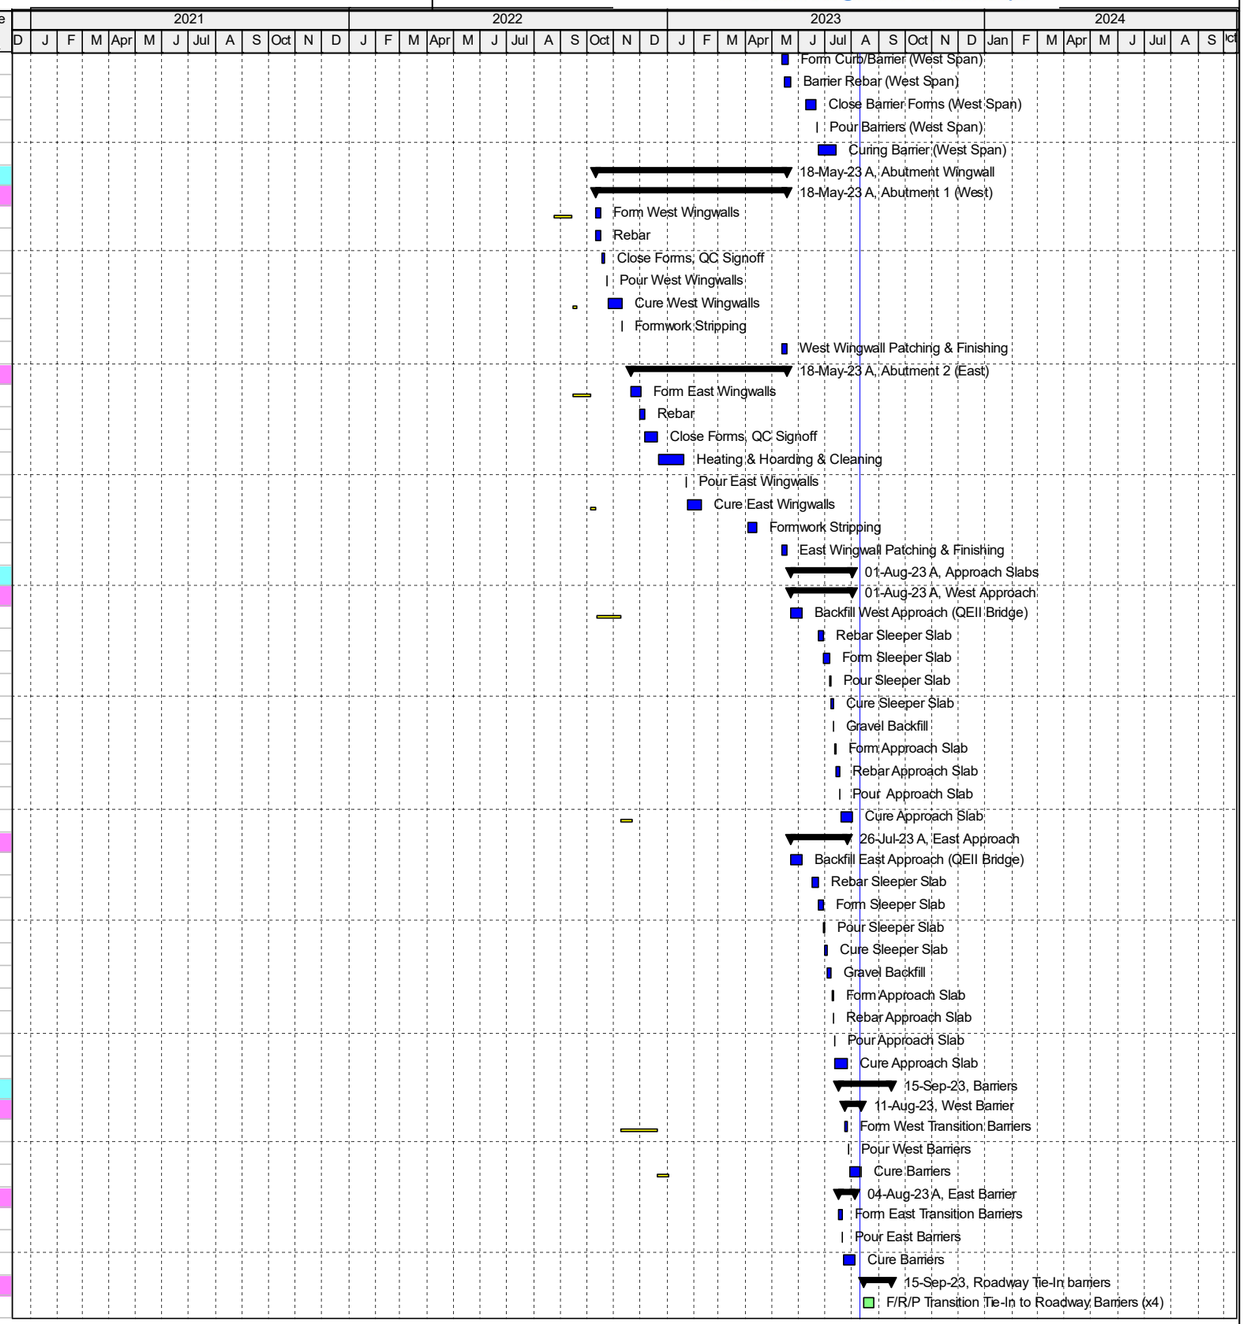

Remaining Level of Effort · Actual Work · Critical Remaining Work · Critical M/S · Project Baseline
Actual Level of Effort · Remaining Work · Milestone · Summary · Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-QE2IB-2040	Tie-In Barriers Cure Time	14d	26-Aug-23	08-Sep-23			
C-QE2IB-2130	Dry-Finishing	5d	11-Sep-23	15-Sep-23			
Paving		33d	26-Jul-23 A	12-Sep-23	09-Jun-23	04-Jul-23	-48d
C-QE2IB-1550	Deck Inspection & Repair	6d	26-Jul-23 A	02-Aug-23 A			
C-QE2IB-1360	Waterproofing	15d	03-Aug-23 A	24-Aug-23	09-Jun-23	15-Jun-23	-48d
C-QE2IB-1350	Sidewalk & Median Concrete Overlay - F/R/P	10d	25-Aug-23	08-Sep-23	16-Jun-23	29-Jun-23	-48d
C-QE2IB-1370	Bridge Paving (2 Lifts - QEII Bridge)	2d	11-Sep-23	12-Sep-23	30-Jun-23	04-Jul-23	-48d
East Retaining Wall		38d	03-Aug-23 A	27-Sep-23			
C-QE2IB-ERW-1000	Form Coping	15d	03-Aug-23 A	24-Aug-23			
C-QE2IB-ERW-1070	Install Anchor Bolts	15d	03-Aug-23 A	24-Aug-23			
C-QE2IB-ERW-1010	Rebar	5d	25-Aug-23	31-Aug-23			
C-QE2IB-ERW-1020	Pour Coping	1d	01-Sep-23*	01-Sep-23			
C-QE2IB-ERW-1030	Cure	14d	02-Sep-23	15-Sep-23			
C-QE2IB-ERW-1040	Stripping	3d	18-Sep-23	20-Sep-23			
C-QE2IB-ERW-1050	Sack-Rub & Finish Coping	5d	21-Sep-23	27-Sep-23			
C-QE2IB-ERW-1060	Railing Install	5d	21-Sep-23	27-Sep-23			
Pier Finishes		15d	08-Sep-23	28-Sep-23			
C-QE2IB-PF-1000	Sack-Rub & Finishing Pier	15d	08-Sep-23	28-Sep-23			
Finishing		13d	13-Sep-23	29-Sep-23	05-Jul-23	26-Jul-23	-45d
C-QE2IB-1380	Line Painting, Signs, etc.	2d	13-Sep-23	14-Sep-23	05-Jul-23	25-Jul-23	-35d
C-QE2IB-1390	Approach and Bridge Rail Installation	2d	13-Sep-23	14-Sep-23	05-Jul-23	25-Jul-23	-35d
C-MFW-QEII-SB-1020	Underpass Lighting Installation	5d	22-Sep-23	28-Sep-23			
C-QE2IB-1400	Internal Bridge Inspection	1d	29-Sep-23	29-Sep-23	26-Jul-23	26-Jul-23	-45d
Earthworks/Roadways		174d	12-Apr-21 A	16-Dec-21 A	12-Apr-21	28-Sep-21	-56d
Nose Creek Re-Alignment		174d	12-Apr-21 A	16-Dec-21 A	12-Apr-21	28-Sep-21	-56d
BF Culverts		127d	12-Apr-21 A	12-Oct-21 A	12-Apr-21	26-Aug-21	-31d
C-NCR-1000	Mowing HRIA Affected Lands	3d	12-Apr-21 A	14-Apr-21 A	12-Apr-21	14-Apr-21	0d
C-NCR-1310	Bulk Excavation	9d	10-May-21 A	21-May-21 A			
C-NCR-1320	Base Gravel & Preshape Bedding Placement	8d	04-Jun-21 A	16-Jun-21 A			
C-NCR-1050	Culvert Installation & Assembly	35d	11-Jun-21 A	31-Jul-21 A	30-Jun-21	28-Jul-21	-2d
C-NCR-1070	Culvert Backfill & Clay Plugs	26d	21-Jul-21 A	26-Aug-21 A	25-Aug-21	26-Aug-21	0d
C-NCR-1330	Cutoff Walls & Shoulders	27d	02-Sep-21 A	12-Oct-21 A			
Channel Construction		173d	13-Apr-21 A	16-Dec-21 A	13-Apr-21	24-Aug-21	-80d
C-NCR-1010	Topsoil Stripping (HRIA Cleared Areas First)	24d	13-Apr-21 A	17-May-21 A	13-Apr-21	17-May-21	1d
C-NCR-1020	Bulk Excavation (Including Pools and Earthen Plugs) - (HRIA Cleared Areas Fir	12d	18-May-21 A	04-Jun-21 A	18-May-21	29-Jun-21	18d
C-NCR-1060	Bulk Excavation (Including Pools and Earthen Plugs) - (HRIA Cleared Areas Fir	46d	11-Aug-21 A	15-Oct-21 A	29-Jul-21	24-Aug-21	-36d
C-NCR-1030	Fine Grading, In-Stream Feature, Bedding and Geotextile Placement	57d	18-Aug-21 A	08-Nov-21 A	28-May-21	24-Jun-21	-93d
C-NCR-1040	Revegetation	80d	25-Aug-21 A	16-Dec-21 A	25-Jun-21	15-Jul-21	-107d
Phase 1 - Temporary Diversion Channels		28d	24-Aug-21 A	01-Oct-21 A	01-Sep-21	14-Sep-21	-13d
Temporary Downstream Channel Diversion / Tie in		15d	24-Aug-21 A	14-Sep-21 A	01-Sep-21	03-Sep-21	-6d
C-NCR-1080	Fish Rescue	11d	24-Aug-21 A	08-Sep-21 A	01-Sep-21	01-Sep-21	-4d
C-NCR-1090	Construct/ Tie In Downstream Temporary Channel Diversion	7d	08-Sep-21 A	14-Sep-21 A	01-Sep-21	03-Sep-21	-11d
C-NCR-1120	Install Isolation Berms	1d	14-Sep-21 A	14-Sep-21 A	02-Sep-21	02-Sep-21	-7d
Temporary Upstream Channel Diversion / Tie In		26d	26-Aug-21 A	01-Oct-21 A	08-Sep-21	14-Sep-21	-13d
C-NCR-1130	Fish Rescue	26d	26-Aug-21 A	01-Oct-21 A	08-Sep-21	09-Sep-21	-16d
C-NCR-1140	Construct Upstream Temporary Channel Diversion	8d	22-Sep-21 A	01-Oct-21 A	09-Sep-21	14-Sep-21	-13d
C-NCR-1170	Install Isolation Berms	1d	01-Oct-21 A	01-Oct-21 A	10-Sep-21	10-Sep-21	-15d
Ultimate Nose Creek Alignment Tie In's and Commission		2d	08-Nov-21 A	09-Nov-21 A	16-Sep-21	28-Sep-21	-29d
C-NCR-1200	Fish Rescue	1d	08-Nov-21 A	08-Nov-21 A	16-Sep-21	16-Sep-21	-36d
C-NCR-1220	Upstream Ultimate Alignment Channel Tie In	1d	09-Nov-21 A	09-Nov-21 A	21-Sep-21	22-Sep-21	-33d
C-NCR-1230	Initiate Water Transfer Process From Existing Nose Creek To Ultimate Nose Cr	1d	09-Nov-21 A	09-Nov-21 A	23-Sep-21	28-Sep-21	-29d
Mainline QEII		105d	02-May-23 A	29-Sep-23			
Mainline QEII		102d	05-May-23 A	29-Sep-23			
Mainline QEII Median		22d	30-Aug-23	29-Sep-23			
C-QE2M-1000	Crossover Removal	5d	30-Aug-23	06-Sep-23			
C-QE2M-1010	Temp Culvert Removal	5d	30-Aug-23	06-Sep-23			
C-QE2M-1020	Grading QEII Median	3d	07-Sep-23	11-Sep-23			

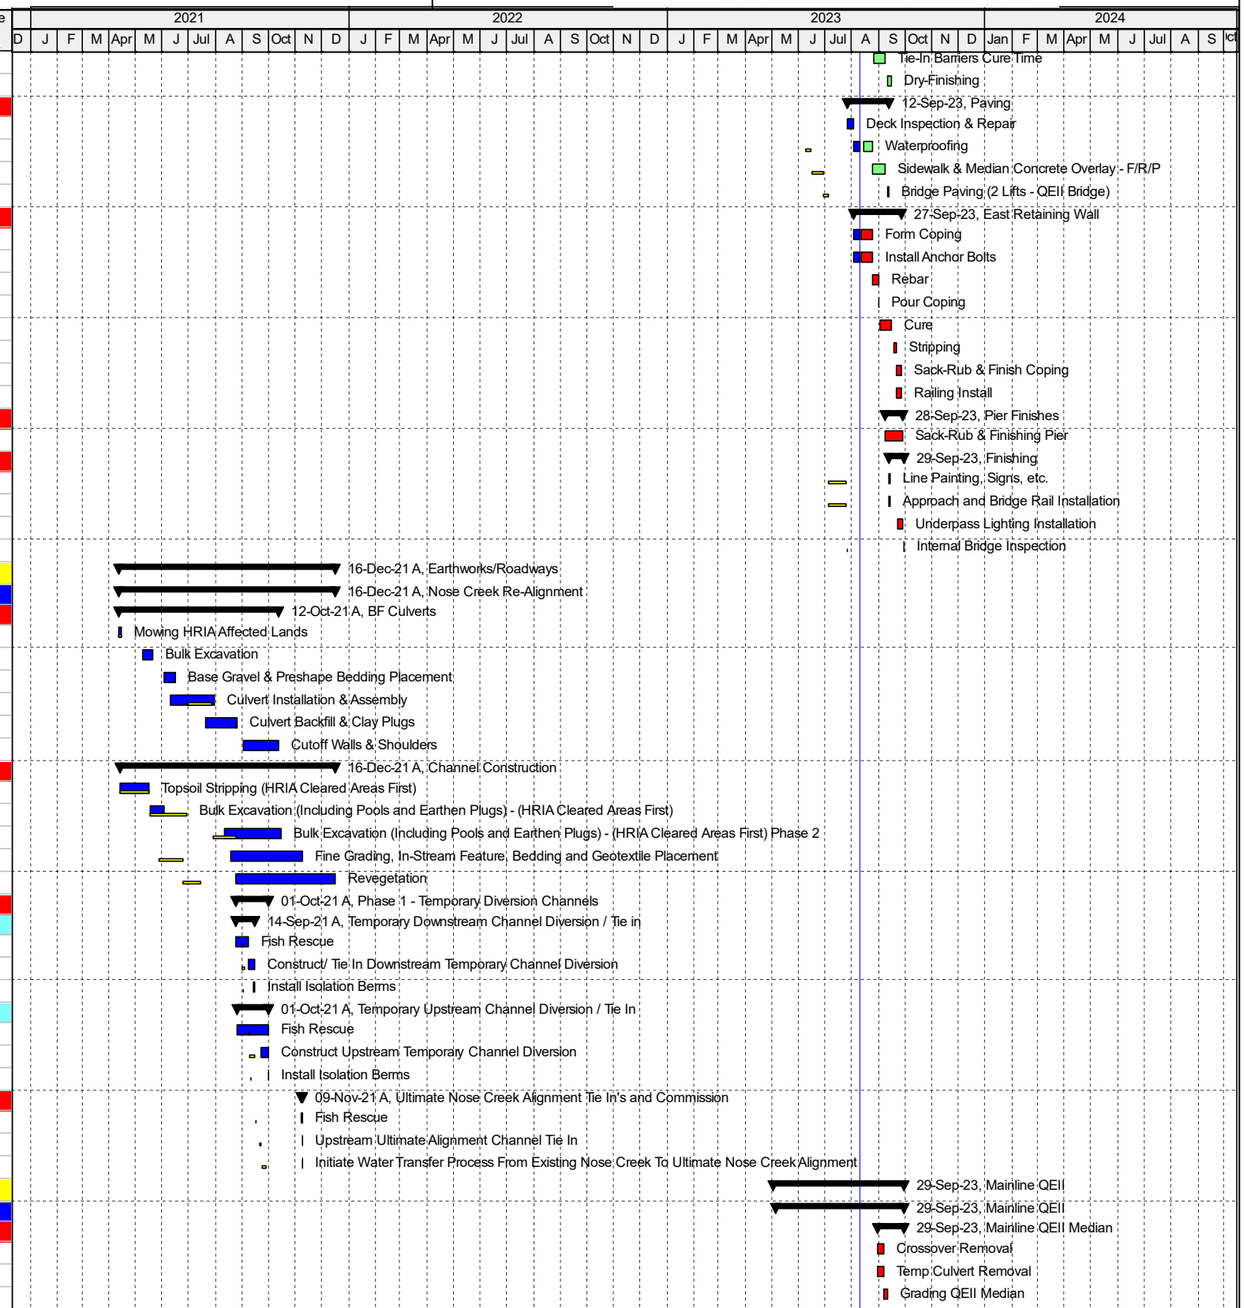

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-QE2M-1070	Topsoiling (QEII Median)	3d	12-Sep-23	14-Sep-23			
C-QE2M-1080	Cable Barrier East (QEII Median)	5d	15-Sep-23	21-Sep-23			
C-QE2M-1090	Cable Barrier West (QEII Median)	5d	22-Sep-23	28-Sep-23			
C-QE2M-1120	Highmast Lighting Completion	0d		28-Sep-23			
C-QE2M-1100	Seeding (QEII Median)	1d	29-Sep-23	29-Sep-23			
C-QE2M-1110	QEII Median Complete	0d		29-Sep-23			
Guide Sign Foundations		7d	07-Sep-23	15-Sep-23			
C-QE2M-1030	NB Ramp/40th - Guide Sign 3 Foundation (Left)	1d	07-Sep-23	07-Sep-23			
C-QE2M-1040	NB Ramp/40th - Guide Sign 3 Stage 2 Form (Left)	2d	08-Sep-23	11-Sep-23			
C-QE2M-1050	NB Ramp/40th - Guide Sign 3 Stage 2 Pour (Left)	1d	12-Sep-23	12-Sep-23			
C-QE2M-1060	NB Ramp/40th - Guide Sign 3 Stage 2 Cure/Strip (Left)	3d	13-Sep-23	15-Sep-23			
East Slope Protection		47d	05-May-23 A	12-Jul-23 A			
C-MFW-QEII-ESP-1500	Rough Grading (QEII Bridge - East Slope Protection)	6d	05-May-23 A	12-May-23 A			
C-MFW-QEII-ESP-1510	F/R/P Toe (QEII Bridge - East Slope Protection)	8d	12-May-23 A	25-May-23 A			
C-MFW-QEII-ESP-1520	Final Grading, Gravel Placement (QEII Bridge - East Slope Protection)	4d	19-May-23 A	25-May-23 A			
C-MFW-QEII-ESP-1530	Formwork (QEII Bridge - East Slope Protection)	4d	26-May-23 A	31-May-23 A			
C-MFW-QEII-ESP-1540	Rebar (QEII Bridge - East Slope Protection)	5d	01-Jun-23 A	07-Jun-23 A			
C-MFW-QEII-ESP-1550	Pour 1 (QEII Bridge - East Slope Protection)	1d	08-Jun-23 A	08-Jun-23 A			
C-MFW-QEII-ESP-1560	Pour 2 (QEII Bridge - East Slope Protection)	1d	13-Jun-23 A	13-Jun-23 A			
C-MFW-QEII-ESP-1570	Pour 3 (QEII Bridge - East Slope Protection)	1d	23-Jun-23 A	23-Jun-23 A			
C-MFW-QEII-ESP-1590	Pour 4 (QEII Bridge - East Slope Protection)	1d	29-Jun-23 A	29-Jun-23 A			
C-MFW-QEII-ESP-1600	Pour 5 (QEII Bridge - East Slope Protection)	1d	05-Jul-23 A	05-Jul-23 A			
C-MFW-QEII-ESP-1580	Concrete Cure Time (QEII Bridge - East Slope Protection)	7d	06-Jul-23 A	12-Jul-23 A			
West Slope Protection		40d	06-Jun-23 A	01-Aug-23 A			
C-MFW-QEII-WSP-1500	Rough Grading (QEII Bridge - West Slope Protection)	4d	06-Jun-23 A	09-Jun-23 A			
C-MFW-QEII-WSP-1510	F/R/P Toe (QEII Bridge - West Slope Protection)	5d	19-Jun-23 A	23-Jun-23 A			
C-MFW-QEII-WSP-1520	Final Grading, Gravel Placement (QEII Bridge - West Slope Protection)	3d	26-Jun-23 A	28-Jun-23 A			
C-MFW-QEII-WSP-1530	Formwork (QEII Bridge - West Slope Protection)	3d	28-Jun-23 A	03-Jul-23 A			
C-MFW-QEII-WSP-1540	Rebar (QEII Bridge - West Slope Protection)	2d	30-Jun-23 A	04-Jul-23 A			
C-MFW-QEII-WSP-1550	Pour 1 (QEII Bridge - West Slope Protection)	1d	05-Jul-23 A	05-Jul-23 A			
C-MFW-QEII-WSP-1560	Pour 2 (QEII Bridge - West Slope Protection)	1d	10-Jul-23 A	10-Jul-23 A			
C-MFW-QEII-WSP-1570	Pour 3 (QEII Bridge - West Slope Protection)	1d	13-Jul-23 A	13-Jul-23 A			
C-MFW-QEII-WSP-1590	Pour 4 (QEII Bridge - West Slope Protection)	1d	19-Jul-23 A	19-Jul-23 A			
C-MFW-QEII-WSP-1600	Pour 5 (QEII Bridge - West Slope Protection)	1d	25-Jul-23 A	25-Jul-23 A			
C-MFW-QEII-WSP-1580	Concrete Cure Time (QEII Bridge - West Slope Protection)	7d	26-Jul-23 A	01-Aug-23 A			
High Mast Lighting (QEII Median)		104d	02-May-23 A	28-Sep-23			
C-HML-1010	Drill Shot Undergrounds (South)	1d	02-May-23 A	02-May-23 A			
C-HML-1020	Drill Shot Underground (North)	1d	02-May-23 A	02-May-23 A			
C-HML-1000	Trench and Install Median Conduit	10d	22-Aug-23	05-Sep-23			
Luminaire #31		22d	21-Aug-23	20-Sep-23			
C-HMS-31-1000	Drill Pile Footing	1d	21-Aug-23*	21-Aug-23			
C-HMS-31-1020	R/P Pile Footing	2d	21-Aug-23	22-Aug-23			
C-HMS-31-1010	Install Conduit	1d	21-Aug-23	21-Aug-23			
C-HMS-31-1050	Pile Cure	28d	23-Aug-23	19-Sep-23			
C-HMS-31-1030	Rough-in Cable	1d	06-Sep-23	06-Sep-23			
C-HMS-31-1040	Install Highmast Pole	1d	20-Sep-23	20-Sep-23			
Luminaire #32		22d	22-Aug-23	21-Sep-23			
C-HMS-32-1000	Drill Pile Footing	1d	22-Aug-23	22-Aug-23			
C-HMS-32-1020	R/P Pile Footing	2d	22-Aug-23	23-Aug-23			
C-HMS-32-1010	Install Conduit	1d	22-Aug-23	22-Aug-23			
C-HMS-32-1030	Rough-in Cable	1d	24-Aug-23	24-Aug-23			
C-HMS-32-1050	Pile Cure	28d	24-Aug-23	20-Sep-23			
C-HMS-32-1040	Install Highmast Pole	1d	21-Sep-23	21-Sep-23			
Luminaire #33		22d	23-Aug-23	22-Sep-23			
C-HMS-33-1000	Drill Pile Footing	1d	23-Aug-23	23-Aug-23			
C-HMS-33-1020	R/P Pile Footing	2d	23-Aug-23	24-Aug-23			
C-HMS-33-1010	Install Conduit	1d	23-Aug-23	23-Aug-23			

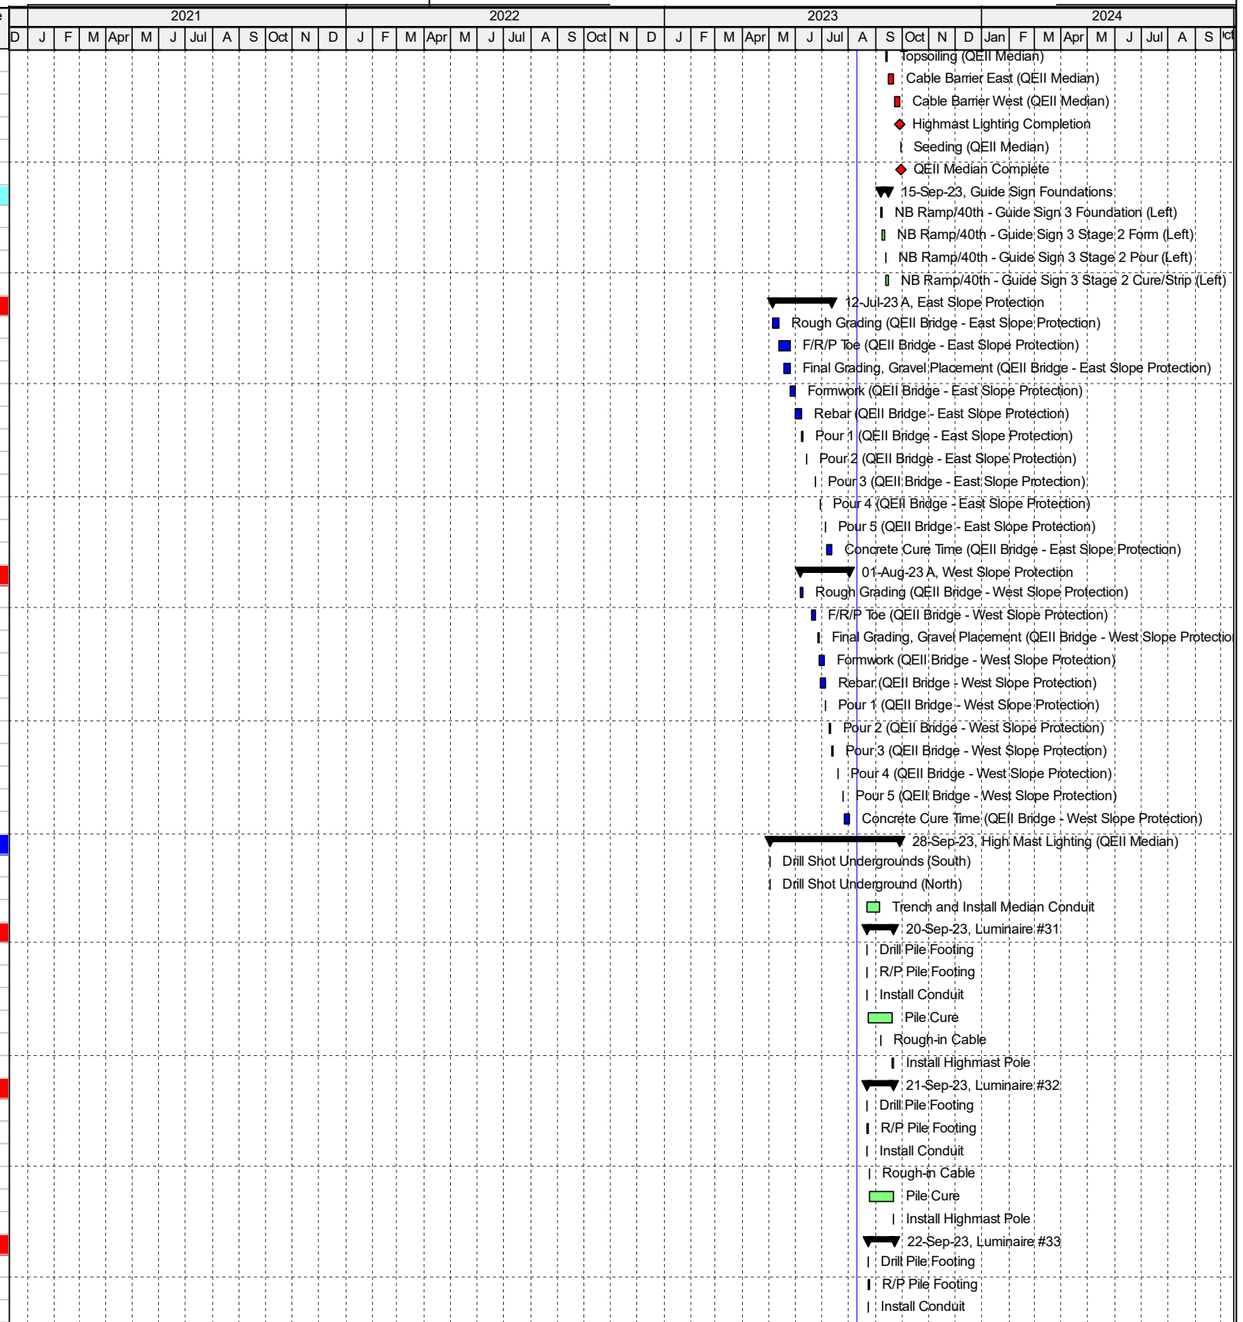

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-HMS-33-1030	Rough-in Cable	1d	25-Aug-23	25-Aug-23			
C-HMS-33-1050	Pile Cure	28d	25-Aug-23	21-Sep-23			
C-HMS-33-1040	Install Highmast Pole	1d	22-Sep-23	22-Sep-23			
Luminaire #34		22d	24-Aug-23	25-Sep-23			
C-HMS-34-1000	Drill Pile Footing	1d	24-Aug-23	24-Aug-23			
C-HMS-34-1020	R/P Pile Footing	2d	24-Aug-23	25-Aug-23			
C-HMS-34-1010	Install Conduit	1d	24-Aug-23	24-Aug-23			
C-HMS-34-1050	Pile Cure	28d	26-Aug-23	22-Sep-23			
C-HMS-34-1030	Rough-in Cable	1d	28-Aug-23	28-Aug-23			
C-HMS-34-1040	Install Highmast Pole	1d	25-Sep-23	25-Sep-23			
Luminaire #35		22d	25-Aug-23	26-Sep-23			
C-HMS-35-1000	Drill Pile Footing	1d	25-Aug-23	25-Aug-23			
C-HMS-35-1020	R/P Pile Footing	2d	25-Aug-23	28-Aug-23			
C-HMS-35-1010	Install Conduit	1d	25-Aug-23	25-Aug-23			
C-HMS-35-1030	Rough-in Cable	1d	29-Aug-23	29-Aug-23			
C-HMS-35-1050	Pile Cure	28d	29-Aug-23	25-Sep-23			
C-HMS-35-1040	Install Highmast Pole	1d	26-Sep-23	26-Sep-23			
Luminaire #36		22d	28-Aug-23	27-Sep-23			
C-HMS-36-1000	Drill Pile Footing	1d	28-Aug-23	28-Aug-23			
C-HMS-36-1020	R/P Pile Footing	2d	28-Aug-23	29-Aug-23			
C-HMS-36-1010	Install Conduit	1d	28-Aug-23	28-Aug-23			
C-HMS-36-1030	Rough-in Cable	1d	30-Aug-23	30-Aug-23			
C-HMS-36-1050	Pile Cure	28d	30-Aug-23	26-Sep-23			
C-HMS-36-1040	Install Highmast Pole	1d	27-Sep-23	27-Sep-23			
Luminaire #37		22d	29-Aug-23	28-Sep-23			
C-HMS-37-1000	Drill Pile Footing	1d	29-Aug-23	29-Aug-23			
C-HMS-37-1020	R/P Pile Footing	2d	29-Aug-23	30-Aug-23			
C-HMS-37-1010	Install Conduit	1d	29-Aug-23	29-Aug-23			
C-HMS-37-1030	Rough-in Cable	1d	31-Aug-23	31-Aug-23			
C-HMS-37-1050	Pile Cure	28d	31-Aug-23	27-Sep-23			
C-HMS-37-1040	Install Highmast Pole	1d	28-Sep-23	28-Sep-23			
West of CPR Bridge		330d	06-Jun-22 A	02-Oct-23			
2022 Eastbound Lane		106d	06-Jun-22 A	05-Nov-22 A			
C-WCPR-EBL-1000	Traffic Flip	1d	06-Jun-22 A	06-Jun-22 A			
C-WCPR-EBL-1010	Removal of Guardrail	1d	07-Jul-22 A	08-Jul-22 A			
C-WCPR-EBL-1020	Remove Existing Signage	1d	08-Jul-22 A	09-Jul-22 A			
C-WCPR-EBL-1030	Grading	50d	13-Jul-22 A	12-Sep-22 A			
C-WCPR-EBL-1040	Light Bases and Underground Conduit (Fortis)	5d	02-Aug-22 A	08-Aug-22 A			
C-WCPR-EBL-1050	Remove and Relocate Catch Basin #1	3d	14-Sep-22 A	16-Sep-22 A			
C-WCPR-EBL-1060	Subgrade Preparation	2d	17-Sep-22 A	19-Sep-22 A			
C-WCPR-EBL-1070	GBC Placement Bottom Lift	5d	26-Sep-22 A	30-Sep-22 A			
C-WCPR-EBL-1080	Median F/R/P [80%]	10d	06-Oct-22 A	20-Oct-22 A			
C-WCPR-EBL-1090	Pathway, Wheel Chair Ramp	3d	07-Oct-22 A	11-Oct-22 A			
C-WCPR-EBL-1100	Curb and Gutter F/R/P	3d	07-Oct-22 A	11-Oct-22 A			
C-WCPR-EBL-1110	Curing Curb and Gutter	3d	12-Oct-22 A	14-Oct-22 A			
C-WCPR-EBL-1120	Asphalt Milling	2d	17-Oct-22 A	18-Oct-22 A			
C-WCPR-EBL-1130	Paving Bottom Lift	0d	19-Oct-22 A	19-Oct-22 A			
C-WCPR-EBL-1140	Temporary Pavement Marking	0d		05-Nov-22 A			
2023 East Bound Lane		102d	08-May-23 A	02-Oct-23			
C-WCPR-EBL-2000	Eastbound - Gravel Grading up to Bridge Tie-In (West of CPR)	3d	08-May-23 A	10-May-23 A			
C-WCPR-EBL-2010	Eastbound - Two Lifts of Asphalt Tie-In into Bridge (West of CPR)	1d	11-May-23 A	11-May-23 A			
C-WCPR-EBL-2070	Eastbound - Temp Barrier Removal (West of CPR)	1d	11-May-23 A	12-May-23 A			
C-WCPR-EBL-2020	Eastbound - Temp Pavement Line Painting (West of CPR)	1d	13-May-23 A	13-May-23 A			
C-WCPR-EBL-2080	East Bound Lane Complete	0d		15-May-23 A			
C-WCPR-EBL-2030	Eastbound - TL-4 Barrier Installation (West of CPR)	5d	11-Aug-23*	17-Aug-23			
Under CPR Bridge		12d	15-Sep-23	02-Oct-23			
C-UCPR-EBL-1000	Grading Under CPR Bridge (EB)	4d	15-Sep-23	20-Sep-23			

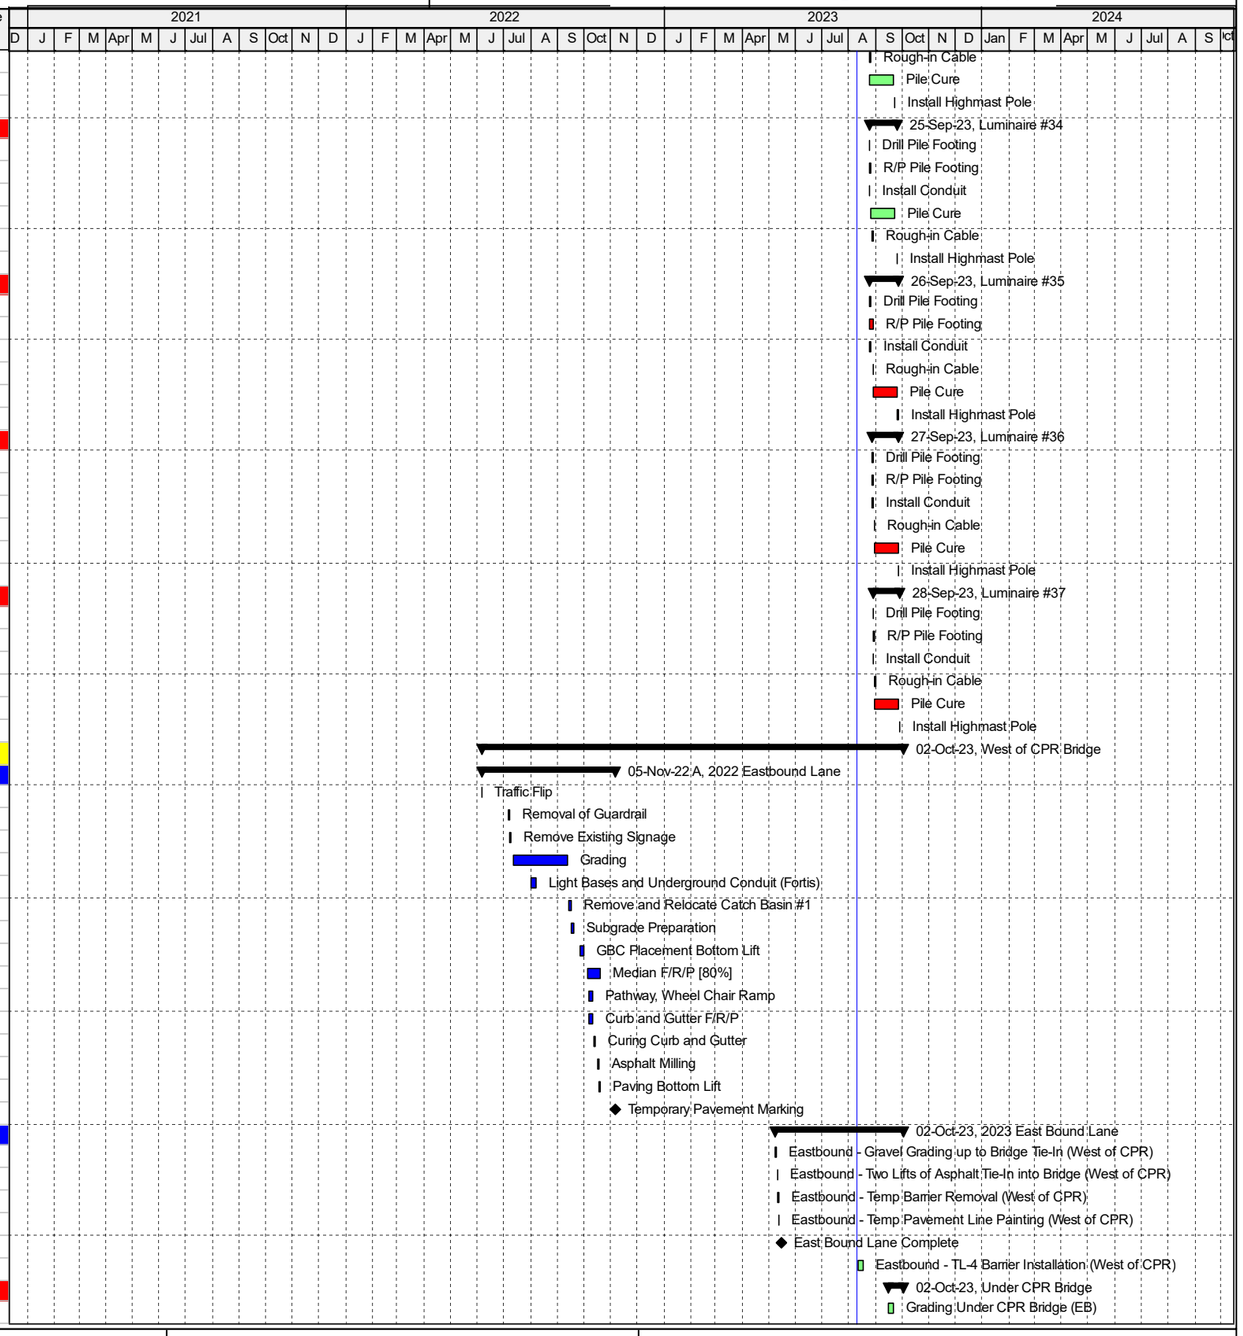

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-UCPR-EBL-1010	GBC Under CPR Bridge (EB)	4d	21-Sep-23	26-Sep-23			
C-UCPR-EBL-1020	Asphalt Pathway Paving Under CPR Bridge (EB)	2d	27-Sep-23	28-Sep-23			
C-UCPR-EBL-1030	Topsoil Under CPR Bridge (EB)	2d	29-Sep-23	02-Oct-23			
West Bound Lane		85d	15-May-23 A	14-Sep-23			
Removals/Utilities		42d	15-May-23 A	13-Jul-23 A			
C-WCPR-WBL-1000	Traffic Flip (WB - West of CPR)	1d	15-May-23 A	15-May-23 A			
C-WCPR-WBL-1030	Sawcutting Edge of Asphalt (WB - West of CPR)	1d	01-Jun-23 A	01-Jun-23 A			
X-DEL-001-1010	Gas Line Conflict	15d	02-Jun-23 A	23-Jun-23 A			
C-WCPR-WBL-1040	Stripping (WB - West of CPR)	24d	05-Jun-23 A	07-Jul-23 A			
C-WCPR-WBL-1010	Remove Existing Signage (WB - West of CPR)	1d	09-Jun-23 A	09-Jun-23 A			
C-WCPR-WBL-1020	Utility Relocation (Fortis) (WB - West of CPR)	19d	09-Jun-23 A	07-Jul-23 A			
X-DEL-001-1020	HydroVac Gas Line (ADDED SCOPE - GAS LINE CONFLICT)	4d	04-Jul-23 A	07-Jul-23 A			
X-DEL-001-1030	Concrete Capping (ADDED SCOPE - GAS LINE CONFLICT)	1d	13-Jul-23 A	13-Jul-23 A			
Subgrade & U-G		10d	06-Jul-23 A	19-Jul-23 A			
C-WCPR-WBL-1510	Subgrade (WB - West of CPR)	6d	06-Jul-23 A	13-Jul-23 A			
C-WCPR-WBL-1520	CB #3 - Relocate & Install (WB - West of CPR)	2d	14-Jul-23 A	17-Jul-23 A			
C-WCPR-WBL-1530	CB #4 - Relocate & Install (WB - West of CPR) (CHANGE)	2d	18-Jul-23 A	19-Jul-23 A			
GBC, Concrete, Paving		24d	14-Jul-23 A	17-Aug-23			
C-WCPR-WBL-2000	Porkchop Grading (WB - West of CPR)	3d	14-Jul-23 A	18-Jul-23 A			
C-WCPR-WBL-2010	GBC Roadway (WB -West of CPR)	5d	20-Jul-23 A	26-Jul-23 A			
C-WCPR-WBL-2020	Curb and Gutter F/R/P (WB - West of CPR)	4d	07-Aug-23 A	11-Aug-23			
C-WCPR-WBL-2030	Porkchop Curbs (WB - West of CPR)	4d	07-Aug-23 A	11-Aug-23			
C-WCPR-WBL-2040	Curing Curb and Gutter (WB - West of CPR)	3d	12-Aug-23	14-Aug-23			
C-WCPR-WBL-2070	Paving Bottom 2 Lifts (WB - West of CPR)	1d	15-Aug-23*	15-Aug-23			
C-WCPR-WBL-2050	GBC Infill Pork Chop (WB - West of CPR)	1d	16-Aug-23	16-Aug-23			
C-WCPR-WBL-2510	Wheelchair Ramp (WB - West of CPR)	2d	16-Aug-23	17-Aug-23			
C-WCPR-WBL-2060	Porkchop Concrete Infill (WB - West of CPR)	1d	17-Aug-23	17-Aug-23			
Finishes		20d	17-Aug-23	14-Sep-23			
C-WCPR-WBL-2500	Milling of Existing Asphalt (WB - West of CPR)	1d	17-Aug-23	17-Aug-23			
C-WCPR-WBL-2520	Paving Top Lift (WB - West of CPR)	1d	18-Aug-23	18-Aug-23			
C-WCPR-WBL-2530	Topsoil Infill & Grading Behind Curbs (WB - West of CPR)	3d	21-Aug-23	23-Aug-23			
C-WCPR-WBL-2540	Permanent Line Painting (WB - West of CPR)	2d	21-Aug-23	22-Aug-23			
C-WCPR-WBL-2550	TL-4 Barrier Install (WB - West of CPR)	5d	21-Aug-23	25-Aug-23			
C-WCPR-WBL-2560	Seeding outside of Curb (WB - West of CPR)	2d	24-Aug-23	25-Aug-23			
C-WCPR-WBL-2570	Install Traffic Signage (WB - West of CPR)	1d	24-Aug-23	24-Aug-23			
C-WCPR-WBL-2580	Temp Crossover Removal (WB - West of CPR @ Crossover)	1d	25-Aug-23	25-Aug-23			
C-WCPR-WBL-2590	Toplift Asphalt EB (EB - West of CPR)	1d	28-Aug-23	28-Aug-23			
C-WCPR-WBL-2600	GBC Infill Grading Crossover (WB - West of CPR @ Crossover)	2d	28-Aug-23	29-Aug-23			
C-WCPR-WBL-2610	Median Curb Completion (WB - West of CPR @ Crossover)	5d	30-Aug-23	06-Sep-23			
C-WCPR-WBL-2620	Curb Curing	3d	07-Sep-23	09-Sep-23			
C-WCPR-WBL-2630	Median Gravel Infill & Grading (WB - West of CPR)	2d	11-Sep-23	12-Sep-23			
C-WCPR-WBL-2640	Median Concrete Infill (WB - West of CPR)	2d	13-Sep-23	14-Sep-23			
C-WCPR-WBL-2650	East & West Lane Complete	0d		14-Sep-23			
Pedestrian Pathway		3d	17-Aug-23	21-Aug-23			
C-UCPR-WBL-2500	Pathway Grading (WB - West of CPR)	1d	17-Aug-23	17-Aug-23			
C-UCPR-WBL-2510	Pathway Gravel (WB - West of CPR)	1d	18-Aug-23	18-Aug-23			
C-UCPR-WBL-2520	Pathway Pavement (WB - West of CPR)	1d	21-Aug-23	21-Aug-23			
Southpoint Landing		265d	12-Sep-22 A	04-Oct-23			
West Ramp (Southbound)		256d	12-Sep-22 A	21-Sep-23			
2022 West Ramp (Southbound)		26d	12-Sep-22 A	18-Oct-22 A			
C-SPL-WR-1000	Grading	6d	12-Sep-22 A	17-Sep-22 A			
C-SPL-WR-1010	Preparation Subgrade	9d	13-Sep-22 A	23-Sep-22 A			
C-SPL-WR-1030	Install Manhole #2	1d	23-Sep-22 A	23-Sep-22 A			
C-SPL-WR-1020	Install Manhole #1	1d	03-Oct-22 A	03-Oct-22 A			
C-SPL-WR-1040	GBC Placement Bottom Lift	3d	04-Oct-22 A	07-Oct-22 A			
C-SPL-WR-1070	Curb and Gutter F/R/P	5d	07-Oct-22 A	13-Oct-22 A			
C-SPL-WR-1110	Island Median F/R/P	5d	07-Oct-22 A	13-Oct-22 A			

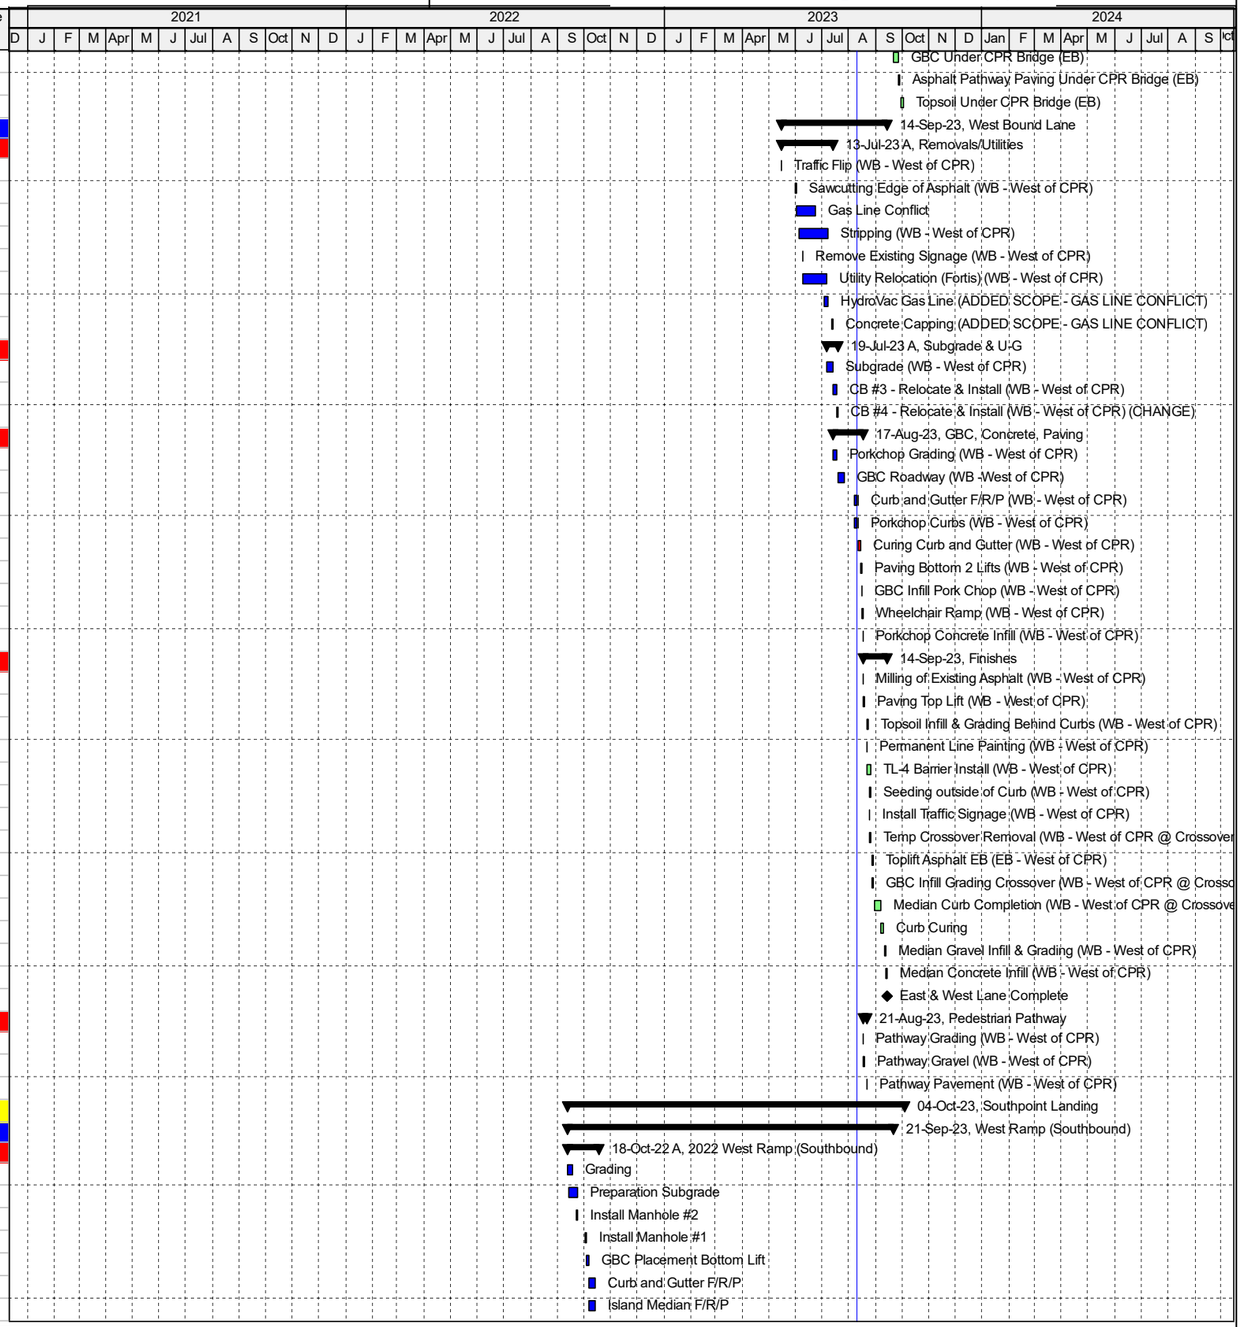

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline

Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-SPL-WR-1090	Curing Curb and Gutter	5d	14-Oct-22 A	18-Oct-22 A			
C-SPL-WR-1060	GBC Placement Top Lift	3d	15-Oct-22 A	18-Oct-22 A			
2023 West Ramp (Southbound)		98d	03-May-23 A	21-Sep-23			
C-SPL-WR-1270	Directional Drilling Under Bridge Lighting (SB - SP Landing)	3d	03-May-23 A	05-May-23 A			
C-SPL-WR-1190	GBC Grading @ Bridge Tie-In (SB - SP Landing)	2d	08-May-23 A	09-May-23 A			
C-SPL-WR-1230	Curb Tie-In and Median Curb Completion (SB - SP Landing)	5d	09-Jun-23 A	15-Jun-23 A			
C-SPL-WR-1200	Install Median Electrical Conduit (SB - SP Landing)	8d	22-Jun-23 A	05-Jul-23 A			
C-SPL-WR-1280	Directional Drilling South Street Lighting (SB - SP Landing)	3d	22-Jun-23 A	26-Jun-23 A			
C-SPL-WR-1290	Porkchop Gravels & Plating (Review Two Lane Turn Bay off Bridge)	2d	23-Jun-23 A	26-Jun-23 A			
C-SPL-WR-1210	Install Light Bases - Median (SB - SP Landing)	3d	07-Jul-23 A	11-Jul-23 A			
C-SPL-WR-1310	Fortis Under-Bridge Lighting Connections	3d	07-Jul-23 A	11-Jul-23 A			
C-SPL-WR-1220	Davit Pole Install - Median (SB - SP Landing)	3d	12-Jul-23 A	14-Jul-23 A			
C-SPL-WR-1120	Paving - Bottom Two Lifts Asphalt (SB - SP Landing)	1d	21-Jul-23 A	21-Jul-23 A			
C-SPL-WR-1240	Median Gravel Infill (SB - SP Landing)	1d	21-Aug-23*	21-Aug-23			
C-SPL-WR-1260	Median Concrete Infill (SB - SP Landing)	1d	22-Aug-23	22-Aug-23			
C-SPL-WR-1140	Paving Top Lift (SB - SP Landing)	1d	31-Aug-23*	31-Aug-23			
C-SPL-WR-1150	Pavement Marking (SB - SP Landing)	1d	01-Sep-23	01-Sep-23			
C-SPL-WR-1300	TL-4 Barrier CPR Bridge Tie-In (SB - SP Landing)	5d	01-Sep-23	08-Sep-23			
C-SPL-WR-1160	Topsoil Outside of Curb (SB - SP Landing)	3d	11-Sep-23	13-Sep-23			
C-SPL-WR-1250	Roadway Barrier Off Bridge (SB - SP Landing)	4d	11-Sep-23	14-Sep-23			
C-SPL-WR-1130	Install Signage (SB - SP Landing)	2d	14-Sep-23	15-Sep-23			
C-SPL-WR-1330	Barrier Curing (SB - SP Landing)	3d	15-Sep-23	17-Sep-23			
C-SPL-WR-1170	Seeding (SB - SP Landing)	2d	18-Sep-23	19-Sep-23			
C-SPL-WR-1320	Roadway Quadguard Instal (SB - SP Landing)	4d	18-Sep-23	21-Sep-23			
C-SPL-WR-1180	West Ramp Complete	0d		21-Sep-23			
East Ramp (Northbound/40th)		99d	15-May-23 A	04-Oct-23			
Removals		41d	16-May-23 A	13-Jul-23 A			
C-SPL-ER-1020	Sawcut & Removal of Existing Curb and Gutter	1d	16-May-23 A	16-May-23 A			
C-SPL-ER-1110	Removal Existing Concrete Barriers	2d	16-May-23 A	17-May-23 A			
C-SPL-ER-1010	Salvage Fortis Street Lights (NB - SP Landing)	1d	17-May-23 A	17-May-23 A			
C-SPL-ER-1240	Asphalt Removal (NB - SP Landing)	1d	18-May-23 A	18-May-23 A			
C-SPL-ER-1100	Median Removal Rip Rap & Curb (NB - SP Landing)	2d	07-Jul-23 A	10-Jul-23 A			
C-SPL-ER-1390	Install Fortis Transformer (NB - SP Landing)	5d	07-Jul-23 A	13-Jul-23 A			
Grading & Undergrounds		40d	15-May-23 A	11-Jul-23 A			
C-SPL-ER-1040	Grading Subgrade (Northbound/40th)	14d	15-May-23 A	02-Jun-23 A			
C-SPL-ER-1440	Grading West Main Street Bridge Slopes	14d	15-May-23 A	02-Jun-23 A			
C-SPL-ER-1050	Subgrade (Northbound/40th)	4d	05-Jun-23 A	09-Jun-23 A			
C-SPL-ER-1220	Traffic Light Conduit Installation (Northbound/40th)	2d	15-Jun-23 A	16-Jun-23 A			
C-SPL-ER-1270	Median Conduit Install (Northbound/40th)	3d	22-Jun-23 A	26-Jun-23 A			
C-SPL-ER-1280	Median Light Bases Install (Northbound/40th)	3d	22-Jun-23 A	27-Jun-23 A			
C-SPL-ER-1060	Remove and Relocate CB #1 (Northbound/40th)	3d	26-Jun-23 A	28-Jun-23 A			
C-SPL-ER-1250	Bridge Slope Grading Coping (Northbound/40th)	6d	04-Jul-23 A	11-Jul-23 A			
GBC, Curbs & Paving & Finishes		50d	07-Jul-23 A	18-Sep-23			
C-SPL-ER-1430	Install Bridge Conduit (53mm Interconnect) (CP to Main)	3d	07-Jul-23 A	11-Jul-23 A			
C-SPL-ER-1080	GBC Placement (Northbound/40th)	2d	17-Jul-23 A	18-Jul-23 A			
C-SPL-ER-1120	NB Curb (Northbound/40th)	3d	19-Jul-23 A	21-Jul-23 A			
C-SPL-ER-1290	Median Curb (Northbound/40th)	3d	20-Jul-23 A	24-Jul-23 A			
C-SPL-ER-1160	Paving Bottom Lift (Northbound/40th)	2d	24-Jul-23 A	25-Jul-23 A			
C-SPL-ER-1150	Davit Pole Install (Northbound/40th)	5d	25-Jul-23 A	31-Jul-23 A			
C-SPL-ER-1140	Curing Curb and Gutter	3d	25-Jul-23 A	27-Jul-23 A			
C-SPL-ER-1260	Traffic Light Base Installation (Northbound/40th)	2d	26-Jul-23 A	27-Jul-23 A			
C-SPL-ER-1130	Wheel Chair Ramp F/R/P	3d	18-Aug-23	22-Aug-23			
C-SPL-ER-1300	Median Infill Gravel (Northbound/40th)	1d	22-Aug-23	22-Aug-23			
C-SPL-ER-1310	Median Infill Concrete (Northbound/40th)	1d	23-Aug-23	23-Aug-23			
C-SPL-ER-1380	Traffic Light Install (Northbound/40th)	6d	23-Aug-23	30-Aug-23			
C-SPL-ER-1180	Paving Top Lift (Northbound/40th)	1d	30-Aug-23*	30-Aug-23			

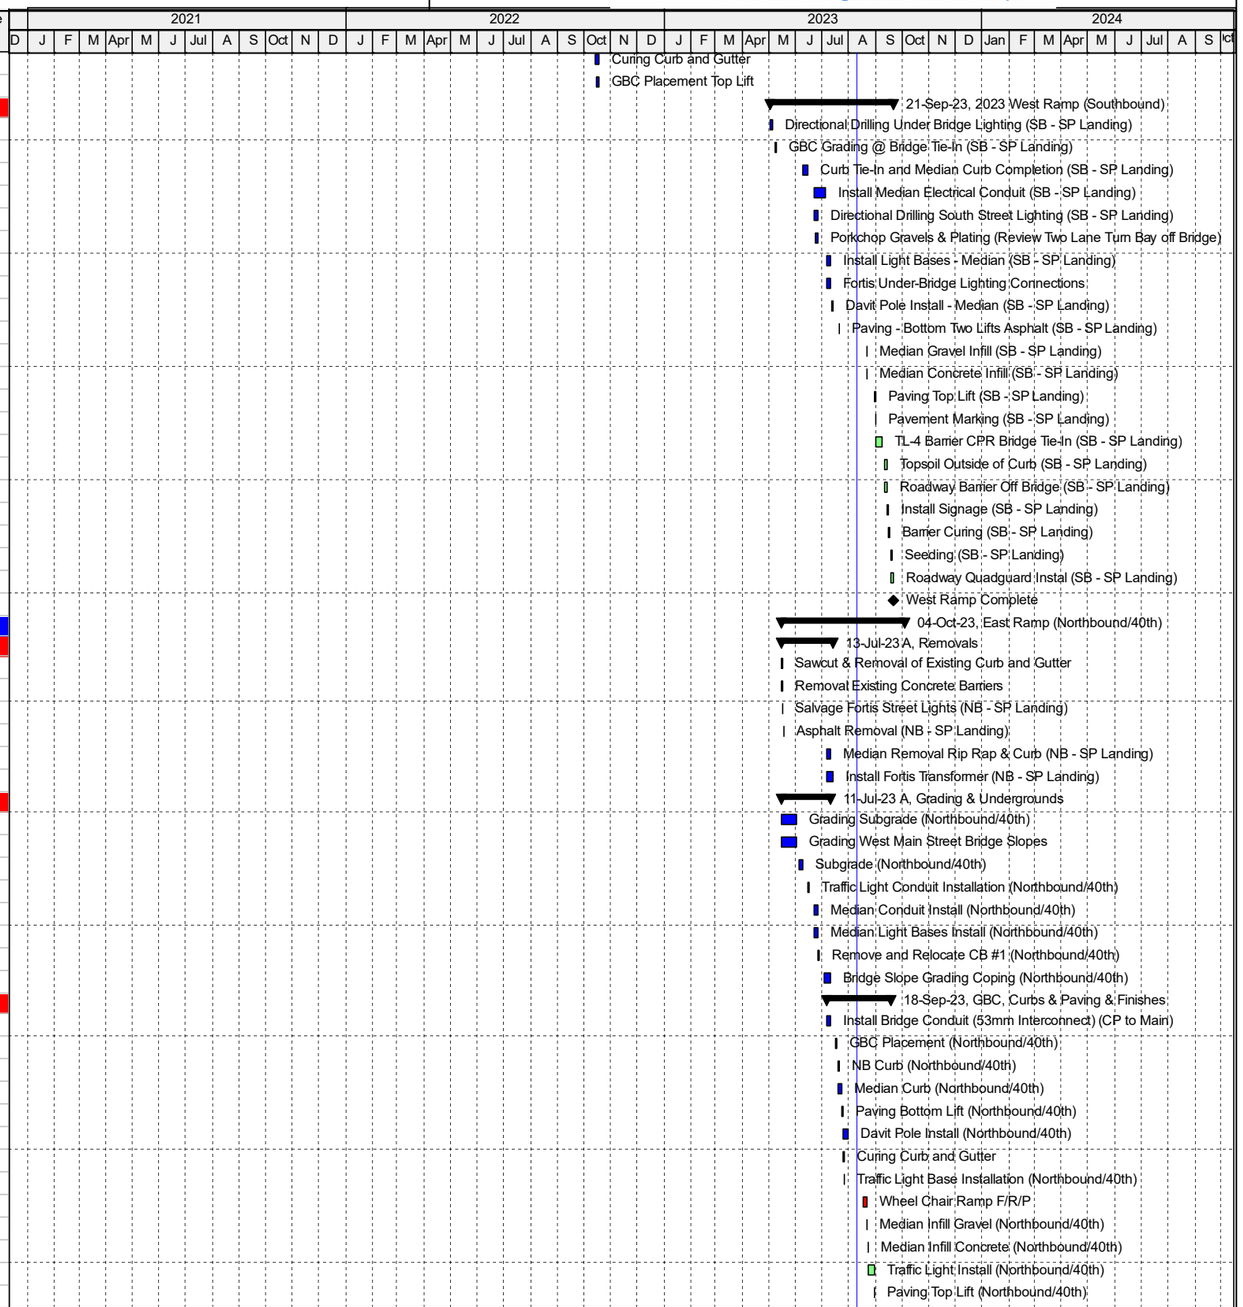

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-SPL-ER-1210	Pavement Marking (Northbound/40th)	1d	31-Aug-23	31-Aug-23			
C-SPL-ER-1190	Install Signage (Northbound/40th)	2d	31-Aug-23	01-Sep-23			
C-SPL-ER-1410	TL-4 Barriers Main Street (Northbound/40th)	5d	31-Aug-23	07-Sep-23			
C-SPL-ER-1420	Topsoil Behind Curbs (Northbound/40th)	5d	08-Sep-23	14-Sep-23			
C-SPL-ER-1200	Seeding (Northbound/40th)	2d	15-Sep-23	18-Sep-23			
C-SPL-ER-1230	Northbound/40th - South Point Landing NB Complete	0d		18-Sep-23			
Pedestrian Pathways		14d	21-Aug-23	08-Sep-23			
C-SPL-ER-1320	South Pathway Tie-In Gravel	1d	21-Aug-23	21-Aug-23			
C-SPL-ER-1330	South Pathway Wheelchair Concrete	4d	22-Aug-23	25-Aug-23			
C-SPL-ER-1350	North Pathway Gravel	3d	22-Aug-23	24-Aug-23			
C-SPL-ER-1360	North Pathway Wheelchair Concrete	4d	25-Aug-23	30-Aug-23			
C-SPL-ER-1340	South Pathway Asphalt	1d	28-Aug-23	28-Aug-23			
C-SPL-ER-1370	North Pathway Pavement	1d	31-Aug-23	31-Aug-23			
C-SPL-ER-1400	Pedestrian Rail North	5d	01-Sep-23	08-Sep-23			
Swale/Slope Pro		12d	19-Sep-23	04-Oct-23			
C-SPL-SWA-1020	Traffic Flip	1d	19-Sep-23	19-Sep-23			
C-SPL-SWA-1030	Pork Chop Infill Concrete	3d	20-Sep-23	22-Sep-23			
C-SPL-SWA-1000	East CPR Under Bridge Grading	5d	21-Sep-23	27-Sep-23			
C-SPL-SWA-1010	East CPR Under Bridge Topsoil	5d	28-Sep-23	04-Oct-23			
Mainstreet		586d	10-May-21 A	13-Sep-23	18-May-21	28-Jun-21	-551d
C-SLMSB-EWL-1000	Topsoil Stripping	2d	10-May-21 A	12-May-21 A	18-May-21	21-May-21	8d
C-SLMSB-EWL-1010	Storm Drainage Installation (Phase 1)	3d	17-May-21 A	20-May-21 A			
C-SLMSB-EWL-1020	Bulk Grading - 2021	36d	25-Aug-21 A	15-Dec-21 A	25-May-21	28-Jun-21	-75d
C-SLMSB-EWL-1040	Grading	7d	03-Oct-22 A	12-Oct-22 A			
Soutbound Closure		33d	24-Jul-23 A	08-Sep-23			
C-MS-SBC-1000	Sawcut & Remove Asphalt (Mainstreet - SB Closure)	2d	24-Jul-23 A	25-Jul-23 A			
C-MS-SBC-1010	Trenching (Mainstreet - SB Closure)	1d	26-Jul-23 A	26-Jul-23 A			
C-MS-SBC-1020	EXIST Lead Install (Mainstreet - SB Closure)	1d	27-Jul-23 A	27-Jul-23 A			
C-MS-SBC-1030	Install Manhole - 23 (Mainstreet - SB Closure)	1d	28-Jul-23 A	28-Jul-23 A			
C-MS-SBC-1040	MH-23 Lead Install (Mainstreet - SB Closure)	1d	31-Jul-23 A	31-Jul-23 A			
C-MS-SBC-1050	Install Manhole - 06 (Mainstreet - SB Closure)	1d	01-Aug-23 A	01-Aug-23 A			
C-MS-SBC-1060	MH-06 Lead Install (Partial) (Mainstreet - SB Closure)	1d	02-Aug-23 A	02-Aug-23 A			
C-MS-SBC-1070	GBC Roadway Structure (Mainstreet - SB Closure)	2d	03-Aug-23 A	04-Aug-23 A			
C-MS-SBC-1080	Paving (Mainstreet - SB Closure)	0d	05-Aug-23 A	05-Aug-23 A			
C-MS-SBC-1090	Grading Under Bridge in Front of MSE Wall (Mainstreet - SB Closure)	3d	29-Aug-23	31-Aug-23			
C-MS-SBC-1100	Gravel Placement Pathway In Front of MSE Wall (Mainstreet - SB Closure)	3d	01-Sep-23	06-Sep-23			
C-MS-SBC-1110	Pavement Pathway MSE Wall to Roadway (Mainstreet - SB Closure)	2d	07-Sep-23	08-Sep-23			
C-MS-SBC-1120	Mainstreet Work Complete	0d		08-Sep-23			
Northbound Closure		36d	24-Jul-23 A	13-Sep-23			
C-MS-NBC-1000	Traffic Flip	1d	24-Jul-23 A	24-Jul-23 A			
C-MS-NBC-1010	Asphalt Removal (Mainstreet - NB Closure)	1d	25-Jul-23 A	25-Jul-23 A			
C-MS-NBC-1020	Trenching (Mainstreet - NB Closure)	1d	26-Jul-23 A	26-Jul-23 A			
C-MS-NBC-1030	MH-05A Lead Install (Mainstreet - NB Closure)	10d	03-Aug-23 A	18-Aug-23			
C-MS-NBC-1040	GBC Roadway Structure (Mainstreet - NB Closure)	1d	04-Aug-23 A	04-Aug-23 A			
C-MS-NBC-1050	Pavement Top Lift (Mainstreet - NB Closure)	1d	04-Aug-23 A	04-Aug-23 A			
C-MS-NBC-1120	Fortis Conflict @ Northbound Mainstreet [DELAYS MH-05A]	8d	07-Aug-23 A	17-Aug-23			
C-MS-NBC-1060	Pavement Marking (Mainstreet - NB Closure)	1d	14-Aug-23*	14-Aug-23			
C-MS-NBC-1070	Grading Under Bridge in Front of MSE Wall (Mainstreet - NB Closure)	4d	28-Aug-23*	31-Aug-23			
C-MS-NBC-1080	Gravel Placement Pathway in Front of MSE Wall (Mainstreet - NB Closure)	3d	05-Sep-23	07-Sep-23			
C-MS-NBC-1090	Pavement Pathway MSE Wall to Roadway (Mainstreet - NB Closure)	2d	08-Sep-23	11-Sep-23			
C-MS-NBC-1100	Seeding (Mainstreet - NB Closure)	2d	12-Sep-23	13-Sep-23			
C-MS-NBC-1110	Mainstreet NB Closure Complete	0d		13-Sep-23			
Main Street Bridge to QE II Bridge		454d	26-Nov-21 A	22-Sep-23	08-Oct-21	28-Oct-21	-474d
2022 Work		231d	26-Nov-21 A	28-Oct-22 A	08-Oct-21	28-Oct-21	-251d
C-MSBQE2-EBL-1000	Site Stripping - Phase 1	0d	26-Nov-21 A	01-Dec-21 A	08-Oct-21	14-Oct-21	-1d
C-MSBQE2-EBL-1010	Bulk Grading (Including Geo Grid) Phase 1	0d	02-Dec-21 A	15-Dec-21 A	15-Oct-21	28-Oct-21	0d

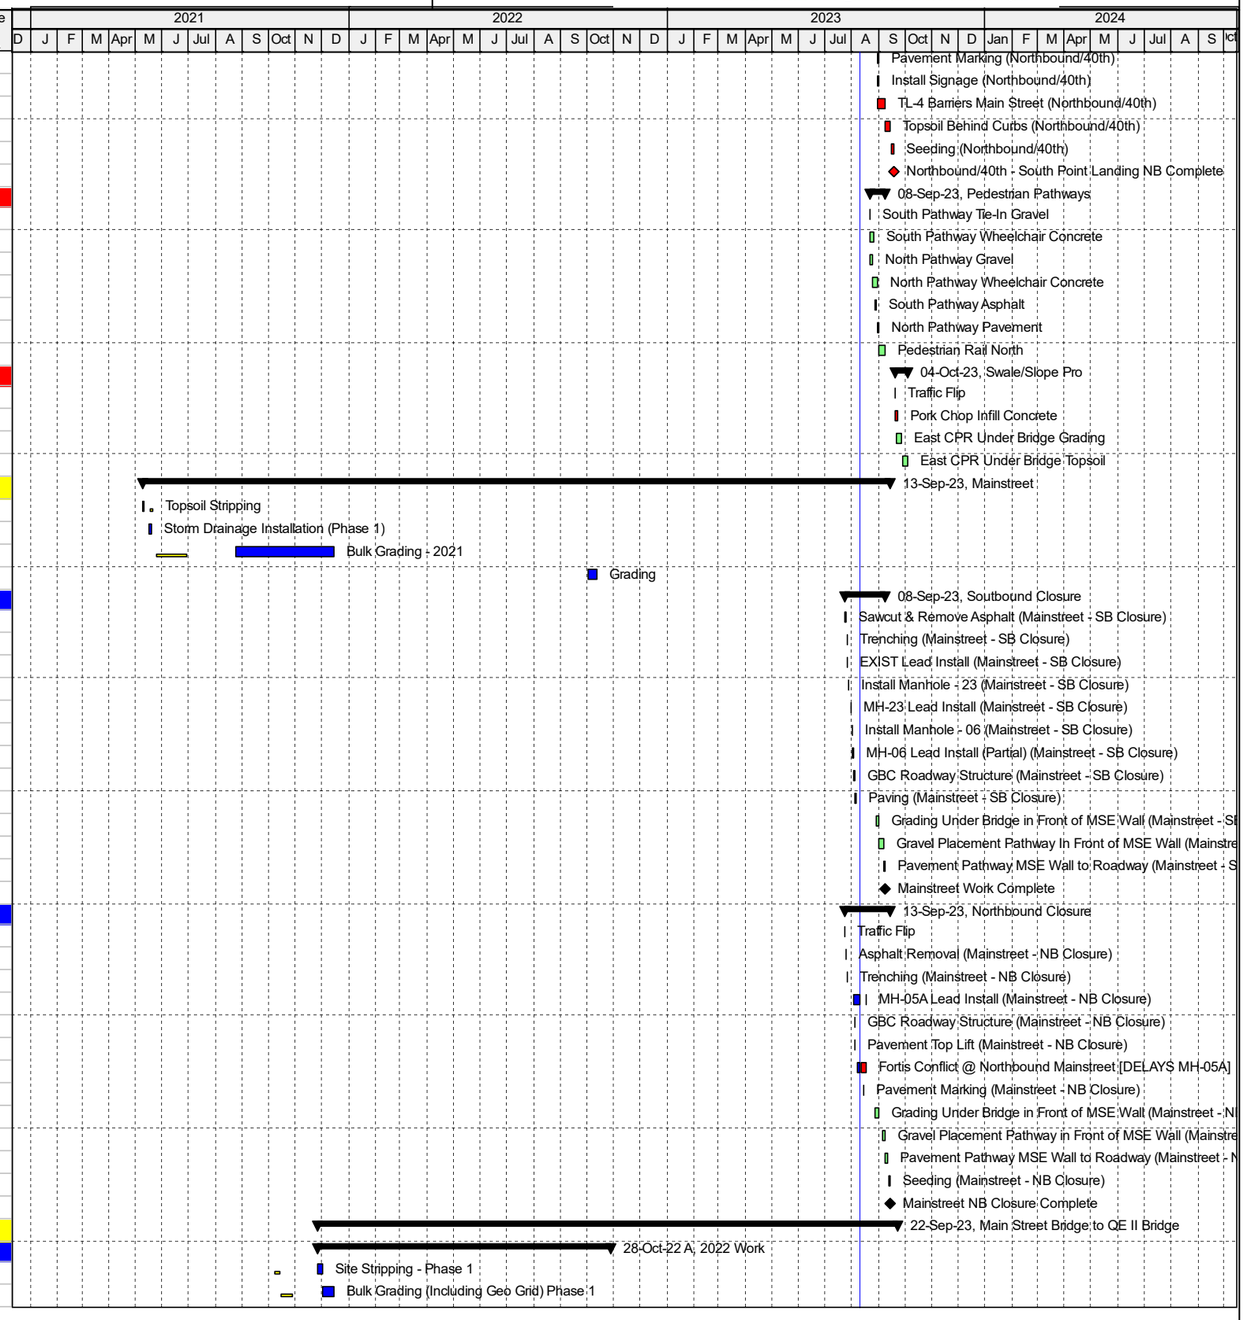

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:27 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE — COMMUNITY & OPPORTUNITY

EllisDon — We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-MSBQE2-EBL-1120	Install Manhole - 05	2d	08-Dec-21 A	10-Dec-21 A			
C-MSBQE2-EBL-1090	Install Manhole - 03	2d	13-Dec-21 A	15-Dec-21 A			
C-MSBQE2-EBL-1110	Install Manhole - 05A	3d	14-Dec-21 A	17-Dec-21 A			
C-MSBQE2-EBL-1100	Install Manhole - 04	4d	24-Oct-22 A	27-Oct-22 A			
C-MSBQE2-EBL-1080	Install Manhole - 01	5d	24-Oct-22 A	28-Oct-22 A			
2023 - Main Street Bridge to QEII Bridge		252d	19-Sep-22 A	22-Sep-23			
Grading & Undergrounds - Main Street to QEII Bridge		198d	19-Sep-22 A	06-Jul-23 A			
C-MSBQE2-WBL-S4-1010	Grading (Mainstreet to QEII)	24d	19-Sep-22 A	21-Apr-23 A			
C-MSBQE2-WBL-S4-1210	QEII Bridge Backfill Complete (West Approach)	0d		05-Jun-23 A			
C-MSBQE2-WBL-S4-1090	Bridge Backfill Complete	0d		05-Jun-23 A			
C-MSBQE2-WBL-S4-1050	Subgrade (Mainstreet to QEII)	5d	06-Jun-23 A	12-Jun-23 A			
C-MSBQE2-WBL-S4-1020	Install Twin CB-04A (Mainstreet to QEII)	1d	13-Jun-23 A	13-Jun-23 A			
C-MSBQE2-EBL-1050	Install Twin CB-04B (Mainstreet to QEII)	1d	13-Jun-23 A	13-Jun-23 A			
C-MSBQE2-WBL-S4-1040	Install CB-01A (Mainstreet to QEII)	1d	16-Jun-23 A	16-Jun-23 A			
C-MSBQE2-EBL-1070	Install CB-01B (Mainstreet to QEII)	1d	19-Jun-23 A	19-Jun-23 A			
C-QE2SR1-1070	Install Twin CB-08 & Lead (Mainstreet to QEII)	1d	20-Jun-23 A	20-Jun-23 A			
C-QE2SR1-1330	Install Twin CB-09 & Lead (Mainstreet to QEII)	1d	21-Jun-23 A	21-Jun-23 A			
C-MSBQE2-EBL-1210	Install Street Light Conduit (Mainstreet to QEII)	5d	22-Jun-23 A	28-Jun-23 A			
C-MSBQE2-WBL-S4-1030	Install Twin CB-03A (Mainstreet to QEII)	1d	22-Jun-23 A	23-Jun-23 A			
C-MSBQE2-EBL-1060	Install Twin CB-03B (Mainstreet to QEII)	1d	23-Jun-23 A	23-Jun-23 A			
C-MSBQE2-EBL-1130	South Bound Ramp - Install Light Bases and Conduit	5d	26-Jun-23 A	30-Jun-23 A			
C-MSBQE2-EBL-1140	South Bound Ramp - Install Light Poles	5d	26-Jun-23 A	30-Jun-23 A			
C-MSBQE2-EBL-1350	Install Street Light Bases (Mainstreet to QEII)	5d	29-Jun-23 A	06-Jul-23 A			
GBC, Concrete - Main Street to QEII Bridge		57d	26-May-23 A	16-Aug-23			
C-MSBQE2-EBL-1310	Slope Protection Grading QEII	7d	26-May-23 A	05-Jun-23 A			
C-MSBQE2-EBL-1300	Grading East Main Street Bridge Slopes	8d	05-Jul-23 A	14-Jul-23 A			
C-MSBQE2-EBL-1170	GBC Base Lift Placement (Mainstreet to QEII)	5d	12-Jul-23 A	18-Jul-23 A			
C-MSBQE2-WBL-S4-1110	Porkchop Grading (Mainstreet to QEII)	2d	15-Jul-23 A	16-Jul-23 A			
C-MSBQE2-WBL-S4-1220	Porkchop Curb (Mainstreet to QEII)	5d	17-Jul-23 A	21-Jul-23 A			
C-MSBQE2-WBL-S4-1060	South Curb Extrusion (Mainstreet to QEII)	2d	19-Jul-23 A	20-Jul-23 A			
C-MSBQE2-EBL-1340	North Curb Extrusion (Mainstreet to QEII)	2d	21-Jul-23 A	24-Jul-23 A			
C-MSBQE2-WBL-S4-1080	East Curb Extrusion (Mainstreet to QEII)	1d	25-Jul-23 A	25-Jul-23 A			
C-MSBQE2-EBL-1190	Median Curb Extrusion (Mainstreet to QEII)	1d	26-Jul-23 A	26-Jul-23 A			
C-MSBQE2-EBL-1180	F/R/P Curb Hand Ties (Mainstreet to QEII)	5d	27-Jul-23 A	02-Aug-23 A			
C-MSBQE2-WBL-S4-1100	GBC Top Lift (Mainstreet to QEII)	3d	01-Aug-23 A	03-Aug-23 A			
C-MSBQE2-EBL-1380	Curb Curing	3d	03-Aug-23 A	05-Aug-23 A			
C-MSBQE2-EBL-1220	Porkchop Gravel Infill (Mainstreet to QEII)	2d	11-Aug-23	14-Aug-23			
C-MSBQE2-WBL-S4-1150	Curb Backfill	2d	11-Aug-23	14-Aug-23			
C-MSBQE2-EBL-1360	Porkchop Concrete Infill (Mainstreet to QEII)	2d	15-Aug-23	16-Aug-23			
Paving & Finishes - Main Street to QEII Bridge		47d	18-Jul-23 A	22-Sep-23			
C-MSBQE2-EBL-1290	Install Street Lights (Mainstreet to QEII)	3d	18-Jul-23 A	20-Jul-23 A			
C-MSBQE2-WBL-S4-1130	Paving Bottom Lift (Mainstreet to QEII)	7d	08-Aug-23 A	17-Aug-23			
C-MSBQE2-WBL-S4-1140	Install Bridge Conduit (53mm Interconnect) (Mainstreet to QEII)	3d	17-Aug-23	21-Aug-23			
C-MSBQE2-EBL-1240	Paving Top Lift (Mainstreet to QEII)	2d	05-Sep-23*	06-Sep-23			
C-MSBQE2-WBL-S4-1120	Install Traffic Lights (Mainstreet to QEII)	3d	07-Sep-23	11-Sep-23			
C-MSBQE2-WBL-S4-1180	TL-4 Barrier Install East Main Street (Mainstreet to QEII)	5d	07-Sep-23	13-Sep-23			
C-MSBQE2-EBL-1250	Pavement Marking (Mainstreet to QEII)	1d	07-Sep-23	07-Sep-23			
C-MSBQE2-EBL-1160	TL-4 Barrier Install West of QEII (Mainstreet to QEII)	5d	07-Sep-23	13-Sep-23			
C-MSBQE2-EBL-1260	Topsoil (East, North South) (Mainstreet to QEII)	2d	14-Sep-23	15-Sep-23			
C-MSBQE2-EBL-1270	Install Signage (Mainstreet to QEII)	2d	14-Sep-23	15-Sep-23			
C-MSBQE2-EBL-1280	Seeding (Mainstreet to QEII)	2d	18-Sep-23	19-Sep-23			
C-MSBQE2-EBL-1370	Install East & West Guardrails (SB Ramp)	5d	18-Sep-23	22-Sep-23			
C-MSBQE2-WBL-S4-1190	Fencing Install	1d	20-Sep-23	20-Sep-23			
C-MSBQE2-WBL-S4-1200	Mainstreet to QEII Complete	0d		20-Sep-23			
Guide Sign Structure 6		118d	29-Mar-23 A	15-Sep-23			
C-QE2NR1-S5-1000	Drill Pile Foundations (Guide Sign 6)	1d	29-Mar-23 A	29-Mar-23 A			

Remaining Level of Effort · Actual Work · Critical Remaining Work · Critical M/S · Project Baseline
Actual Level of Effort · Remaining Work · Milestone · Summary · Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:28 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE — COMMUNITY & OPPORTUNITY

EllisDon — We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-QE2NR1-S5-1010	F/R/P Guide Sign Foundation Stage 2 (Structure 6)	15d	21-Aug-23*	11-Sep-23			
C-QE2NR1-S5-1040	Install Structure	3d	12-Sep-23	14-Sep-23			
C-QE2NR1-S5-1050	Erect Guide Sign Panel	1d	15-Sep-23	15-Sep-23			
Pedestrian Pathway		15d	29-Aug-23	19-Sep-23			
C-MSBQE2-WBL-S4-1070	Pedestrian Pathway Grading (Mainstreet to QEII)	4d	29-Aug-23	01-Sep-23			
C-MSBQE2-WBL-S4-1230	Pedestrian Pathway GBC (Mainstreet to QEII)	4d	05-Sep-23	08-Sep-23			
C-MSBQE2-WBL-S4-1240	Pedestrian Pedestrian Pathway Paving (Mainstreet to QEII)	2d	11-Sep-23	12-Sep-23			
C-MSBQE2-EBL-1230	Install Pedestrian Railing (Mainstreet to QEII)	5d	13-Sep-23	19-Sep-23			
40th Ave to QEII Ramp South Bound 4+200 (North Half)		109d	01-Jun-22 A	04-Nov-22 A			
Grading		85d	01-Jun-22 A	30-Sep-22 A			
C-QE2SR1-1050	Grading (Done to U/S Storm)	85d	01-Jun-22 A	30-Sep-22 A			
Utilities		11d	21-Oct-22 A	04-Nov-22 A			
C-QE2SR1-1100	Install Manhole - 10	4d	21-Oct-22 A	26-Oct-22 A			
C-QE2SR1-1090	Install Manhole - 09	4d	27-Oct-22 A	01-Nov-22 A			
C-QE2SR1-1080	Install Manhole - 08	1d	31-Oct-22 A	31-Oct-22 A			
C-QE2SR1-1110	Culvert Inlet	3d	02-Nov-22 A	04-Nov-22 A			
QEII Ramp South Bound 4+200 to QE II Hwy (South Half)		120d	16-May-22 A	04-Nov-22 A			
C-QE2SR2-1000	Removal of Billboard Sign	1d	16-May-22 A	16-May-22 A			
C-QE2SR2-1010	Stripping of Topsoil	10d	25-Aug-22 A	08-Sep-22 A			
C-QE2SR2-1020	Grading	11d	09-Sep-22 A	23-Sep-22 A			
C-QE2SR2-1060	Subgrade Preparation	2d	26-Sep-22 A	27-Sep-22 A			
C-QE2SR2-1080	GBC Placement Bottom Lift	3d	27-Sep-22 A	29-Sep-22 A			
C-QE2SR2-1120	Paving Bottom Lift	1d	05-Oct-22 A	05-Oct-22 A			
C-QE2SR2-1040	Installation of Culvert West Storage Ditch	4d	25-Oct-22 A	28-Oct-22 A			
C-QE2SR2-1030	Install Manhole - 70	3d	02-Nov-22 A	04-Nov-22 A			
QEII NB 4+200 to Kingsview Blvd Intersection North Bound Ramp (North Half)		167d	17-Aug-21 A	19-Oct-22 A	07-Apr-21	04-Aug-22	-49d
Grading		115d	17-Aug-21 A	02-Aug-22 A	07-Apr-21	04-Aug-22	3d
C-QE2NR1-1000	Utility Salvaging and Relocations	42d	17-Aug-21 A	19-Oct-21 A	09-Aug-21	26-Aug-21	-34d
C-QE2NR1-1010	Removals - Kingsview/Sharp Hill	8d	18-Apr-22 A	27-Apr-22 A	08-Apr-21	21-Apr-21	-130d
C-QE2NR1-1130	2022 Grading - Before Contamination Impact	45d	20-Apr-22 A	22-Jun-22 A			
C-QE2NR1-1020	Road Closure Notification (Kingsview Rd and Sharp Hill Way)	1d	21-Apr-22 A	21-Apr-22 A	07-Apr-21	07-Apr-21	-136d
C-QE2NR1-1030	Site Stripping	10d	28-Apr-22 A	11-May-22 A	26-Apr-22	09-May-22	-2d
C-QE2NR1-1040	Bulk Grading Stage 1 (30000cu.m)	4d	02-May-22 A	06-May-22 A	25-May-22	04-Aug-22	62d
C-QE2NR1-1110	Standalone MSE Wall	33d	01-Jun-22 A	19-Jul-22 A			
C-QE2NR1-1780	2022 Grading - After Contamination Impact	15d	11-Jul-22 A	02-Aug-22 A			
Utilities		71d	09-May-22 A	18-Aug-22 A			
C-QE2NR1-1240	Install Manhole - 24	5d	09-May-22 A	16-May-22 A			
C-QE2NR1-1250	Install Manhole - 25	4d	16-May-22 A	20-May-22 A			
C-QE2NR1-1230	Install Manhole - 60	5d	20-May-22 A	30-May-22 A			
C-QE2NR1-1370	Install Manhole - 20	7d	30-May-22 A	08-Jun-22 A			
C-QE2NR1-1400	Install Manhole - 22	3d	07-Jun-22 A	10-Jun-22 A			
C-QE2NR1-1380	Install Twin CB - 20B	1d	17-Jun-22 A	18-Jun-22 A			
C-QE2NR1-1480	Install Twin CB - 20A	1d	17-Jun-22 A	18-Jun-22 A			
C-QE2NR1-1390	Install Twin CB - 22B	0d	18-Jun-22 A	20-Jun-22 A			
C-QE2NR1-1510	Install Twin CB - 22A	1d	21-Jun-22 A	22-Jun-22 A			
C-QE2NR1-1220	Install Manhole - 15	1d	23-Jun-22 A	24-Jun-22 A			
C-QE2NR1-1180	Install Manhole - 14	1d	24-Jun-22 A	25-Jun-22 A			
C-QE2NR1-1190	Install Twin CB - 14A	2d	27-Jun-22 A	29-Jun-22 A			
C-QE2NR1-1200	Install Twin CB - 14B	2d	27-Jun-22 A	29-Jun-22 A			
C-QE2NR1-1360	Install Manhole - 19	3d	27-Jun-22 A	29-Jun-22 A			
C-QE2NR1-1210	Install CB - 15	1d	29-Jun-22 A	30-Jun-22 A			
C-QE2NR1-1330	Install Manhole - 11	3d	02-Aug-22 A	04-Aug-22 A			
C-QE2NR1-1170	Install Manhole - 13	2d	04-Aug-22 A	08-Aug-22 A			
C-QE2NR1-1320	Install Manhole - 17	2d	08-Aug-22 A	09-Aug-22 A			
C-QE2NR1-1340	Install Twin CB - 11B	2d	09-Aug-22 A	10-Aug-22 A			
C-QE2NR1-1350	Install Twin CB - 19B	2d	09-Aug-22 A	10-Aug-22 A			

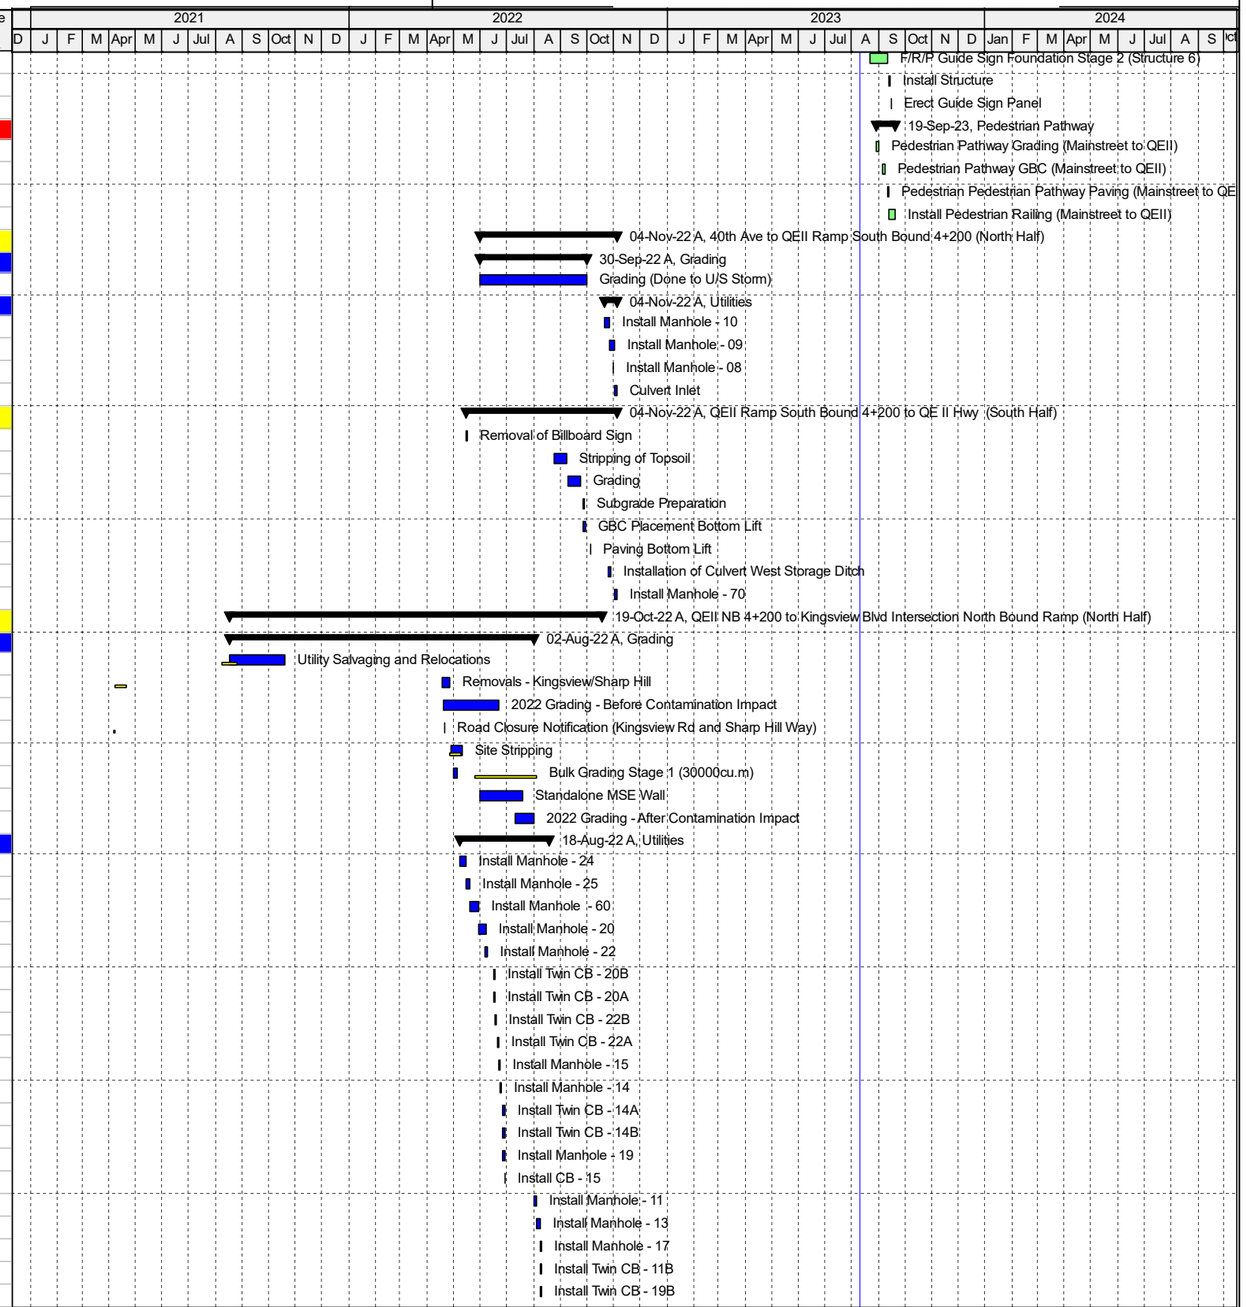

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:28 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-QE2NR1-1450	Install Twin CB - 11A	1d	18-Aug-22 A	18-Aug-22 A			
C-QE2NR1-1460	Install Twin CB - 19A	1d	18-Aug-22 A	18-Aug-22 A			
Roadway		52d	02-Aug-22 A	19-Oct-22 A			
C-QE2NR1-1540	Subgrade Preparation	14d	02-Aug-22 A	22-Aug-22 A			
C-QE2NR1-1550	GBC Placement Bottom Lift	5d	29-Aug-22 A	02-Sep-22 A			
C-QE2NR1-1590	Island Median F/R/P	3d	19-Sep-22 A	21-Sep-22 A			
C-QE2NR1-1600	Curb with Gutter F/R/P	17d	19-Sep-22 A	12-Oct-22 A			
C-QE2NR1-1710	Paving Bottom Lift	0d	17-Oct-22 A	19-Oct-22 A			
QEII NB 4+200 to QE II Hwy North Bound Ramp (South Sliver)		22d	24-Aug-22 A	23-Sep-22 A			
C-QE2NR2-1020	Removal of Signage	1d	24-Aug-22 A	24-Aug-22 A			
C-QE2NR2-1010	Stripping of Topsoil	5d	24-Aug-22 A	30-Aug-22 A			
C-QE2NR2-1030	Grading	5d	31-Aug-22 A	07-Sep-22 A			
C-QE2NR2-1120	Sawcut and Remove Existing Asphalt	2d	31-Aug-22 A	01-Sep-22 A			
C-QE2NR2-1110	Subgrade Preparation	1d	07-Sep-22 A	07-Sep-22 A			
C-QE2NR2-1130	GBC Placement Bottom Lift	3d	08-Sep-22 A	12-Sep-22 A			
C-QE2NR2-1160	GBC Placement Top Lift	5d	12-Sep-22 A	16-Sep-22 A			
C-QE2NR2-1050	Extension of Ex Culvert	1d	16-Sep-22 A	16-Sep-22 A			
C-QE2NR2-1170	Paving Bottom Lift	3d	21-Sep-22 A	23-Sep-22 A			
QEII to Kingsview Blvd		136d	27-Mar-23 A	10-Oct-23			
Major Guide Signs - QEII to Kingsview Blvd		121d	27-Mar-23 A	18-Sep-23			
Guide Sign Structure 2		105d	10-Apr-23 A	07-Sep-23			
C-QE2NR2-S1-1000	Drill Pile Foundation (Guide Sign 2)	1d	10-Apr-23 A	10-Apr-23 A			
C-QE2NR2-S1-1010	R/P Pile Foundation	1d	26-Jun-23 A	26-Jun-23 A			
C-QE2NR2-S1-1050	F/R/P Guide Sign Foundation Stage 2 (Structure 2)	15d	11-Aug-23	31-Aug-23			
C-QE2NR2-S1-1020	Install Structure	3d	01-Sep-23	06-Sep-23			
C-QE2NR2-S1-1030	Erect Guide Sign Panel	1d	07-Sep-23	07-Sep-23			
Guide Sign Structure 3		109d	04-Apr-23 A	08-Sep-23			
C-QE2NR1-S2-1000	Drill Pile Foundations (Guide Sign 3)	2d	04-Apr-23 A	05-Apr-23 A			
C-QE2NR1-S2-1010	R/P Pile Foundations	2d	27-Jun-23 A	28-Jun-23 A			
C-QE2NR1-S2-1030	F/R/P Guide Sign Foundation Stage 2 (Structure 3)	15d	11-Aug-23	31-Aug-23			
C-QE2NR1-S2-1040	Install Structure	3d	01-Sep-23	05-Sep-23			
C-QE2NR1-S2-1050	Erect Guide Sign Panel	1d	08-Sep-23	08-Sep-23			
Guide Sign Structure 4		113d	30-Mar-23 A	11-Sep-23			
C-QE2NR1-S3-1000	Drill Pile Foundations (Guide Sign 4)	2d	30-Mar-23 A	31-Mar-23 A			
C-QE2NR1-S3-1010	R/P Pile Foundations	2d	29-Jun-23 A	30-Jun-23 A			
C-QE2NR1-S3-1030	F/R/P Guide Sign Foundation Stage 2 (Structure 4)	15d	11-Aug-23	31-Aug-23			
C-QE2NR1-S3-1040	Install Structure	3d	01-Sep-23	06-Sep-23			
C-QE2NR1-S3-1050	Erect Guide Sign Panel	1d	11-Sep-23	11-Sep-23			
Guide Sign Structure 5		121d	27-Mar-23 A	18-Sep-23			
C-MSBQE2-EBL-S4-1000	Drill Pile Foundations (Guide Sign 5)	2d	27-Mar-23 A	28-Mar-23 A			
C-MSBQE2-EBL-S4-1010	R/P Pile Foundations	2d	04-Jul-23 A	05-Jul-23 A			
C-MSBQE2-EBL-S4-1030	F/R/P Guide Sign Foundation Stage 2 (Structure 5)	15d	11-Aug-23	31-Aug-23			
C-MSBQE2-EBL-S4-1040	Install Structure	3d	01-Sep-23	06-Sep-23			
C-MSBQE2-EBL-S4-1050	Erect Guide Sign Panel	1d	18-Sep-23	18-Sep-23			
Roadway - QEII to Kingsview Blvd		108d	05-May-23 A	10-Oct-23			
Grading & Undergrounds - QEII to Kingsview Blvd		72d	05-May-23 A	17-Aug-23			
C-QE2KV-1030	Slope Protection Grading QEII	6d	05-May-23 A	12-May-23 A			
C-QE2KV-1040	Subgrade (QEII to Kingsview Blvd)	4d	29-May-23 A	02-Jun-23 A			
C-QE2KV-1000	Bridge Backfill East QEII Complete	0d		05-Jun-23 A			
C-MSBQE2-WBL-S4-1250	Bridge Backfill Complete	0d		05-Jun-23 A			
C-QE2KV-1050	Install Twin CB - 17A	2d	13-Jul-23 A	14-Jul-23 A			
C-QE2KV-1060	Install Twin CB - 17B	2d	17-Jul-23 A	18-Jul-23 A			
C-QE2KV-1070	CB-22B Readjustment	2d	19-Jul-23 A	20-Jul-23 A			
C-QE2KV-1080	Island Grading (QEII to Kingsview Blvd)	2d	21-Jul-23 A	24-Jul-23 A			
C-QE2KV-1090	Install Traffic Light Conduit (QEII to Kingsview Blvd)	2d	11-Aug-23	14-Aug-23			
C-MSBQE2-WBL-S4-1260	North Bound Ramp - Install Light Poles	4d	11-Aug-23	16-Aug-23			
C-QE2KV-1100	Install Traffic Light Bases (QEII to Kingsview Blvd)	3d	15-Aug-23	17-Aug-23			

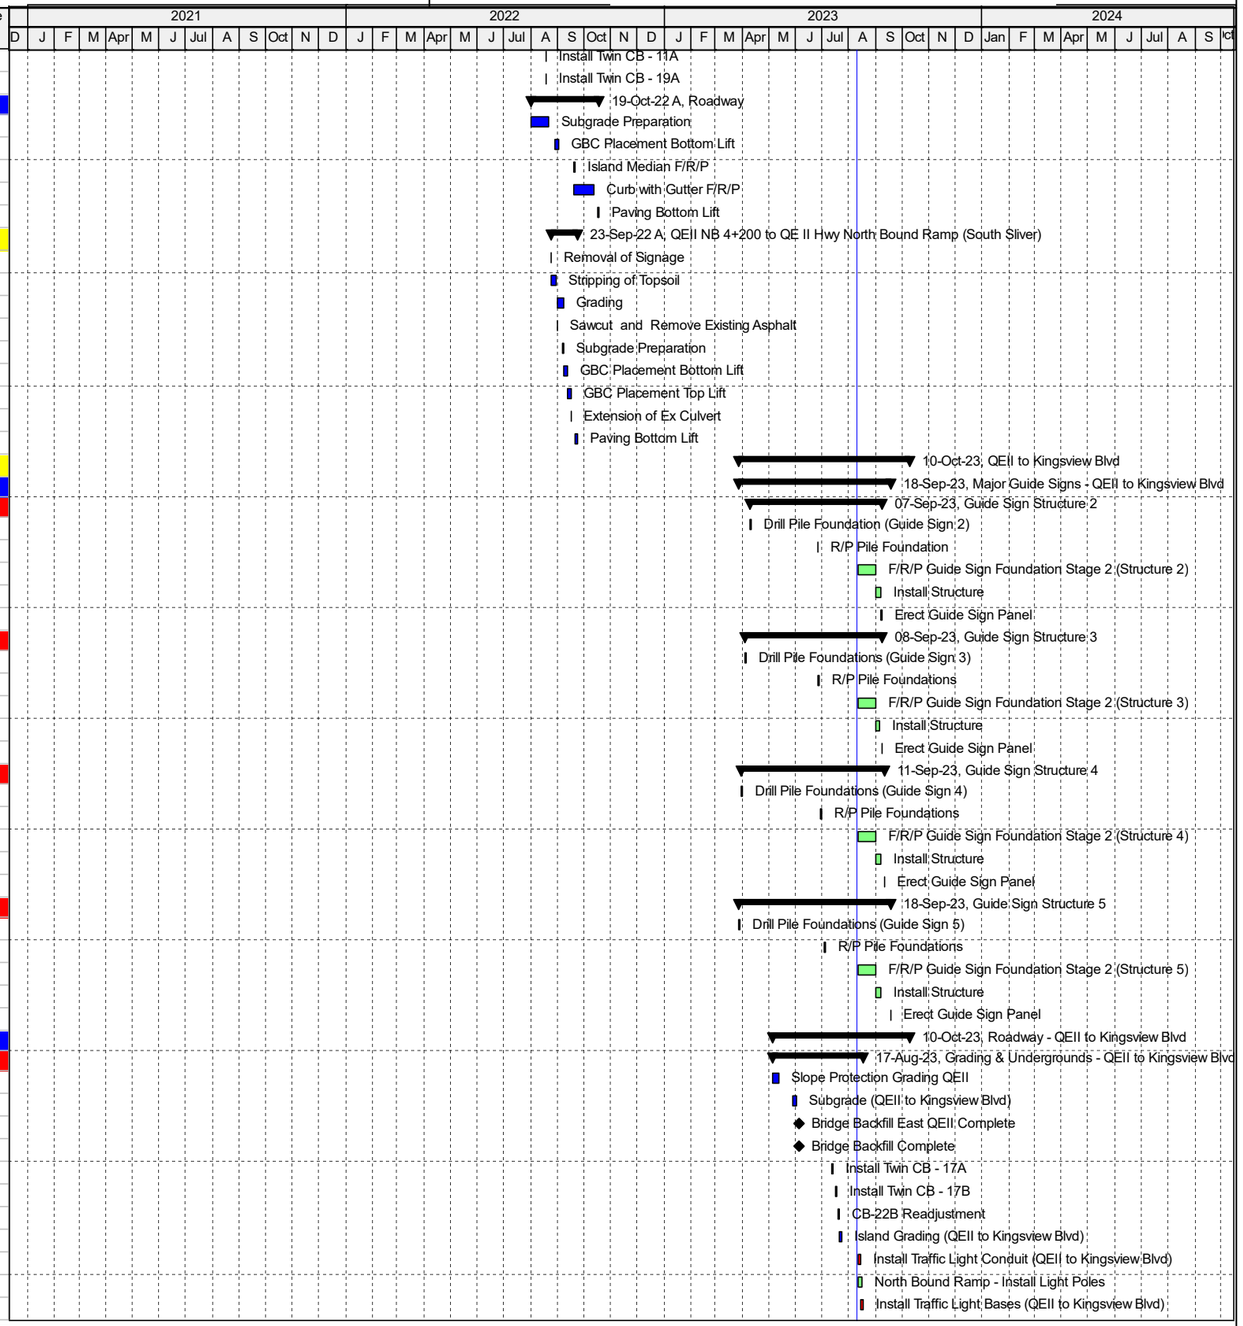

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:28 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE COMMUNITY & OPPORTUNITY

EllisDon We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-QE2KV-1110	Install Bridge Conduit (53mm Interconnect) (QEII to Kingsview Blvd)	3d	15-Aug-23	17-Aug-23			
GBC, Concrete, Paving - QEII to Kingsview Blvd		38d	22-Jul-23 A	15-Sep-23			
C-QE2KV-2040	Sawcut & Remove Asphalt North	0d	22-Jul-23 A	22-Jul-23 A			
C-QE2KV-2000	GBC Bridge Tie-In (QEII Bridge East)	3d	01-Aug-23 A	03-Aug-23 A			
C-QE2KV-2010	F/R/P Island Curbs (QEII to Kingsview Blvd)	4d	07-Aug-23 A	11-Aug-23			
C-QE2KV-2030	Median Curbs (QEII to Kingsview Blvd)	4d	07-Aug-23 A	11-Aug-23			
C-QE2KV-2120	Guardrail Install West Ramp	6d	07-Aug-23 A	15-Aug-23			
C-QE2KV-2050	F/R/P Hand-Tied Curbs (QEII to Kingsview Blvd)	2d	14-Aug-23	15-Aug-23			
C-QE2KV-2060	Median GBC Infill (QEII to Kingsview Blvd)	2d	14-Aug-23	15-Aug-23			
C-QE2KV-2100	Asphalt Paving Bottom Lift (QEII to Kingsview Blvd)	2d	16-Aug-23*	17-Aug-23			
C-QE2KV-2070	Median Concrete Infill (QEII to Kingsview Blvd)	2d	18-Aug-23	21-Aug-23			
C-QE2KV-2080	Island Gravel Infill (QEII to Kingsview Blvd)	2d	18-Aug-23	21-Aug-23			
C-QE2KV-2110	Guardrail Install North (QEII to Kingsview Blvd)	4d	18-Aug-23	23-Aug-23			
C-QE2KV-2130	Topsoil Slopes (QEII to Kingsview Blvd)	2d	18-Aug-23	21-Aug-23			
C-QE2KV-2090	Island Concrete Infill (QEII to Kingsview Blvd)	2d	22-Aug-23	23-Aug-23			
C-QE2KV-2140	Topsoil Curbs (QEII to Kingsview Blvd)	2d	22-Aug-23	23-Aug-23			
C-QE2KV-2150	Seeding (QEII to Kingsview Blvd)	2d	24-Aug-23	25-Aug-23			
C-QE2KV-2160	Asphalt Paving Top Lift (QEII to Kingsview Blvd)	3d	24-Aug-23	28-Aug-23			
C-QE2KV-2170	Install Traffic Light Poles (QEII to Kingsview Blvd)	3d	29-Aug-23	31-Aug-23			
C-QE2KV-2180	Pavement Line Painting (QEII to Kingsview Blvd)	2d	29-Aug-23	30-Aug-23			
C-QE2KV-2190	Install Traffic Signs (QEII to Kingsview Blvd)	3d	31-Aug-23	05-Sep-23			
C-QE2KV-2200	Landscaping Rock Placement (QEII to Kingsview Blvd)	3d	06-Sep-23	08-Sep-23			
C-QE2KV-2210	Install Fencing (QEII to Kingsview Blvd)	5d	11-Sep-23	15-Sep-23			
C-QE2KV-2220	Control Structure Dog Park Orifice Plate	5d	11-Sep-23	15-Sep-23			
C-QE2KV-2230	QEII to Kingsview Intersection Complete	0d		15-Sep-23			
Pedestrian Pathway - QEII to Kingsview Blvd		36d	18-Aug-23	10-Oct-23			
C-QE2KV-3020	Pedestrian Pathway Asphalt Paving (QEII to Kingsview Blvd)	2d	18-Aug-23	21-Aug-23			
C-QE2KV-3030	Install Pedestrian Railing (QEII to Kingsview Blvd)	4d	22-Aug-23	25-Aug-23			
C-QE2KV-1010	Sawcut Asphalt North (QEII to Kingsview Blvd)	1d	21-Sep-23*	21-Sep-23			
C-QE2KV-1020	Remove Excess Asphalt (QEII to Kingsview Blvd)	2d	22-Sep-23	25-Sep-23			
C-QE2KV-2020	Curb Extrusion North (QEII to Kingsview Blvd)	2d	26-Sep-23	27-Sep-23			
C-QE2KV-3000	Pedestrian Pathway Grading (QEII to Kingsview Blvd)	3d	28-Sep-23	02-Oct-23			
C-QE2KV-3010	GBC Pedestrian Pathway (QEII to Kingsview Blvd)	5d	03-Oct-23	10-Oct-23			
Kingsview Blvd Intersection		80d	01-Jun-23 A	25-Sep-23			
Kingsview Intersection - Stage 1		68d	01-Jun-23 A	07-Sep-23			
Removals & Undergrounds - Kingsview Intersection - Stage 1		30d	26-Jul-23 A	07-Sep-23			
C-KVBI-1000	NW Porkchop Removal (Kingsview Intersection - Stage 1)	2d	26-Jul-23 A	27-Jul-23 A			
C-KVBI-1060	Traffic Light Conduits Install (Kingsview Blvd Intersection - Stage 1)	3d	26-Jul-23 A	28-Jul-23 A			
C-KVBI-1050	Water Main Install (Kingsview Blvd Intersection - Stage 1)	7d	31-Jul-23 A	09-Aug-23 A			
C-KVBI-1070	Fire Hydrant Relocation (Kingsview Blvd Intersection - Stage 1)	7d	31-Jul-23 A	09-Aug-23 A			
C-KVBI-1080	Sanitary Line Install (Kingsview Blvd Intersection - Stage 1)	8d	07-Aug-23 A	17-Aug-23			
C-KVBI-1090	Install MH-01N (Kingsview Blvd Intersection - Stage 1)	5d	11-Aug-23	17-Aug-23			
C-KVBI-1100	NE Porkchop Removal (Interior Concrete no Curb) (Kingsview Intersection - St	2d	11-Aug-23*	14-Aug-23			
C-KVBI-1030	Install MH-21 (Kingsview Blvd Intersection - Stage 1)	2d	14-Aug-23*	15-Aug-23			
C-KVBI-1110	Install Traffic Light Bases (Kingsview Intersection - Stage 1)	3d	05-Sep-23*	07-Sep-23			
GBC, Concrete, Paving - Kingsview Intersection - Stage 1		68d	01-Jun-23 A	07-Sep-23			
C-KVBI-1500	Subgrade (Kingsview Intersection - Stage 1)	2d	01-Jun-23 A	02-Jun-23 A			
C-KVBI-1510	GBC Placement Bottom Lift (Kingsview Intersection - Stage 1)	3d	21-Aug-23*	23-Aug-23			
C-KVBI-1520	Curb Extrusion (Kingsview Intersection)	1d	24-Aug-23	24-Aug-23			
C-KVBI-1580	Curb Median (Kingsview Intersection - Stage 1)	2d	25-Aug-23	28-Aug-23			
C-KVBI-1620	Asphalt Paving - Bottom Lift (Kingsview Intersection - Stage 1)	2d	29-Aug-23	30-Aug-23			
C-KVBI-1590	Curb Curing	3d	29-Aug-23	31-Aug-23			
C-KVBI-1600	Median Infill Gravel (Kingsview Intersection - Stage 1)	2d	01-Sep-23	05-Sep-23			
C-KVBI-1570	Curb Infill Concrete - Porkchop SW, SE, NW, NE (Kingsview Intersection - Stag	2d	06-Sep-23	07-Sep-23			
C-KVBI-1610	Median Concrete Infill (Kingsview Intersection - Stage 1)	1d	06-Sep-23	06-Sep-23			
C-KVBI-1630	Milling (Kingsview Intersection - Stage 1)	1d	07-Sep-23	07-Sep-23			

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline

Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:28 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

CITY of AIRDRIE — COMMUNITY & OPPORTUNITY

EllisDon — We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-KVBI-1640	Stage 1 Complete	0d		07-Sep-23			
Kingsview Intersection - Stage 2		12d	08-Sep-23	25-Sep-23			
C-KVBI-2000	Curb Wall (Kingsview Intersection - Stage 2)	2d	08-Sep-23	11-Sep-23			
C-KVBI-2010	Toplift Paving (Kingsview Intersection - Stage 2)	1d	12-Sep-23	12-Sep-23			
C-KVBI-2020	Line Painting (Kingsview Intersection - Stage 2)	2d	13-Sep-23	14-Sep-23			
C-KVBI-2030	Topsoil Outside Curb (Kingsview Intersection - Stage 2)	3d	15-Sep-23	19-Sep-23			
C-KVBI-2040	Install Traffic Lights (Kingsview Intersection - Stage 2)	2d	20-Sep-23	21-Sep-23			
C-KVBI-2050	Seeding (Kingsview Intersection - Stage 2)	2d	22-Sep-23	25-Sep-23			
C-KVBI-2060	Stage 2 Complete (Kingsview Blvd Intersection)	0d		25-Sep-23			
Storm Pond		338d	24-May-22 A	29-Sep-23			
2022 Work		121d	24-May-22 A	14-Nov-22 A			
C-STP-1000	Stripping of Topsoil	9d	24-May-22 A	06-Jun-22 A			
C-STP-1270	Grading Phase - I	6d	06-Jun-22 A	14-Jun-22 A			
C-STP-1250	Cut Maincell to Shape	67d	04-Jul-22 A	06-Oct-22 A			
C-STP-1110	Install Manhole - 56 and Lead	4d	07-Oct-22 A	13-Oct-22 A			
C-STP-1120	Install Subdrain in Manhole - 56	3d	07-Oct-22 A	12-Oct-22 A			
C-STP-1150	Install NW CSP Culvert	1d	12-Oct-22 A	12-Oct-22 A			
C-STP-1100	Install Manhole - 57 and Lead	5d	14-Oct-22 A	20-Oct-22 A			
C-STP-1160	Install South CSP Culvert	0d	19-Oct-22 A	19-Oct-22 A			
C-STP-1130	Install Control Structure and Lead	16d	24-Oct-22 A	14-Nov-22 A			
2023 Work		233d	24-Oct-22 A	29-Sep-23			
C-STP-1020	Install Maincell GCL Liner (CEC)	91d	24-Oct-22 A	08-Mar-23 A			
C-STP-1140	Install Slide Gate and plate in Control Structure	3d	13-Mar-23 A	15-Mar-23 A			
C-STP-1280	Drywell MH#1 Install Subdrain	6d	18-Apr-23 A	25-Apr-23 A			
C-STP-1290	Drywell MH#2 Install Subdrain	6d	18-Apr-23 A	25-Apr-23 A			
C-STP-1550	Access Road Re-Grading	12d	24-Apr-23 A	11-May-23 A			
C-STP-1560	Topsoil Maincell of Pond to NWL to HWL	4d	02-May-23 A	05-May-23 A			
C-STP-1570	Move Topsoil Pile	5d	16-May-23 A	23-May-23 A			
C-STP-1300	Trenching for MH-27 Lead	10d	12-Jun-23 A	23-Jun-23 A			
C-STP-1170	MH-27 Install	2d	26-Jun-23 A	27-Jun-23 A			
C-STP-1320	Forebay Subdrain Trenching	32d	26-Jun-23 A	11-Aug-23			
C-STP-1180	MH-27 1200mm Lead Install	7d	28-Jun-23 A	07-Jul-23 A			
C-STP-1190	MH-26 1200mm Lead Install	7d	28-Jun-23 A	07-Jul-23 A			
C-KVBI-1010	Install MH-26 (Kingsview Blvd Intersection - Stage 1)	1d	07-Jul-23 A	07-Jul-23 A			
C-STP-1240	Complete Cutting Forebay/Material Haul-Out	10d	10-Jul-23 A	21-Jul-23 A			
C-KVBI-1020	Install MH-26 Lead (Kingsview Blvd Intersection - Stage 1)	3d	10-Jul-23 A	12-Jul-23 A			
C-STP-1330	Forebay Subdrain Rock Install	29d	10-Jul-23 A	18-Aug-23			
C-STP-1310	Backfill 1200mm Lead	7d	13-Jul-23 A	21-Jul-23 A			
C-STP-1340	Forebay Drain Tube Install	36d	17-Jul-23 A	06-Sep-23			
C-STP-1440	Weir Rip Rap	4d	25-Jul-23 A	28-Jul-23 A			
C-STP-1450	450 Inlet Rip-Rap	4d	25-Jul-23 A	28-Jul-23 A			
C-STP-1460	1200 Inlet Rip-Rap	4d	25-Jul-23 A	28-Jul-23 A			
C-STP-1470	1050 Outlet Rip-Rap	4d	25-Jul-23 A	28-Jul-23 A			
C-STP-1350	Install Forebay GCL Liner	18d	11-Aug-23*	06-Sep-23			
C-STP-1360	Forebay Geocell Install	18d	11-Aug-23	06-Sep-23			
C-STP-1370	Forebay Gravel Install	18d	11-Aug-23	06-Sep-23			
C-STP-1380	NWL/HWL Topsoiling	2d	07-Sep-23	08-Sep-23			
C-STP-1390	NWL/HWL Seeding/Willows	5d	11-Sep-23	15-Sep-23			
C-STP-1500	Southwest Overflow Rip-Rap	3d	21-Sep-23	25-Sep-23			
C-STP-1510	Outside Perimeter Topsoiling	3d	26-Sep-23	28-Sep-23			
C-STP-1520	Outside Perimeter Seeding	1d	29-Sep-23	29-Sep-23			
C-STP-1530	Pond Complete	0d		29-Sep-23			
Pond Maintenance Road/Access Ramps		14d	07-Sep-23	26-Sep-23			
Ramps		14d	07-Sep-23	26-Sep-23			
C-STP-1480	Maintenance Road Grading	5d	07-Sep-23	13-Sep-23			
C-STP-1490	Maintenance Road Gravel Placement	5d	14-Sep-23	20-Sep-23			

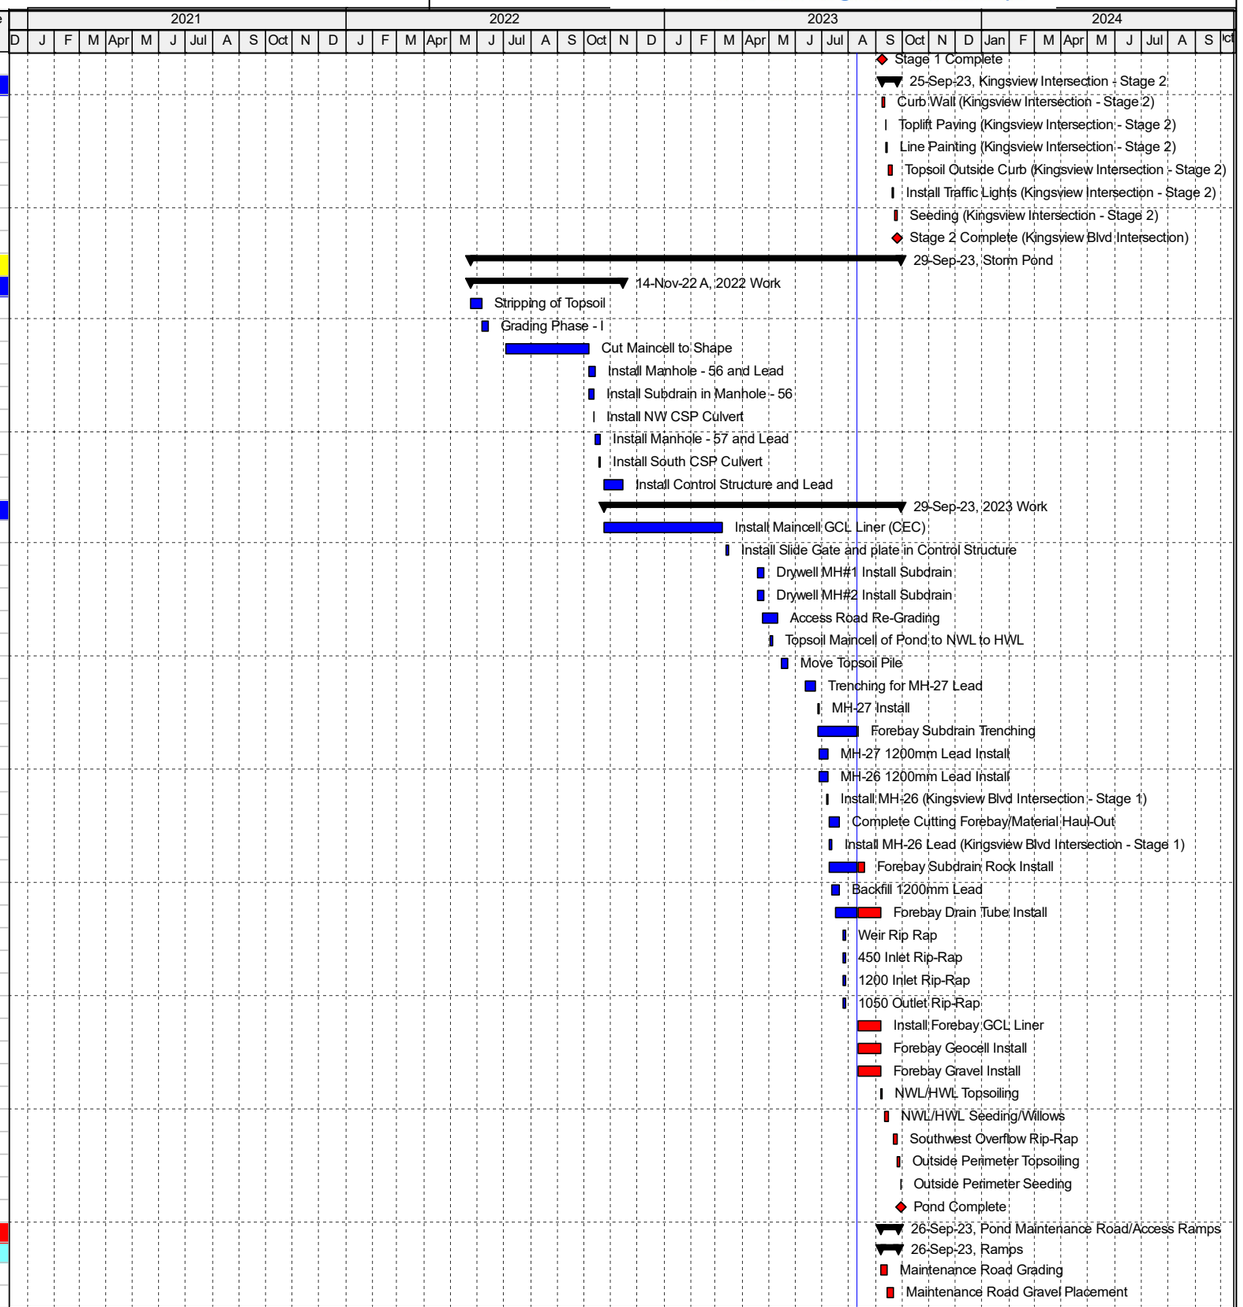

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:28 10-Aug-23

40th Ave QEII Interchange Update 2023.08.10

EllisDon
We build on great relationships™

Activity ID	Activity Name	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Variance - BL Project
C-STP-1540	Maintenance Road Paving	4d	21-Sep-23	26-Sep-23			
Maintenance Road		11d	07-Sep-23	21-Sep-23			
C-STP-1400	Access Ramp Gravel	2d	07-Sep-23	08-Sep-23			
C-STP-1410	Access Ramp Sand	1d	11-Sep-23	11-Sep-23			
C-STP-1420	Access Ramp Paving Stones	6d	12-Sep-23	19-Sep-23			
C-STP-1430	Access Ramp Topsoil Paving Stones	2d	20-Sep-23	21-Sep-23			
Opening Preparation		512d	02-Oct-23	15-Oct-25	17-Aug-23	02-Oct-25	-8d
PCO-1000	EllisDon Inspections & Deficiency Correction	1d	02-Oct-23	02-Oct-23	17-Aug-23	14-Sep-23	-12d
PCO-1020	Owner Deficiency Correction & Sign Off (Safety Audit)	5d	03-Oct-23	10-Oct-23	19-Sep-23	02-Oct-23	-5d
PCO-1070	Float to Substantial	12d	03-Oct-23	14-Oct-23			
PCO-1030	Substantial Performance	1d	15-Oct-23	15-Oct-23	02-Oct-23	02-Oct-23	-13d
PCO-1040	Warranty Period (2 Years)	731d	16-Oct-23	15-Oct-25	03-Oct-23	02-Oct-25	-13d
PCO-1050	Landscape Maintenance	731d	16-Oct-23	15-Oct-25	03-Oct-23	02-Oct-25	-13d
PCO-1080	QEII/40th Ave Overpass Bridge/Roadways Open For Traffic	1d	16-Oct-23	16-Oct-23			
PCO-1060	Final Acceptance Certificate	0d		15-Oct-25		02-Oct-25	-8d

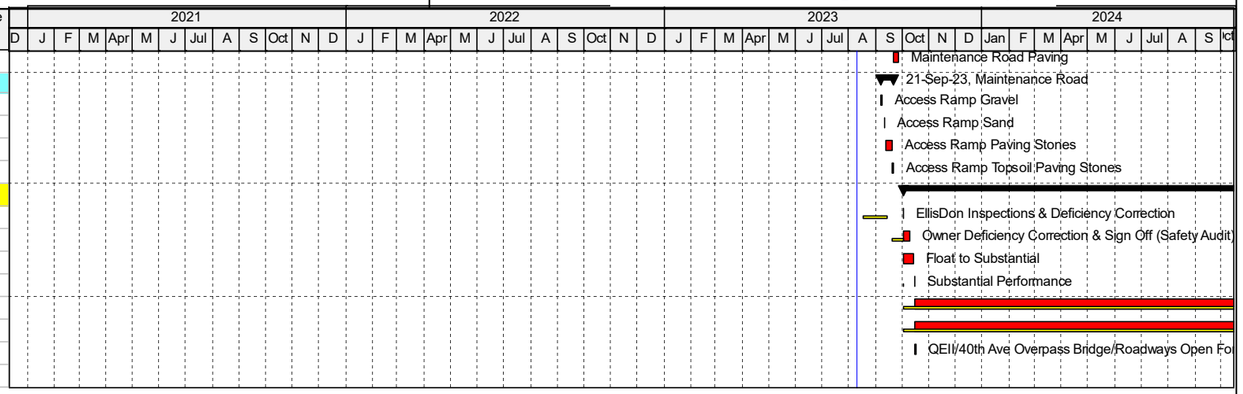

Remaining Level of Effort | Actual Work | Critical Remaining Work | Critical M/S | Project Baseline
Actual Level of Effort | Remaining Work | Milestone | Summary | Project BL Milestones

Data Date: 10-Aug-23 Project ID: UP.53918.2023.08.10
Current Date: 18:28 10-Aug-23
